



**Battery Park  
City Authority**

# **South Battery Park City Resiliency Project**

December 10, 2025 Update







## Progress

### **Wagner Park/MJH Sitework: 98% Complete**

- South Allee
- South Esplanade Staircase
- Floodwall Stone

### **Wagner Park Pavilion: 90% Complete**

- Classroom Ceiling Baffles Installation
- Classroom Lighting Fixtures Installation

### **Pier A/The Battery: 65% Complete**

- Pier A Inlet
- Pier A Plaza Tide Gate Jet Grouting
- Flood Wall Construction



## Schedule

### **Wagner Park**

- Punch List Work (January 2026)

### **Pavilion Classroom (Late Dec)**

- IT/AV Equipment Installation
- Equipment Controls Installation
- NYCDOB Approvals

### **Pavilion Restaurant (Late Dec)**

- Ceiling Baffles Installation
- Lighting Fixtures Installation
- Equipment Controls Installation
- NYCDOB Approvals

### **Package 4 Substantial Completion (Late May 2026)**

- Pier A Inlet Viewing Platform (Mid Dec 2025)



# **Pavilion Classroom Ceiling Baffles Installation**

BATTERY PARK CITY AUTHORITY





# **Pavilion**

## **Restaurant**

### **Ceiling**

### **Baffles**

### **Installation**



# Wagner Park Lawn Replacement





# Wagner Park South Allee







# **Wagner Park**

## **First Place**

## **Tide Gate**

## **Modifications**

BATTERY PARK CITY AUTHORITY





**First Place /  
MJH**

**Pavement  
Installation**






# **Pier A Plaza**

## **Tide Gate Jet Grouting**

BATTERY PARK CITY AUTHORITY



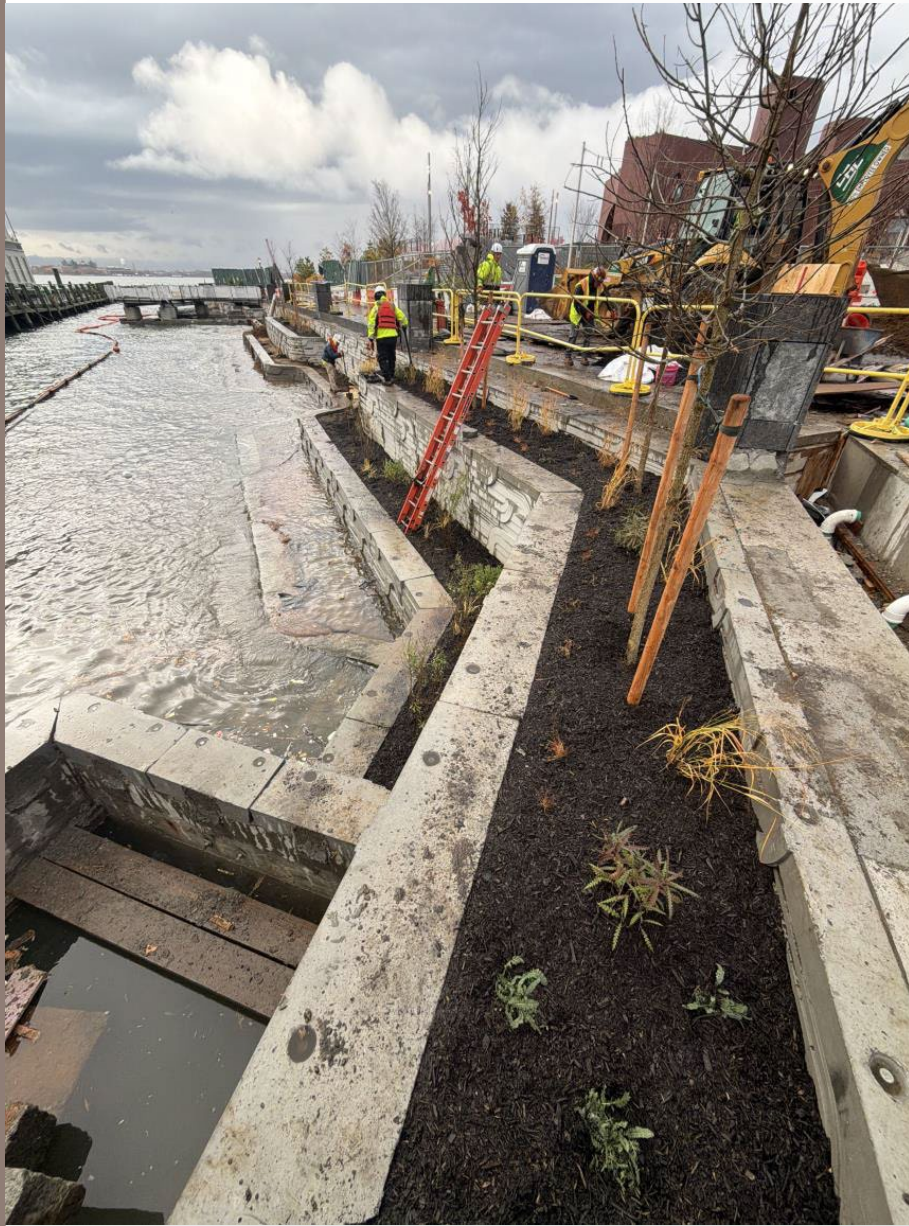

# Pier A

## Inlet ECOncrete Structure Plantings





# **The Battery**

## **Flood Wall Stone Mockup**

BATTERY PARK CITY AUTHORITY





**Battery Park  
City Authority**
