

# NW BATTERY PARK CITY RESILIENCY PROJECT

## MONTHLY COMMUNITY AIR QUALITY MONITORING REPORT

05 | 2026

ISSUE DATE: June 26, 2026

PERIOD COVERED: May 1 to May 31, 2026

PREPARED BY: Enovate Engineering, PLLC

SUBCONSULTANT TO: Turner-SPC JV



**Battery Park  
City Authority**

# TABLE OF CONTENTS

Introduction .....	3
Environmental Review .....	4
Community Air Quality Monitoring for PM10 and PM2.5 .....	4
Community Air Quality Monitoring for VOC.....	6
How to Read the Data Reports.....	8
Construction Summary .....	11
Summary of Monitoring Report .....	12
REACH 1.....	12
PM10.....	12
PM2.5.....	13
VOCs.....	13
NOTES .....	14
REACH 3.....	14
PM10.....	14
PM2.5.....	14
VOCs.....	14
NOTES .....	14
REACH 5.....	14
PM10.....	14
PM2.5.....	17
VOCs.....	17
NOTES .....	17
REACH 6 (Albany St).....	17
PM10.....	17
PM2.5.....	18
VOCs.....	18
NOTES .....	18
REACH 6 (Rector St).....	18
PM10.....	18
PM2.5.....	18
VOCs.....	18
NOTES .....	18
REACH 7 .....	18
PM10.....	18
PM2.5.....	19
VOCs.....	19
NOTES .....	20
Appendix A.....	21

## Introduction

In response to the devastating impacts of Superstorm Sandy on Lower Manhattan and in anticipation of future severe storm activity exacerbated by climate change, the North/West Battery Park City Resiliency (NWBPCR) Project has been developed as a critical component of the broader coastal flood risk management efforts in Lower Manhattan. The NWBPCR Project is being led by the Battery Park City Authority (BPCA) and represents the next phase of integrated resilience work following the South Battery Park City Resiliency (SBPCR) Project and other related initiatives.

The NWBPCR Project contemplates the creation of a continuous coastal flood risk management system extending from First Place in Battery Park City northward along the Battery Park City Esplanade, across to the east side of West Street/Route 9A and terminating above Chambers Street at a designated high point on Greenwich Street. This system is designed to provide reliable risk reduction to property, residents, infrastructure, and public assets within Battery Park City and adjacent western Tribeca neighborhoods, while preserving and enhancing open space, waterfront access, and community character.

NORTH/WEST BATTERY PARK CITY RESILIENCY PROJECT



Figure 1: Project Location

The purpose of the NWBPCR Project is to:

- Provide a reliable coastal flood risk management system that reduces flood risk to property, residents, critical infrastructure, and public assets within northern and western Battery Park City and adjacent portions of Lower Manhattan, in response to the design storm event.
- Protect and preserve, to the maximum extent practicable, existing open space resources, waterfront access, and opportunities for public use and recreation along the Battery Park City Esplanade, while maintaining the character of surrounding neighborhoods.
- Avoid or minimize disruption to existing below- and above-ground infrastructure (i.e., water and sewer infrastructure, roadways, subways, tunnels, and utilities) during flood events and throughout construction activities.

The NWBPCR Project builds upon earlier resiliency initiatives in Battery Park City and advances long-term coastal protection goals identified in the Lower Manhattan Coastal Resiliency (LMCR) Master Plan. The flood alignment is intended to meet Federal Emergency Management Agency (FEMA) accreditation requirements for protection against the 100-year storm event and to provide adaptability for future climate conditions, including sea level rise projections associated with mid-century storm scenarios. The project is designed to tie into adjacent resiliency systems, including the SBPCR Project, to create a unified coastal defense strategy. In addition to flood protection, the project incorporates enhancements to public open spaces, circulation, and waterfront amenities to improve overall resiliency, accessibility, and community use.

## Environmental Review

An Environmental Impact Statement (EIS) was prepared for the NWBPCR Project, which evaluated potential impacts associated with construction and operation, including air quality, noise, traffic, and other environmental parameters. The air quality analysis for construction activities considered the following on-site emission sources:

- Trucks and non-road construction equipment diesel engine exhaust.
- Surface fugitive dust generated by the movement of trucks and non-road equipment.
- Dust emissions associated with material handling and construction activities.

Potentially affected residential receptors within the study area were identified and evaluated as part of the environmental review, along with the proposed construction areas.

The NWBPCR team will be conducting air quality monitoring throughout construction in all seven Project Areas to ensure the ongoing health and safety of the adjacent community. In particular, the NWBPCR Air Quality Monitoring program will measure levels of Particulate Matter (PM) at two sizes: PM10 and PM2.5 and Volatile Organic Compounds (VOCs).

## Community Air Quality Monitoring for PM10 and PM2.5

PM stands for **particulate matter** (also called particle pollution or dust): the term for a mixture of solid particles and liquid droplets found in the air. Some particles, such as dust, dirt, soot, or smoke, are large or dark enough to be seen with the naked eye. Others are so small they can only be detected using an electron microscope. Particle pollution includes inhalable particles, with aerodynamic diameters that are generally 10 micrometers and smaller (PM10; also refer to as dust). Additionally, particles generally 2.5 micrometers and smaller (PM2.5; typically, from vehicle emissions) pose the greatest risk to health. Please see the following link from the Environmental Protection Agency (EPA) for reference: [EPA Particulate Matter \(PM\) Basics](#)

The BPCR team will be conducting real-time air quality monitoring throughout construction to ensure the ongoing health and safety of the adjacent community. In particular, the NWBPCR Air Quality Monitoring program will measure levels of Particulate Matter (PM) at PM10 and PM2.5.

The project area is divided into seven (7) reaches (Reach 1 through Reach 7) to facilitate construction phasing and environmental monitoring coverage. Stationary air monitoring units, located at pre-set sites, will monitor wider ambient air conditions. The stationary units are equipped with PM10 and PM2.5 continuous, real-time remote sensing instruments. They provide consistent air quality measurements over time, offering an extensive overview of regional air quality changes. However, this is not an environmental, safety of hygiene report as long as the action is immediate and effective.

The Clean Air Act (CAA) requires EPA to set National Ambient Air Quality Standards (NAAQS) for particulate matter, as one of the six criteria pollutants considered harmful to public health and the environment. The law also requires the United States EPA to periodically review the standards to ensure that they provide adequate health and environmental protection, and to update those standards as necessary. NAAQS for PM pollution specify a maximum amount of PM to be present in outdoor air.

The Permissible Exposure Limit (PEL) is a regulatory limit to protect public health/welfare set by the NAAQS in line with the requirements of the CAA on the amount or concentration of a substance in the air. The EPA has set a 24-

hour time weighted average (TWA) as standard for evaluating PM levels, meaning that they average potential PM exposure over a 24-hour period. This is also referred to as the daily value. New York State Department of Environmental Conservation (NYSDEC) and New York State Department of Health (NYSDOH) has set a 15-minute time weighted average as the standard for evaluating PM levels. In the line graphs presented in the NWBPCR monthly data plots, readings are averaged in 15-minute intervals and do not represent the standard TWA of 24-hrs. This more conservative approach will help the NWBPCR project team monitor the project's effect on air quality more closely.

The primary standard is a regulatory levels to protect public health/welfare set by the NAAQS in line with the requirements of the CAA on the amount or concentration of a substance in the air. The EPA primary standard for PM10 and PM2.5 is:

Averaging time:	24 hours
Regulatory level PM10:	150 $\mu\text{g}/\text{m}^3$
Regulatory level PM2.5:	35 $\mu\text{g}/\text{m}^3$
NAAQS form:	Not to be exceeded more than once per year on average over 3 years

The NYSDEC and NYCDOH standard for PM10 is:

Averaging time:	15 minutes
Action level PM10:	150 $\mu\text{g}/\text{m}^3$

The following procedure has been established if air quality measurements exceed the action levels for the 15-minute periods:

**PM10 Action Level 1.** If the downwind PM10 particulate level is 100  $\mu\text{g}/\text{m}^3$  greater than background for the 15-minute period or if airborne dust is measured leaving the work area, then automated alerts are dispatched to the general contractor and the construction management team. Dust suppression techniques must be employed. Work may continue with dust suppression techniques provided that downwind PM10 particulate levels do not exceed 150  $\mu\text{g}/\text{m}^3$  above the upwind level and provided that no visible dust is migrating from the work area.

**PM10 Action Level 2.** If, after implementation of dust suppression techniques, downwind PM10 particulate levels are greater than 150  $\mu\text{g}/\text{m}^3$  above the upwind level, work must be stopped, and a re-evaluation of activities initiated. Work can resume provided that dust suppression measures and other controls are successful in reducing the downwind PM10 particulate concentration to within 150  $\mu\text{g}/\text{m}^3$  of the upwind level and in preventing visible dust migration.

**PM2.5 Action Level 1.** If the downwind PM2.5 particulate level is 25  $\mu\text{g}/\text{m}^3$  greater than background for the 15-minute period or if airborne dust is measured leaving the work area, then automated alerts are dispatched to the general contractor and the construction management team. Dust suppression techniques must be employed. Work may continue with dust suppression techniques provided that downwind PM2.5 particulate levels do not exceed 35  $\mu\text{g}/\text{m}^3$  above the upwind level and provided that no visible dust is migrating from the work area.

**PM2.5 Action Level 2.** If, after implementation of dust suppression techniques, downwind PM2.5 particulate levels are greater than 35  $\mu\text{g}/\text{m}^3$  above the upwind level, work must be stopped, and a re-evaluation of activities initiated. Work can resume provided that dust suppression measures and other controls are successful in reducing the downwind PM2.5 particulate concentration to within 35  $\mu\text{g}/\text{m}^3$  of the upwind level and in preventing visible dust migration.

The PM10 and PM2.5 readings that follow by month in this report are shown in data plots, as below. The data plots illustrate PM levels in a **15-minute TWA**. As mentioned above, the local limits for PM are evaluated on a **15-minute TWA** and the federal limits for PM exposure are evaluated on a **24-hour TWA**. By evaluating PM readings on the 15-minute TWA, the NWBPCR project can ensure that Net PM never exceeds the 24-hour TWA, or daily value.

Along with air quality monitoring, the contractor is required to take extensive preventative measures to control dust and limit vehicle emissions. Potential mitigation techniques include but are not limited to:

- use of water spray for roads, trucks, excavation areas and stockpiles.
- use of anchored tarps to cover stockpiles.
- use of truck covers during soil transport within site limits and during off-site transport.
- employment of extra care during dry and/or high-wind periods.
- use of gravel or recycled concrete aggregate on egress and other roadways to provide a clean and dust-free road surface.
- use of a truck wheel wash at site access/egress points to prevent fugitive dust and off-site migration of dust and other particulates.

## Community Air Quality Monitoring for VOC

The NWBPCR team will be conducting air quality monitoring throughout construction to ensure the ongoing health and safety of the adjacent community. In particular, the NWBPCR Air Quality Monitoring program will measure levels of Volatile Organic Compounds (VOCs).

The project area is divided into seven (7) reaches (Reach 1 through Reach 7) to facilitate construction phasing and environmental monitoring coverage. Stationary air monitoring units, located at pre-set sites, will monitor wider ambient air conditions. The stationary units are equipped with VOC continuous, real-time remote sensing instruments. They provide consistent air quality measurements over time, offering an extensive overview of regional air quality changes. However, this is not an environmental, safety of hygiene report as long as the action is immediate and effective.

The action level to protect public health/welfare set by the New York State Department of Environmental Conservation (NYSDEC) and New York State Department of Health (NYSDOH). The NYSDEC and NYSDOH has set a 15-minute time weighted average (TWA) as standard for evaluating VOC levels, meaning that they average potential VOC exposure over a 15-minute period. In the line graphs presented in the NWBPCR monthly data plots, readings are averaged in 15-minute intervals.

The NYSDEC and NYSDOH standard for VOC is:

Averaging time:	15 minutes
Action level VOC:	25 ppm

The following procedure has been established if air quality measurements exceed the action levels for the 15-minute periods:


**VOC Action level 1.** If the ambient air concentration of total organic vapors at the downwind perimeter of the work area or exclusion zone exceeds 5 ppm above background for the 15-minute average, then automated alerts are dispatched to the general contractor and the construction management team. Work activities must be temporarily halted and monitoring continued. If the total organic vapor level readily decreases (per instantaneous readings) below 5 ppm over background, work activities can resume with continued monitoring. As a background, the value of 0 ppm has been adopted based on the final Environmental Impact Statement (EIS) for the project. **Hence, the VOC Action Level 1 is >5 ppm.**

**VOC Action Level 2.** If total organic vapor levels at the downwind perimeter of the work area or exclusion zone persist at levels in excess of 5 ppm over background but less than 25 ppm, work activities must be halted, the source of vapors identified, corrective actions taken to abate emissions, and monitoring continued. After these steps, work activities can resume provided that the total organic vapor level 200 feet downwind of the exclusion zone or half the distance to the nearest potential receptor or residential/commercial structure, whichever is less - but in no case less than 20 feet, is below 5 ppm over background for the 15-minute average. **Hence, the VOC Action Level 2 is applicable when the range is >5 and <25 ppm.**

**VOC Action Level 3.** If the organic vapor level is above 25 ppm at the perimeter of the work area, activities must be shutdown. **Hence, the VOC Action Level 3 is >25 ppm.**

# How to Read the Data Reports

The PM and VOC readings that follow by week in this report are shown in data reports, as below. The data plots illustrate PM and VOC levels in a 15-minute TWA.



**Environmental Summary**

**Title**  
Reach 6\_EWP\_AQS Report

**Action Levels**

PM10 Action Level:	100 µg/m³
PM2.5 Action Level:	25 µg/m³
VOC Action Level:	5 ppm

**Reporting Period**

Battery Park_AQS	
Report Period	
From:	02/02/2026 00:00
To:	02/08/2026 23:59


Daily Environmental Summary	Temp (°F)	Relative Humidity (%)	Barometer (inHg)	Wind Speed (mph)	Prevailing Wind Direction
02/02/2026	26.1 - 33.1	0.0 - 0.0	29.7 - 31.0	0.6 - 6.0	NNW
02/03/2026	21.9 - 32.7	0.0 - 0.0	26.9 - 31.8	0.5 - 6.9	NNE
02/04/2026	25.9 - 33.4	0.0 - 0.0	27.0 - 31.5	0.0 - 7.5	NNE
02/05/2026	20.5 - 31.5	0.0 - 0.0	26.8 - 33.8	0.5 - 5.2	SE
02/06/2026	22.8 - 34.9	0.0 - 0.0	26.6 - 32.7	0.5 - 4.8	E
02/07/2026	5.4 - 26.6	0.0 - 0.0	26.7 - 31.0	0.8 - 11.4	SE
02/08/2026	3.2 - 16.2	0.0 - 0.0	26.8 - 31.4	1.8 - 10.6	SE

Daily Monitoring Summary	PM2.5 (µg/m³)	Time	PM10 (µg/m³)	Time	VOC (ppm)	Time
Min Contribution (15 min avg.) - 2/2/2026	0.0	11:45	0.0	11:15	0.0000	11:30
Max Contribution (15 min avg.) - 2/2/2026	0.4	11:15	0.4	15:00	0.0060	11:15
Daily Avg. Contribution (15 min avg.) - 2/2/2026	0.1	-	0.0	-	0.0002	-
Min Contribution (15 min avg.) - 2/3/2026	0.0	16:30	0.0	00:00	0.0000	00:00
Max Contribution (15 min avg.) - 2/3/2026	6.5	10:00	5.1	10:00	0.0013	22:15
Daily Avg. Contribution (15 min avg.) - 2/3/2026	1.7	-	0.5	-	0.0001	-
Min Contribution (15 min avg.) - 2/4/2026	0.0	00:15	0.0	00:15	0.0000	00:00
Max Contribution (15 min avg.) - 2/4/2026	4.7	07:45	3.9	01:30	0.0040	02:45
Daily Avg. Contribution (15 min avg.) - 2/4/2026	0.9	-	0.5	-	0.0002	-
Min Contribution (15 min avg.) - 2/5/2026	0.0	00:00	0.0	00:00	0.0000	00:00
Max Contribution (15 min avg.) - 2/5/2026	1.3	09:30	4.0	15:30	0.0220	13:00
Daily Avg. Contribution (15 min avg.) - 2/5/2026	0.1	-	0.4	-	0.0038	-
Min Contribution (15 min avg.) - 2/6/2026	0.0	00:00	0.0	00:00	0.0000	00:00
Max Contribution (15 min avg.) - 2/6/2026	26.8	13:30	111.5	13:30	0.0540	13:30
Daily Avg. Contribution (15 min avg.) - 2/6/2026	0.4	-	1.4	-	0.0026	-
Min Contribution (15 min avg.) - 2/7/2026	0.0	00:00	0.0	00:00	0.0000	00:00
Max Contribution (15 min avg.) - 2/7/2026	2.4	05:30	4.2	05:30	0.0060	05:00
Daily Avg. Contribution (15 min avg.) - 2/7/2026	0.0	-	0.8	-	0.0003	-
Min Contribution (15 min avg.) - 2/8/2026	0.0	00:00	0.0	00:00	0.0000	00:00
Max Contribution (15 min avg.) - 2/8/2026	0.0	00:00	0.7	15:15	0.0020	09:00
Daily Avg. Contribution (15 min avg.) - 2/8/2026	0.0	-	0.0	-	0.0001	-




Air Monitor Station Locations

PM2.5 Average Contribution ( $\mu\text{g}/\text{m}^3$ )

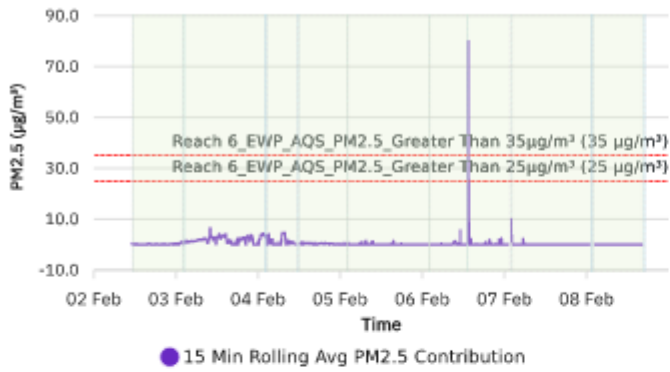


PM10 Average Contribution ( $\mu\text{g}/\text{m}^3$ )


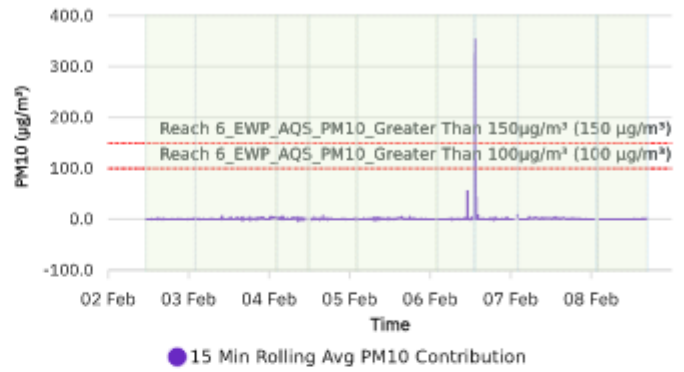


Stopped Initial Avg Rolling Avg

VOC Average Contribution (ppm)

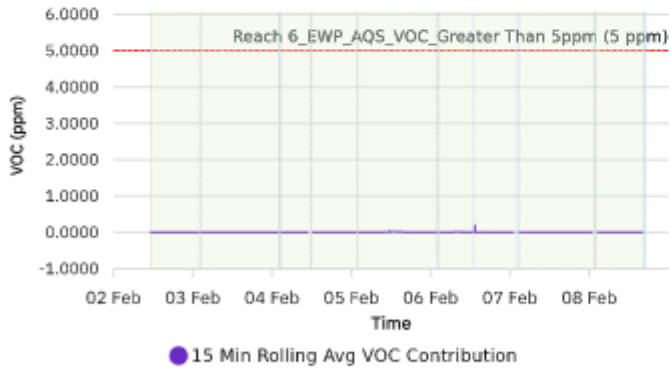

Contribution Measurements

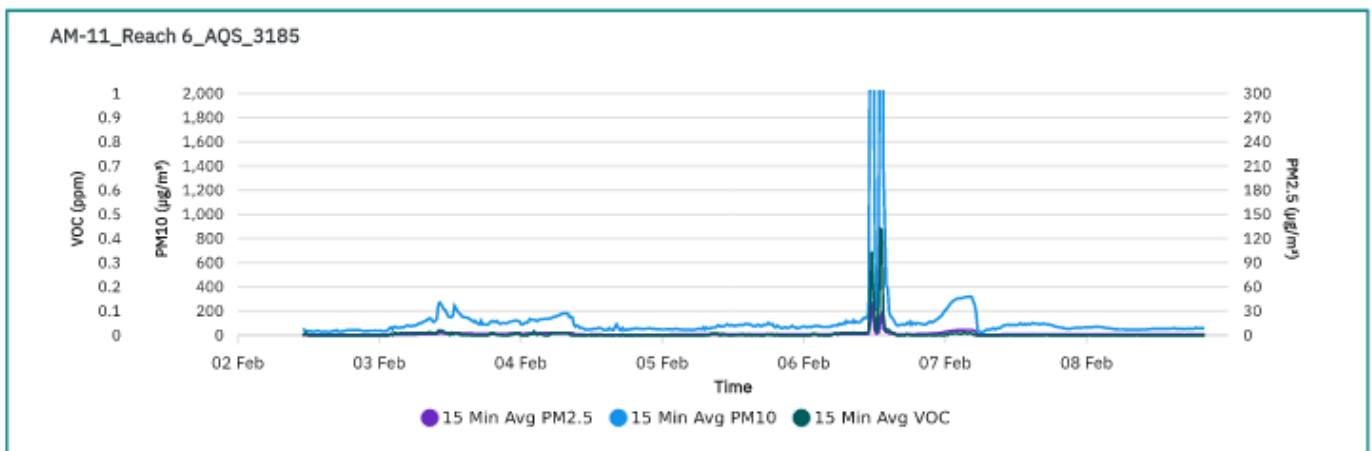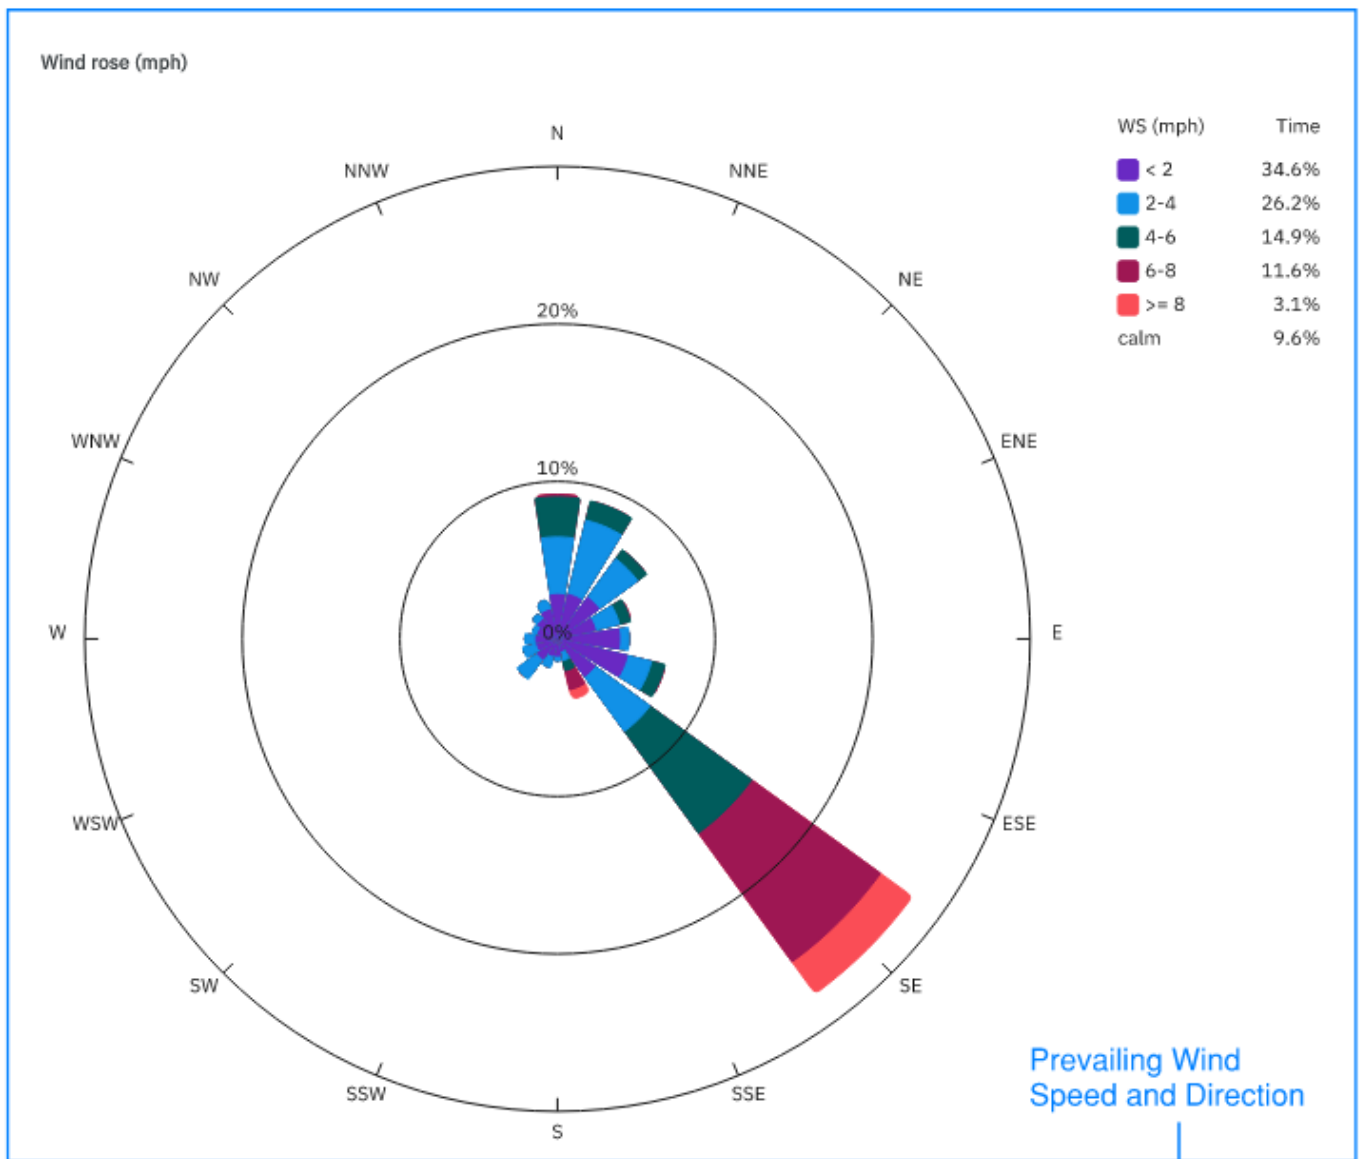

Individual Air Monitor Measurements

**Exceedance Summary**

Parameter	Action Level	Time Triggered	Cause	Mitigation
PM10	100.0 µg/m³	2/6/2026 13:19		
PM2.5	25.0 µg/m³	2/6/2026 13:20		

**Exceedance Summary**

- The title states the location and work phase of each report.
- The reporting period is the start and end date of each report.
- The action levels correspond to the regulatory levels and the action levels described above.
- The environmental summary provides a daily summary of Temperature, Relative Humidity, Barometric Level, Wind Speed, and Prevailing Wind Direction over the reporting period.
- The Daily Summary of Site Contributions provides the minimum, maximum and daily average of each measured parameter for the reporting period. The contribution measurements are determined as the difference between the upwind and downwind monitoring stations as determined on any day given the wind speed and wind direction. At each reach location at least two air quality monitors are required to determine the Site Contribution. The Site Contribution value is important because it measures the potential increase of particulate matter due to construction activities. If the wind speed is less than 1 mile per hour, the downwind station is considered undetermined, and the Site Contribution will be absent from the data plot. In these circumstances, high measurements at one or both monitoring stations will still be noted, however the increased levels in the PM and VOC measurements may be due to conditions unrelated to construction.
- The air monitoring stations are presented on a map view for each reach. Air monitoring stations are GPS tracked and will update automatically if relocated within the reach.
- The Site Contribution charts for 15-minute periods over the reporting period. Action levels for each parameter are shown on the charts.
- The wind rose displays the wind speed and prevailing wind direction over the reporting period based on percentage.
- The individual air monitoring station charts show different parameters for that individual monitoring station only. No site contribution data is presented in this chart. The data within this chart is used with other individual monitoring stations to create the site contribution. The chart title corresponds to the air monitor location on the map view.
- The exceedance summary provides a quick view of all site contribution exceedances for the 15-minute periods over the reporting period.

**Construction Summary**

Construction started November 11, 2025. Contractor working hours are 7am-4pm Monday-Friday.

**Reach 1**

Turner-SPC to provide construction summary

- Excavation
- Utility Relocations
- Electrical Conduit and Ductbank Installation
- Manhole Installation
- Support of Excavation Installation

### Reach 3

Turner-SPC to provide construction summary

- Utility Relocation Preparation
- Electrical Trench Excavation
- Electrical Conduit and Ductbank Installation
- Water Main Relocation Activities

### Reach 5

Turner-SPC to provide construction summary

- Excavation
- Utility Relocations
- Electrical Conduit and Ductbank Installation
- Manhole Installation
- Tree Removal and Site Clearing
- Salvage and Early Demolition Activities

### Reach 6

Turner-SPC to provide construction summary

- Utility Relocations
- Tide Gate Construction
- Support of Excavation Installation
- Electrical Demolition and Conduit Installation

### Reach 7

Turner-SPC to provide construction summary

- Tree Pruning and Tree Removal
- Surface Demolition and Salvage Activities
- Site Fence Installation
- Utility Investigations and Soil Sampling
- Water Main Relocation Activities

## Summary of Monitoring Report

For the reporting period of May 1 - 31, 2026, Reach 1 was monitored with two (2) stationary units, Reach 3 was monitored with two (2) stationary units, Reach 5 was monitored with five (5) stationary units, Reach 6 with four (4) stationary units and Reach 7 with five (5) stationary units. Locations of these air monitoring stations are presented within each report in **Appendix A**.

For the reporting period the construction-related site contribution for PM10 and PM2.5 did not exceed the regulatory levels for the 24-hour TWA. Exceedances of the 15-min TWA site contributions, the cause of the exceedances, and the contractor's mitigation methods are detailed below.

### REACH 1

#### PM10

Time series plots of PM10 15-min average concentrations are shown in **Appendix A** for each monitoring location. The action level 1 (PM10 > 100 µg/m<sup>3</sup>) and action level 2 (PM10 > 150 µg/m<sup>3</sup>) are shown as well.

- One (1) PM10 exceedance of Action Level 1 (PM10 > 100 µg/m<sup>3</sup>) occurred on Wednesday 05/13/2026 at approximately 04:51. Elevated readings were attributable to subcontractor activities.
- One (1) PM10 exceedance of Action Level 2 (PM10 > 150 µg/m<sup>3</sup>) occurred on Wednesday 05/13/2026 at approximately 04:59. Elevated readings were attributable to subcontractor activities. PM10 levels returned to below action levels by the subsequent monitoring interval. Contractor deemed mitigation methods were not warranted.

- One (1) PM10 exceedance of Action Level 2 ( $\text{PM}_{10} > 150 \mu\text{g}/\text{m}^3$ ) occurred on Friday 05/15/2026 at approximately 04:54. Elevated readings were attributable to subcontractor activities. PM10 levels returned to below action levels by the subsequent monitoring interval. Contractor deemed mitigation methods were not warranted.
- One (1) PM10 exceedance of Action Level 2 ( $\text{PM}_{10} > 150 \mu\text{g}/\text{m}^3$ ) occurred on Wednesday 05/20/2026 at approximately 18:16. Elevated readings were attributable to wind-blown dust across the site. Contractor wetted the area to mitigate dust levels and fugitive dust. PM10 levels returned to below action levels by the subsequent monitoring interval.
- One (1) PM10 exceedance of Action Level 2 ( $\text{PM}_{10} > 150 \mu\text{g}/\text{m}^3$ ) occurred on Friday 05/29/2026 at approximately 01:12. Elevated readings were attributable to wind-blown dust across the site. Contractor wetted the area to mitigate dust levels and fugitive dust. PM10 levels returned to below action levels by the subsequent monitoring interval.
- Two (2) PM10 exceedances of Action Level 1 ( $\text{PM}_{10} > 100 \mu\text{g}/\text{m}^3$ ) occurred on Saturday 05/30/2026 at approximately 02:48 and 04:05. Elevated readings were attributable to wind-blown dust across the site.
- Two (2) PM10 exceedances of Action Level 2 ( $\text{PM}_{10} > 150 \mu\text{g}/\text{m}^3$ ) occurred on Saturday 05/30/2026 at approximately 03:19 and 11:51. Elevated readings were attributable to wind-blown dust across the site. Contractor wetted the area to mitigate dust levels and fugitive dust. PM10 levels returned to below action levels by the subsequent monitoring interval.

## PM2.5

Time series plots of PM2.5 15-min average concentrations are shown in **Appendix A** for each monitoring location. The action level 1 ( $\text{PM}_{2.5} > 25 \mu\text{g}/\text{m}^3$ ) and action level 2 ( $\text{PM}_{2.5} > 35 \mu\text{g}/\text{m}^3$ ) are shown as well.

- One (1) PM2.5 exceedance of Action Level 1 ( $\text{PM}_{2.5} > 25 \mu\text{g}/\text{m}^3$ ) occurred on Friday 05/15/2026 at approximately 04:36. Elevated readings were attributable to subcontractor activities.
- One (1) PM2.5 exceedance of Action Level 2 ( $\text{PM}_{2.5} > 35 \mu\text{g}/\text{m}^3$ ) occurred on Friday 05/15/2026 at approximately 05:01. Elevated readings were attributable to subcontractor activities. PM2.5 levels returned to below action levels by the subsequent monitoring interval. Contractor deemed mitigation methods were not warranted.
- Two (2) PM2.5 exceedances of Action Level 1 ( $\text{PM}_{2.5} > 25 \mu\text{g}/\text{m}^3$ ) occurred on Thursday 05/28/2026 at approximately 23:03 and 23:21. Elevated readings were attributable to wind-blown dust across the site.
- One (1) PM2.5 exceedance of Action Level 2 ( $\text{PM}_{2.5} > 35 \mu\text{g}/\text{m}^3$ ) occurred on Friday 05/29/2026 at approximately 01:11. Elevated readings were attributable to wind-blown dust across the site. Contractor wetted the area to mitigate dust levels and fugitive dust. PM2.5 levels returned to below action levels by the subsequent monitoring interval.
- One (1) PM2.5 exceedance of Action Level 1 ( $\text{PM}_{2.5} > 25 \mu\text{g}/\text{m}^3$ ) occurred on Saturday 05/30/2026 at approximately 12:00. Elevated readings were attributable to wind-blown dust across the site. Contractor wetted the area to mitigate dust levels and fugitive dust. PM2.5 levels returned to below action levels by the subsequent monitoring interval.

## VOCs

Time series plots of VOCs 15-min average concentrations are shown in **Appendix A** for each monitoring location. The action level (VOC Action Level 1:  $\text{VOC} > 5\text{ppm}$ ) is shown as well.

- No VOC exceedances were recorded during this monitoring period.

## NOTES

- AM-32 disconnected from power on Monday 05/25/2026 at 22:00 to Tuesday 05/26/2026 at 07:00.
- AM-33 disconnected from power on Monday 05/18/2026 at 22:00 to Tuesday 05/19/2026 at 06:00.

## REACH 3

### PM10

Time series plots of PM10 15-min average concentrations are shown in **Appendix A** for each monitoring location. The action level 1 (PM10 > 100 µg/m<sup>3</sup>) and action level 2 (PM10 > 150 µg/m<sup>3</sup>) are shown as well.

- No PM10 exceedances were recorded during this monitoring period.

### PM2.5

Time series plots of PM2.5 15-min average concentrations are shown in **Appendix A** for each monitoring location. The action level 1 (PM2.5 > 25 µg/m<sup>3</sup>) and action level 2 (PM2.5 > 35µg/m<sup>3</sup>) are shown as well.

- Five (5) PM2.5 exceedances of Action Level 1 (PM2.5 > 25 µg/m<sup>3</sup>) occurred on Sunday 05/10/2026 at approximately 01:26, 12:16, 12:52, 15:18 and 15:38. Elevated readings were attributable to subcontractor work activities within the project area. PM2.5 levels returned to below action levels by the subsequent monitoring interval. Contractor deemed mitigation methods were not warranted.

## VOCs

Time series plots of VOCs 15-min average concentrations are shown in **Appendix A** for each monitoring location. The action level (VOC Action Level 1: VOC > 5ppm) is shown as well.

- No VOC exceedances were recorded during this monitoring period.

## NOTES

- AM-31 disconnected from power on Monday 05/25/2026 at 19:00 to Tuesday 05/26/2026 at 07:00.
- AM-30 disconnected from power on Friday 05/29/2026 at 09:00 to Sunday 05/31/2026 at 23:00.

## REACH 5

### PM10

Time series plots of PM10 15-min average concentrations are shown in **Appendix A** for each monitoring location. The action level 1 (PM10 > 100 µg/m<sup>3</sup>) and action level 2 (PM10 > 150 µg/m<sup>3</sup>) are shown as well.

- One (1) PM10 exceedance of Action Level 2 (PM10 > 150 µg/m<sup>3</sup>) occurred on Friday 05/01/2026 at approximately 13:36. Elevated readings were attributable to construction activities within the project area. Contractor utilized a garden hose to mitigate dust levels and fugitive dust. PM10 levels returned to below action levels by the subsequent monitoring interval.
- Two (2) PM10 exceedances of Action Level 2 (PM10 > 150 µg/m<sup>3</sup>) occurred on Sunday 05/03/2026 at approximately 13:27 and 17:24. Elevated readings were attributable to wind-blown dust across the site.
- One (1) PM10 exceedance of Action Level 2 (PM10 > 150 µg/m<sup>3</sup>) occurred on Monday 05/04/2026 at approximately 21:08. Elevated readings were attributable to wind-blown dust across the site.
- One (1) PM10 exceedance of Action Level 1 (PM10 > 100 µg/m<sup>3</sup>) occurred on Monday 05/04/2026 at approximately 22:04. Elevated readings were attributable to wind-blown dust across the site.

- One (1) PM10 exceedances of Action Level 1 (PM10 > 100 µg/m<sup>3</sup>) occurred on Tuesday 05/05/2026 at approximately 12:50. Elevated readings were attributable to construction activities within the project area. Contractor utilized a garden hose to mitigate dust levels and fugitive dust. PM10 levels returned to below action levels by the subsequent monitoring interval.
- Two (2) PM10 exceedances of Action Level 2 (PM10 > 150 µg/m<sup>3</sup>) occurred on Tuesday 05/05/2026 at approximately 15:25 and 15:44. Elevated readings were attributable to construction activities within the project area. Contractor utilized a garden hose to mitigate dust levels and fugitive dust. PM10 levels returned to below action levels by the subsequent monitoring interval.
- Two (2) PM10 exceedance of Action Level 1 (PM10 > 100 µg/m<sup>3</sup>) occurred on Tuesday 05/05/2026 at approximately 16:48 and 17:22. Elevated readings were attributable to wind-blown dust across the site.
- One (1) PM10 exceedances of Action Level 2 (PM10 > 150 µg/m<sup>3</sup>) occurred on Wednesday 05/06/2026 at approximately 07:46. Elevated readings were attributable to construction activities within the project area. Contractor utilized a garden hose to mitigate dust levels and fugitive dust. PM10 levels returned to below action levels by the subsequent monitoring interval.
- Two (2) PM10 exceedances of Action Level 1 (PM10 > 100 µg/m<sup>3</sup>) occurred on Thursday 05/07/2026 at approximately 12:47 and 14:49. Elevated readings were attributable to construction activities within the project area. Contractor utilized a garden hose to mitigate dust levels and fugitive dust. PM10 levels returned to below action levels by the subsequent monitoring interval.
- Two (2) PM10 exceedances of Action Level 2 (PM10 > 150 µg/m<sup>3</sup>) occurred on Thursday 05/07/2026 at approximately 13:19 and 13:52. Elevated readings were attributable to construction activities within the project area. Contractor utilized a garden hose to mitigate dust levels and fugitive dust. PM10 levels returned to below action levels by the subsequent monitoring interval.
- One (1) PM10 exceedance of Action Level 1 (PM10 > 100 µg/m<sup>3</sup>) occurred on Thursday 05/07/2026 at approximately 17:39. Elevated readings were attributable to wind-blown dust across the site.
- One (1) PM10 exceedances of Action Level 2 (PM10 > 150 µg/m<sup>3</sup>) occurred on Friday 05/08/2026 at approximately 16:04. Elevated readings were attributable to construction activities within the project area. Contractor utilized a garden hose to mitigate dust levels and fugitive dust. PM10 levels returned to below action levels by the subsequent monitoring interval.
- One (1) PM10 exceedance of Action Level 2 (PM10 > 150 µg/m<sup>3</sup>) occurred on Monday 05/11/2026 at approximately 07:29. Elevated readings were attributable to construction activities within the project area. Contractor utilized a garden hose to mitigate dust levels and fugitive dust. PM10 levels returned to below action levels by the subsequent monitoring interval.
- One (1) PM10 exceedances of Action Level 1 (PM10 > 100 µg/m<sup>3</sup>) occurred on Tuesday 05/12/2026 at approximately 13:04. Elevated readings were attributable to construction activities within the project area. Contractor utilized a garden hose to mitigate dust levels and fugitive dust. PM10 levels returned to below action levels by the subsequent monitoring interval.
- One (1) PM10 exceedances of Action Level 2 (PM10 > 150 µg/m<sup>3</sup>) occurred on Tuesday 05/12/2026 at approximately 11:33. Elevated readings were attributable to construction activities within the project area. Contractor utilized a garden hose to mitigate dust levels and fugitive dust. PM10 levels returned to below action levels by the subsequent monitoring interval.
- One (1) PM10 exceedance of Action Level 2 (PM10 > 150 µg/m<sup>3</sup>) occurred on Wednesday 05/13/2026 at approximately 13:33. Elevated readings were attributable to construction activities within the project area. Contractor utilized a garden hose to mitigate dust levels and fugitive dust. PM10 levels returned to below

action levels by the subsequent monitoring interval.

- One (1) PM10 exceedance of Action Level 2 ( $\text{PM}_{10} > 150 \mu\text{g}/\text{m}^3$ ) occurred on Thursday 05/14/2026 at approximately 18:31. Elevated readings were attributable to wind-blown dust across the site.
- Four (4) PM10 exceedances of Action Level 2 ( $\text{PM}_{10} > 150 \mu\text{g}/\text{m}^3$ ) occurred on Friday 05/15/2026 at approximately 07:15, 10:18, 12:57 and 13:39. Elevated readings were attributable to construction activities within the project area. Contractor utilized a garden hose to mitigate dust levels and fugitive dust. PM10 levels returned to below action levels by the subsequent monitoring interval.
- One (1) PM10 exceedance of Action Level 1 ( $\text{PM}_{10} > 100 \mu\text{g}/\text{m}^3$ ) occurred on Monday 05/18/2026 at approximately 13:22. Elevated readings were attributable to wind-blown dust across the site.
- One (1) PM10 exceedance of Action Level 2 ( $\text{PM}_{10} > 150 \mu\text{g}/\text{m}^3$ ) occurred on Monday 05/18/2026 at approximately 14:04. Elevated readings were attributable to wind-blown dust across the site. Contractor wetted the area to mitigate dust levels and fugitive dust. PM10 levels returned to below action levels by the subsequent monitoring interval.
- Two (2) PM10 exceedances of Action Level 1 ( $\text{PM}_{10} > 100 \mu\text{g}/\text{m}^3$ ) occurred on Tuesday 05/19/2026 at approximately 13:54 and 16:50. Elevated readings were attributable to wind-blown dust across the site.
- One (1) PM10 exceedance of Action Level 2 ( $\text{PM}_{10} > 150 \mu\text{g}/\text{m}^3$ ) occurred on Tuesday 05/19/2026 at approximately 14:56. Elevated readings were attributable to wind-blown dust across the site. Contractor wetted the area to mitigate dust levels and fugitive dust. PM10 levels returned to below action levels by the subsequent monitoring interval.
- Two (2) PM10 exceedances of Action Level 2 ( $\text{PM}_{10} > 150 \mu\text{g}/\text{m}^3$ ) occurred on Wednesday 05/20/2026 at approximately 18:16 and 19:01. Elevated readings were attributable to wind-blown dust across the site. Contractor wetted the area to mitigate dust levels and fugitive dust. PM10 levels returned to below action levels by the subsequent monitoring interval.
- Two (2) PM10 exceedances of Action Level 2 ( $\text{PM}_{10} > 150 \mu\text{g}/\text{m}^3$ ) occurred on Wednesday 05/27/2026 at approximately 23:32 and 23:51. Elevated readings were caused by wind-blown dust across the site. Contractor wetted soil to mitigate dust levels and fugitive dust. PM10 levels returned to below action levels by the subsequent monitoring interval.
- One (1) PM10 exceedance of Action Level 1 ( $\text{PM}_{10} > 100 \mu\text{g}/\text{m}^3$ ) occurred on Thursday 05/28/2026 at approximately 01:47. Elevated readings were caused by wind-blown dust across the site.
- One (1) PM10 exceedances of Action Level 1 ( $\text{PM}_{10} > 100 \mu\text{g}/\text{m}^3$ ) occurred on Thursday 05/28/2026 at approximately 13:21. Elevated readings were attributable to construction activities within the project area. Contractor utilized a garden hose to mitigate dust levels and fugitive dust. PM10 levels returned to below action levels by the subsequent monitoring interval.
- Three (3) PM10 exceedances of Action Level 2 ( $\text{PM}_{10} > 150 \mu\text{g}/\text{m}^3$ ) occurred on Thursday 05/28/2026 at approximately 08:59, 11:38 and 14:32. Elevated readings were attributable to construction activities within the project area. Contractor wetted soil to mitigate dust levels and fugitive dust. PM10 levels returned to below action levels by the subsequent monitoring interval.
- Five (5) PM10 exceedances of Action Level 1 ( $\text{PM}_{10} > 100 \mu\text{g}/\text{m}^3$ ) occurred on Saturday 05/30/2026 at approximately 02:42, 04:14, 05:55, 06:39 and 09:14. Elevated readings were attributable to wind-blown dust across the site and a generator operating improperly. The generator was removed from service.

## PM2.5

Time series plots of PM2.5 15-min average concentrations are shown in **Appendix A** for each monitoring location. The action level 1 (PM2.5 > 25 µg/m<sup>3</sup>) and action level 2 (PM2.5 > 35µg/m<sup>3</sup>) are shown as well.

- One (1) PM2.5 exceedance of Action Level 2 (PM2.5 > 35 µg/m<sup>3</sup>) occurred on Thursday 05/07/2026 at approximately 07:06. Elevated readings were attributable to construction activities within the project area. Contractor utilized a garden hose to mitigate dust levels and fugitive dust. PM2.5 levels returned to below action levels by the subsequent monitoring interval.
- One (1) PM2.5 exceedance of Action Level 1 (PM2.5 > 25 µg/m<sup>3</sup>) occurred on Sunday 05/10/2026 at approximately 11:49. Elevated readings were caused by wind-blown dust across the site.
- One (1) PM2.5 exceedance of Action Level 2 (PM2.5 > 35 µg/m<sup>3</sup>) occurred on Tuesday 05/12/2026 at approximately 11:43. Elevated readings were attributable to construction activities within the project area. Contractor utilized a garden hose to mitigate dust levels and fugitive dust. PM2.5 levels returned to below action levels by the subsequent monitoring interval.
- One (1) PM2.5 exceedance of Action Level 1 (PM2.5 > 25 µg/m<sup>3</sup>) occurred on Monday 05/18/2026 at approximately 14:08. Elevated readings were caused by wind-blown dust across the site. Contractor wetted soil to mitigate dust levels and fugitive dust. PM10 levels returned to below action levels by the subsequent monitoring interval.
- Three (3) PM2.5 exceedances of Action Level 1 (PM2.5 > 25 µg/m<sup>3</sup>) occurred on Thursday 05/28/2026 at approximately 13:27, 14:39 and 14:55. Elevated readings were attributable to construction activities within the project area. Contractor wetted soil to mitigate dust levels and fugitive dust. PM2.5 levels returned to below action levels by the subsequent monitoring interval.
- One (1) PM2.5 exceedance of Action Level 1 (PM2.5 > 25 µg/m<sup>3</sup>) occurred on Saturday 05/30/2026 at approximately 04:23. Elevated readings were caused by wind-blown dust across the site.

## VOCs

Time series plots of VOCs 15-min average concentrations are shown in **Appendix A** for each monitoring location. The action level (VOC Action Level 1: VOC > 5ppm) is shown as well.

- No VOC exceedances were recorded during this monitoring period.

## NOTES

- AM-18 disconnected from power on Monday 05/04/2026 at 02:00 to Monday 05/04/2026 at 08:00.
- AM-18 disconnected from power on Monday 05/25/2026 at 07:00 to Monday 05/26/2026 at 06:00.
- AM-16 disconnected from power on Tuesday 05/26/2026 at 00:00 to Tuesday 05/26/2026 at 06:00.

## REACH 6 (Albany St)

### PM10

Time series plots of PM10 15-min average concentrations are shown in **Appendix A** for each monitoring location. The action level 1 (PM10 > 100 µg/m<sup>3</sup>) and action level 2 (PM10 > 150 µg/m<sup>3</sup>) are shown as well.

- One (1) PM10 exceedance of Action Level 2 (PM10 > 150 µg/m<sup>3</sup>) occurred on Monday 05/18/2026 at approximately 13:14. Elevated readings were due to concrete demolition. Contractor wetted the area to mitigate dust levels and fugitive dust. PM10 levels returned to below action levels by the subsequent monitoring interval.
- One (1) PM10 exceedance of Action Level 1 (PM10 > 100 µg/m<sup>3</sup>) occurred on Saturday 05/30/2026 at approximately 04:14. Elevated readings were caused by wind-blown dust across the site.

## PM2.5

Time series plots of PM2.5 15-min average concentrations are shown in **Appendix A** for each monitoring location. The action level 1 (PM2.5 > 25 µg/m<sup>3</sup>) and action level 2 (PM2.5 > 35µg/m<sup>3</sup>) are shown as well.

- No PM2.5 exceedances were recorded during this monitoring period.

## VOCs

Time series plots of VOCs 15-min average concentrations are shown in **Appendix A** for each monitoring location. The action level (VOC Action Level 1: VOC > 5ppm) is shown as well.

- No VOC exceedances were recorded during this monitoring period.

## NOTES

- AM-12 disconnected from power on Monday 05/25/2026 at 09:00 to Tuesday 05/26/2026 at 06:00.

## REACH 6 (Rector St)

### PM10

Time series plots of PM10 15-min average concentrations are shown in **Appendix A** for each monitoring location. The action level 1 (PM10 > 100 µg/m<sup>3</sup>) and action level 2 (PM10 > 150 µg/m<sup>3</sup>) are shown as well.

- No PM10 exceedances were recorded during this monitoring period.

### PM2.5

Time series plots of PM2.5 15-min average concentrations are shown in **Appendix A** for each monitoring location. The action level 1 (PM2.5 > 25 µg/m<sup>3</sup>) and action level 2 (PM2.5 > 35µg/m<sup>3</sup>) are shown as well.

- No PM2.5 exceedances were recorded during this monitoring period.

## VOCs

Time series plots of VOCs 15-min average concentrations are shown in **Appendix A** for each monitoring location. The action level (VOC Action Level 1: VOC > 5ppm) is shown as well.

- No VOC exceedances were recorded during this monitoring period.

## NOTES

- AM-09 disconnected from power on Thursday 05/07/2026 at 09:00 to Friday 05/08/2026 at 08:00.
- AM-09 disconnected from power on Sunday 05/17/2026 at 05:00 to Monday 05/18/2026 at 07:00.
- AM-10 disconnected from power on Thursday 05/07/2026 at 09:00 to Friday 05/08/2026 at 08:00.
- AM-10 disconnected from power on Saturday 05/23/2026 at 14:00 to Tuesday 05/26/2026 at 08:00.

## REACH 7

### PM10

Time series plots of PM10 15-min average concentrations are shown in **Appendix A** for each monitoring location. The action level 1 (PM10 > 100 µg/m<sup>3</sup>) and action level 2 (PM10 > 150 µg/m<sup>3</sup>) are shown as well.

- Four (4) PM10 exceedances of Action Level 1 (PM10 > 100 µg/m<sup>3</sup>) occurred on Tuesday 05/12/2026 at approximately 09:42, 11:45, 12:12, and 12:13. Elevated readings were attributable to construction activities within the project area.
- One (1) PM10 exceedance of Action Level 2 (PM10 > 150 µg/m<sup>3</sup>) occurred on Tuesday 05/12/2026. Elevated readings were attributable to construction activities within the project area. Contractor utilized a garden hose

to mitigate dust levels and fugitive dust. PM10 levels returned to below action levels by the subsequent monitoring interval.

- Two (2) PM10 exceedances of Action Level 2 (PM10 > 150 µg/m<sup>3</sup>) occurred on Monday 05/18/2026 at approximately 18:16 and 19:01. Elevated readings were attributable to wind-blown dust across the site. Contractor wetted the area to mitigate dust levels and fugitive dust. PM10 levels returned to below action levels by the subsequent monitoring interval.
- Three (3) PM10 exceedances of Action Level 2 (PM10 > 150 µg/m<sup>3</sup>) occurred on Tuesday 05/19/2026 at approximately 07:38, 08:31, and 13:21. Elevated readings were due to concrete demolition. Contractor wetted the area to mitigate dust levels and fugitive dust. PM10 levels returned to below action levels by the subsequent monitoring interval.
- Four (4) PM10 exceedances of Action Level 1 (PM10 > 100 µg/m<sup>3</sup>) occurred on Wednesday 05/20/2026 at approximately 07:42, 07:45, 09:25, and 13:34. Elevated readings were due to concrete demolition.
- Three (3) PM10 exceedances of Action Level 2 (PM10 > 150 µg/m<sup>3</sup>) occurred on Wednesday 05/20/2026 at approximately 12:46, 13:37, and 18:59. Elevated readings were due to concrete demolition. Contractor wetted the area to mitigate dust levels and fugitive dust. PM10 levels returned to below action levels by the subsequent monitoring interval.
- Two (2) PM10 exceedances of Action Level 2 (PM10 > 150 µg/m<sup>3</sup>) occurred on Wednesday 05/27/2026 at approximately 08:50 and 09:41. Elevated readings were attributable to construction activities within the project area. Contractor implemented dust control measures to mitigate fugitive dust. PM10 levels returned to below action levels by the subsequent monitoring interval.

## PM2.5

Time series plots of PM2.5 15-min average concentrations are shown in **Appendix A** for each monitoring location. The action level 1 (PM2.5 > 25 µg/m<sup>3</sup>) and action level 2 (PM2.5 > 35µg/m<sup>3</sup>) are shown as well.

- One (1) PM2.5 exceedance of Action Level 2 (PM2.5 > 35 µg/m<sup>3</sup>) occurred on Monday 05/18/2026 at approximately 09:40. Elevated readings were attributable to construction activities within the project area. Contractor wetted the area to mitigate dust levels and fugitive dust. PM2.5 levels returned to below action levels by the subsequent monitoring interval.
- Two (2) PM2.5 exceedances of Action Level 1 (PM2.5 > 15 µg/m<sup>3</sup>) occurred on Wednesday 05/27/2026 at approximately 08:10 and 10:06. Elevated readings were attributable to construction activities within the project area. Contractor implemented dust control measures to mitigate fugitive dust. PM2.5 levels returned to below action levels by the subsequent monitoring interval.
- Two (2) PM2.5 exceedances of Action Level 2 (PM2.5 > 35 µg/m<sup>3</sup>) occurred on Wednesday 05/27/2026 at approximately 08:36 and 09:40. Elevated readings were attributable to construction activities within the project area. Contractor implemented dust control measures to mitigate fugitive dust. PM2.5 levels returned to below action levels by the subsequent monitoring interval.
- One (1) PM2.5 exceedance of Action Level 1 (PM2.5 > 25 µg/m<sup>3</sup>) occurred on 05/30/2026 at approximately 15:06. Elevated readings were attributable to construction activities within the project area. Contractor implemented dust control measures to mitigate fugitive dust. PM2.5 levels returned to below action levels by the subsequent monitoring interval.

## VOCs

Time series plots of VOCs 15-min average concentrations are shown in **Appendix A** for each monitoring location. The action level (VOC Action Level 1: VOC > 5ppm) is shown as well.

- No VOC exceedances were recorded during this monitoring period.

## NOTES

- AM-01 disconnected from power on Friday 05/08/2026 at 05:00 to Monday 05/11/2026 at 13:00.
- AM-01 disconnected from power on Sunday 05/17/2026 at 07:00 to Monday 05/18/2026 at 07:00.
- AM-01 disconnected from power on Monday 05/25/2026 at 03:00 to Tuesday 05/26/2026 at 09:00.
- AM-02 disconnected from power on Friday 05/08/2026 at 13:00 to Monday 05/11/2026 at 13:00.
- AM-02 disconnected from power on Sunday 05/17/2026 at 13:00 to Monday 05/18/2026 at 07:00.
- AM-02 disconnected from power on Monday 05/25/2026 at 11:00 to Tuesday 05/26/2026 at 09:00.
- AM-03 disconnected from power on Friday 05/08/2026 at 13:00 to Monday 05/11/2026 at 12:00.
- AM-03 disconnected from power on Sunday 05/17/2026 at 14:00 to Monday 05/18/2026 at 07:00.
- AM-03 disconnected from power on Monday 05/25/2026 at 14:00 to Tuesday 05/26/2026 at 09:00.
- AM-04 disconnected from power on Tuesday 05/05/2026 at 07:00 to Wednesday 05/06/2026 at 07:00.
- AM-04 disconnected from power on Friday 05/22/2026 at 19:00 to Monday 05/25/2026 at 07:00.
- AM-04 disconnected from power on Monday 05/25/2026 at 09:00 to Tuesday 05/26/2026 at 08:00.
- AM-05 disconnected from power on Friday 05/08/2026 at 12:00 to Monday 05/11/2026 at 08:00.
- AM-05 disconnected from power on Monday 05/25/2026 at 10:00 to Tuesday 05/26/2026 at 08:00.
- AM-06 disconnected from power on Monday 05/25/2026 at 10:00 to Tuesday 05/26/2026 at 09:00.

Turner-SPC JV implemented mitigation when necessary to keep concentration levels below local and national air quality standards to ensure the ongoing health and safety of the adjacent community is not impacted.

**Appendix A**  
**Data Monitoring Summary**  
**May 1-31, 2026**




Reach 1\_EWP\_AQS Report

Battery Park_AQS	
Report Period	
From:	05/01/2026 00:00
To:	05/03/2026 23:59
PM10 Action Level:	100 µg/m³
PM2.5 Action Level:	25 µg/m³
VOC Action Level:	5 ppm


Daily Environmental Summary	Temp (°F)	Relative Humidity (%)	Barometer (inHg)	Wind Speed (mph)	Prevailing Wind Direction
05/01/2026	46.2 - 67.5	0.0 - 0.0	29.8 - 32.6	0.6 - 7.1	E
05/02/2026	51.1 - 61.7	0.0 - 0.0	29.8 - 33.3	0.4 - 6.3	ENE
05/03/2026	44.8 - 58.1	0.0 - 0.0	29.7 - 32.6	0.4 - 6.8	ENE

Daily Monitoring Summary	PM2.5 (µg/m³)	Time	PM10 (µg/m³)	Time	VOC (ppm)	Time
Min Contribution (15 min avg.) - 5/1/2026	0.0	00:15	0.0	00:15	0.0000	00:00
Max Contribution (15 min avg.) - 5/1/2026	3.0	04:45	25.3	16:15	0.2400	16:15
Daily Avg. Contribution (15 min avg.) - 5/1/2026	0.4	-	3.0	-	0.0564	-
Min Contribution (15 min avg.) - 5/2/2026	0.0	03:00	0.0	01:45	0.0000	00:30
Max Contribution (15 min avg.) - 5/2/2026	15.0	04:45	57.2	04:15	0.2093	00:00
Daily Avg. Contribution (15 min avg.) - 5/2/2026	0.8	-	2.8	-	0.0056	-
Min Contribution (15 min avg.) - 5/3/2026	0.0	04:00	0.0	04:00	0.0000	00:00
Max Contribution (15 min avg.) - 5/3/2026	1.9	19:00	13.0	16:00	0.0300	23:45
Daily Avg. Contribution (15 min avg.) - 5/3/2026	0.3	-	1.1	-	0.0006	-

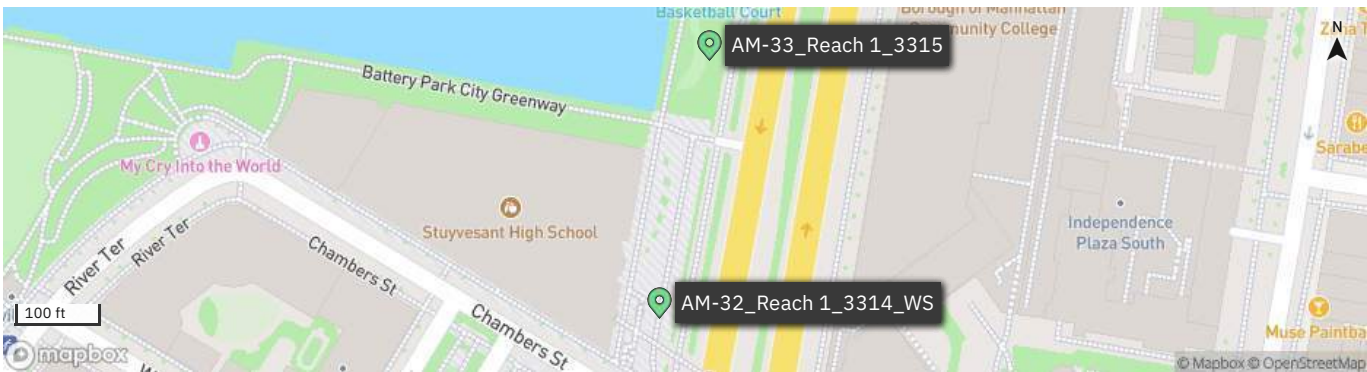

Stopped Initial Avg Rolling Avg


PM2.5 Average Contribution (µg/m³)

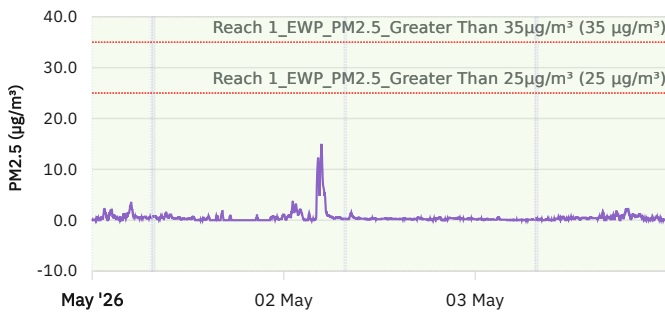

15 Min Rolling Avg PM2.5 Contribution

Stopped Initial Avg Rolling Avg


PM10 Average Contribution (µg/m³)

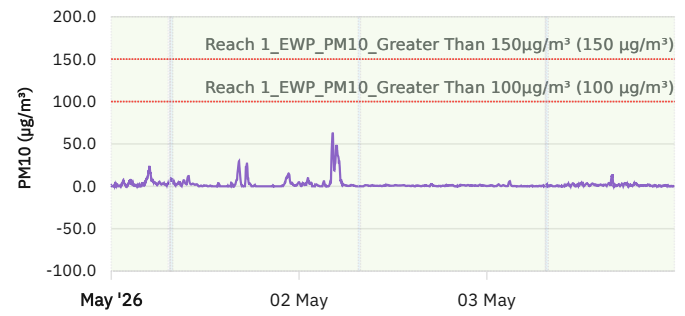


15 Min Rolling Avg PM10 Contribution

Stopped Initial Avg Rolling Avg


VOC Average Contribution (ppm)

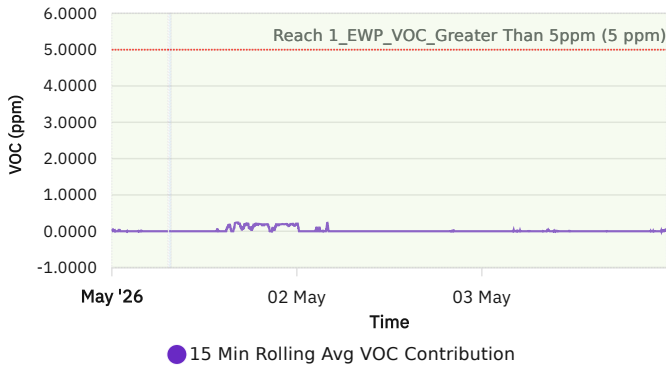


Wind rose (mph)

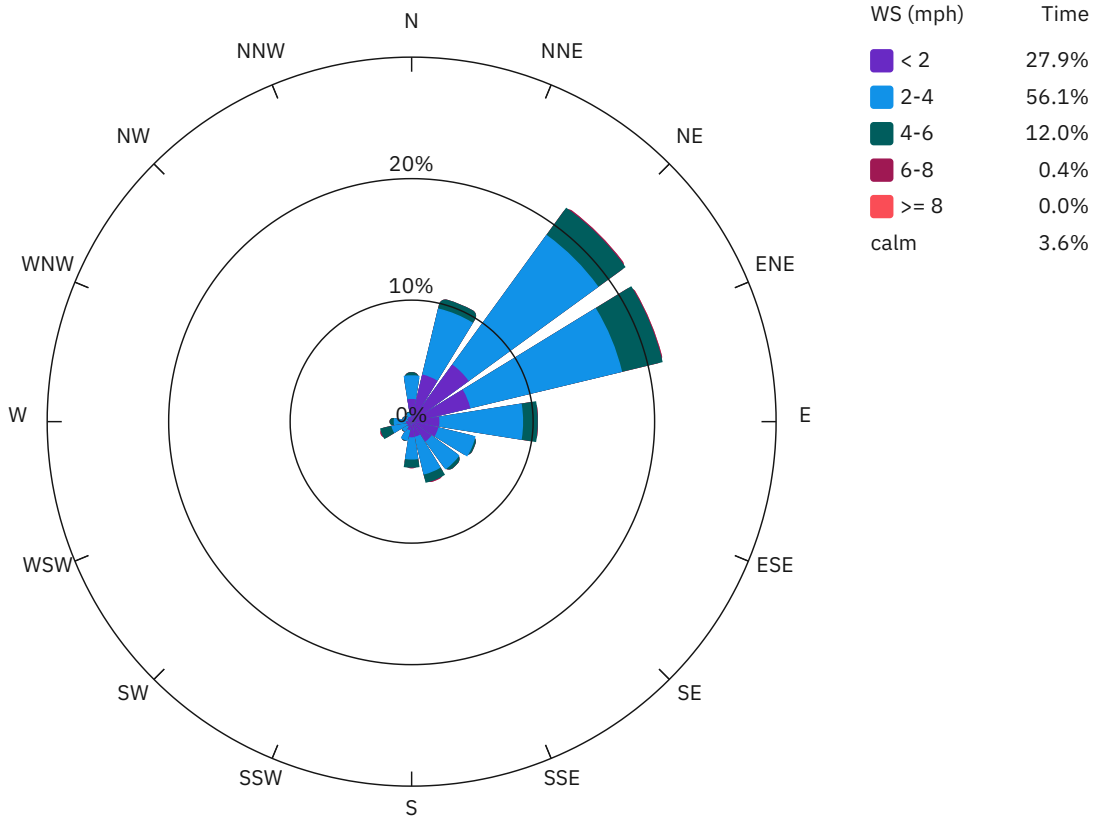

AM-32\_Reach 1\_3314\_WS

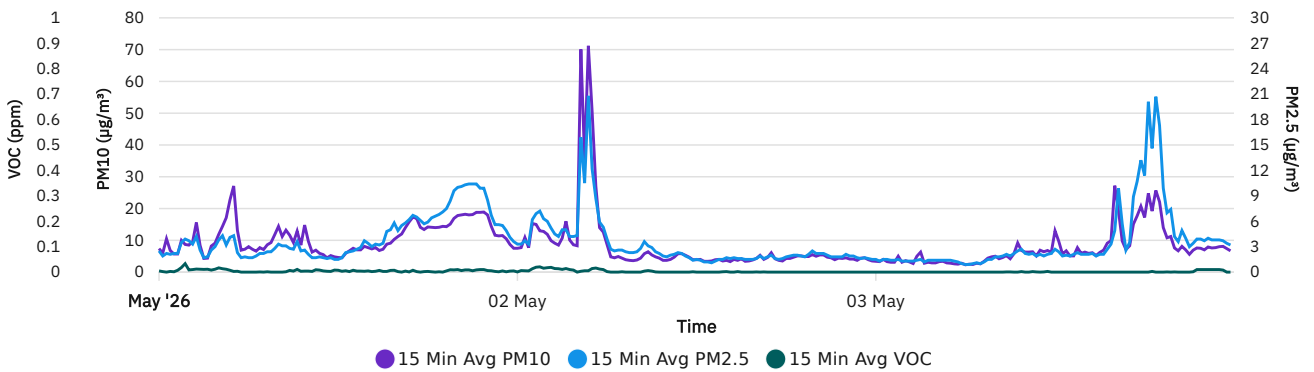

AM-33\_Reach 1\_3315

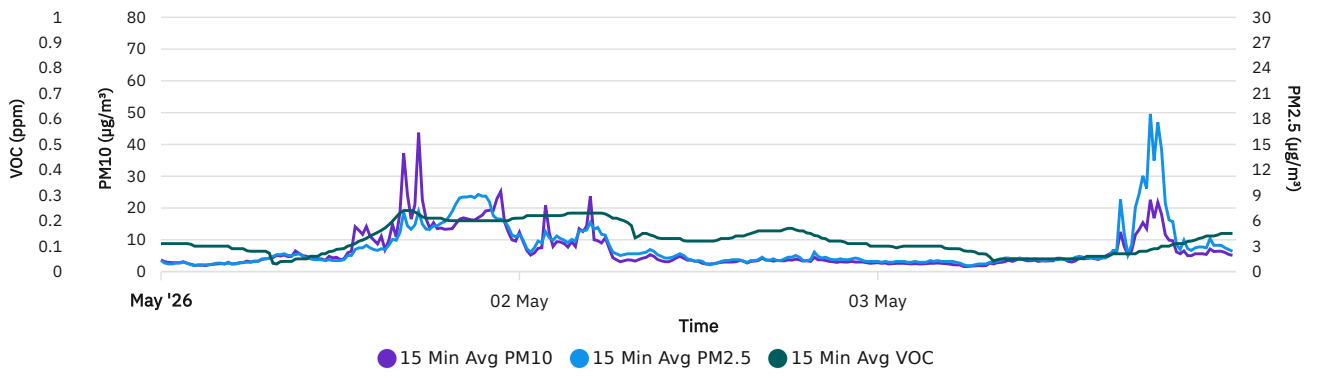




Reach 1\_EWP\_AQS Report

Battery Park_AQS	
Report Period	
From:	05/04/2026 00:00
To:	05/10/2026 23:59
PM10 Action Level:	100 µg/m³
PM2.5 Action Level:	25 µg/m³
VOC Action Level:	5 ppm

Daily Environmental Summary	Temp (°F)	Relative Humidity (%)	Barometer (inHg)	Wind Speed (mph)	Prevailing Wind Direction
05/04/2026	49.5 - 74.8	0.0 - 0.0	29.8 - 32.6	0.6 - 5.5	E
05/05/2026	59.2 - 82.9	0.0 - 0.0	29.6 - 32.5	0.7 - 6.5	SSE
05/06/2026	55.6 - 73.2	0.0 - 0.0	29.7 - 32.5	0.3 - 4.9	SE
05/07/2026	48.7 - 66.0	0.0 - 0.0	29.7 - 32.7	0.5 - 7.7	NE
05/08/2026	48.0 - 65.8	0.0 - 0.0	29.7 - 32.8	0.4 - 7.9	NE
05/09/2026	54.7 - 65.8	0.0 - 0.0	29.8 - 33.4	0.3 - 6.3	E
05/10/2026	52.7 - 72.9	0.0 - 0.0	29.7 - 35.1	0.3 - 6.0	NNE


Daily Monitoring Summary	PM2.5 (µg/m³)	Time	PM10 (µg/m³)	Time	VOC (ppm)	Time
Min Contribution (15 min avg.) - 5/4/2026	0.0	00:00	0.0	00:00	0.0000	01:00
Max Contribution (15 min avg.) - 5/4/2026	2.1	13:15	8.6	13:30	0.3653	19:00
Daily Avg. Contribution (15 min avg.) - 5/4/2026	0.3	-	0.6	-	0.0755	-
Min Contribution (15 min avg.) - 5/5/2026	0.0	00:00	0.0	00:00	0.0000	03:15
Max Contribution (15 min avg.) - 5/5/2026	5.3	04:45	81.2	20:45	0.8533	13:45
Daily Avg. Contribution (15 min avg.) - 5/5/2026	0.5	-	3.1	-	0.3124	-
Min Contribution (15 min avg.) - 5/6/2026	0.0	00:00	0.0	02:30	0.0000	10:15
Max Contribution (15 min avg.) - 5/6/2026	8.1	04:30	62.2	03:15	0.5460	00:00
Daily Avg. Contribution (15 min avg.) - 5/6/2026	1.2	-	4.3	-	0.1932	-
Min Contribution (15 min avg.) - 5/7/2026	0.0	04:00	0.0	02:45	0.0000	00:00
Max Contribution (15 min avg.) - 5/7/2026	6.9	03:30	14.7	16:30	0.0740	04:00
Daily Avg. Contribution (15 min avg.) - 5/7/2026	0.9	-	2.5	-	0.0017	-
Min Contribution (15 min avg.) - 5/8/2026	0.0	00:15	0.0	00:15	0.0000	00:00
Max Contribution (15 min avg.) - 5/8/2026	16.0	05:00	134.6	05:00	0.2680	00:15
Daily Avg. Contribution (15 min avg.) - 5/8/2026	2.0	-	10.5	-	0.0156	-
Min Contribution (15 min avg.) - 5/9/2026	0.0	00:00	0.0	00:00	0.0000	00:00
Max Contribution (15 min avg.) - 5/9/2026	29.5	04:45	311.7	04:45	0.3000	07:15
Daily Avg. Contribution (15 min avg.) - 5/9/2026	1.4	-	7.0	-	0.0948	-
Min Contribution (15 min avg.) - 5/10/2026	0.0	07:15	0.0	07:15	0.0000	00:00
Max Contribution (15 min avg.) - 5/10/2026	19.0	02:45	21.6	02:45	0.3547	22:00
Daily Avg. Contribution (15 min avg.) - 5/10/2026	6.7	-	7.2	-	0.0251	-

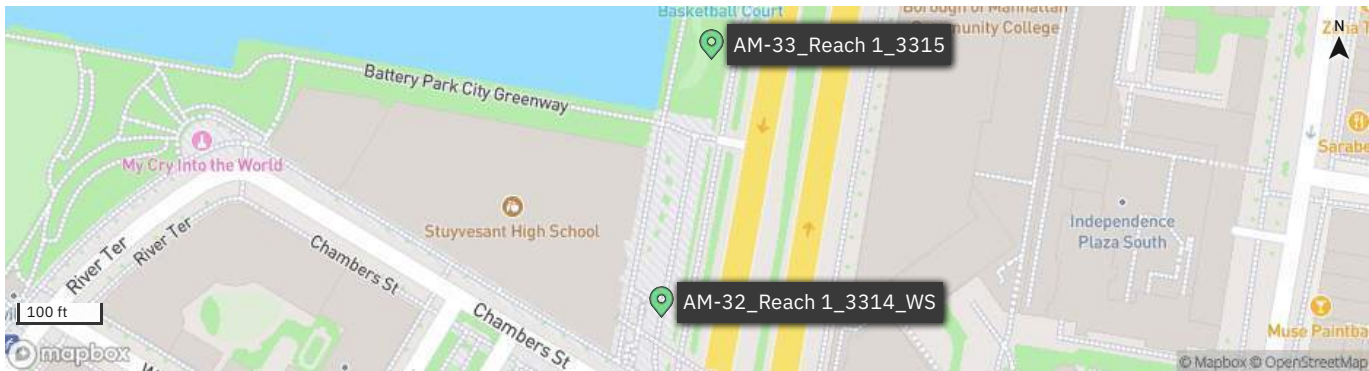


Stopped 
  Initial Avg 
  Rolling Avg

Stopped 
  Initial Avg 
  Rolling Avg

PM2.5 Average Contribution ( $\mu\text{g}/\text{m}^3$ )

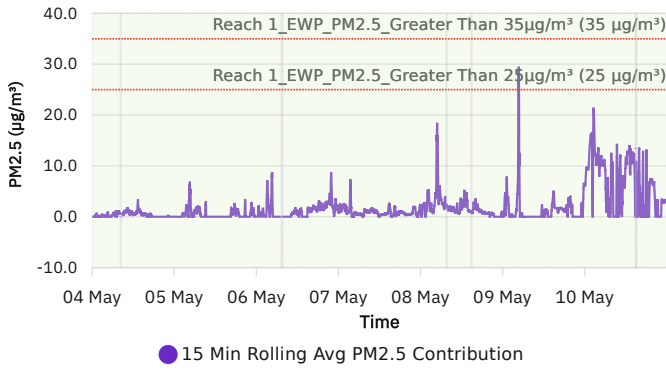


PM10 Average Contribution ( $\mu\text{g}/\text{m}^3$ )

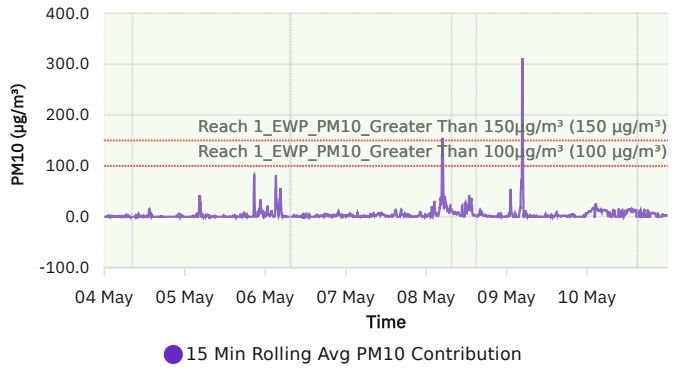


Stopped Initial Avg Rolling Avg


VOC Average Contribution (ppm)

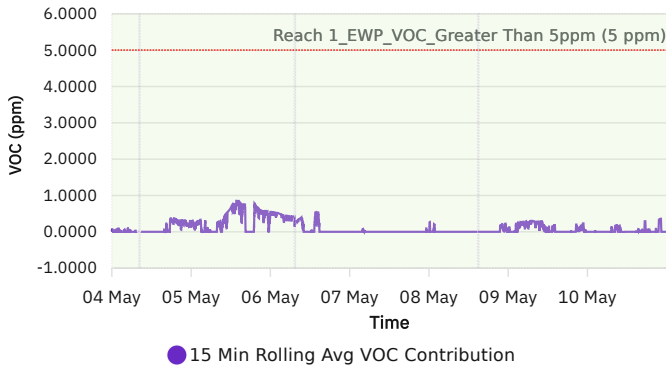


Wind rose (mph)

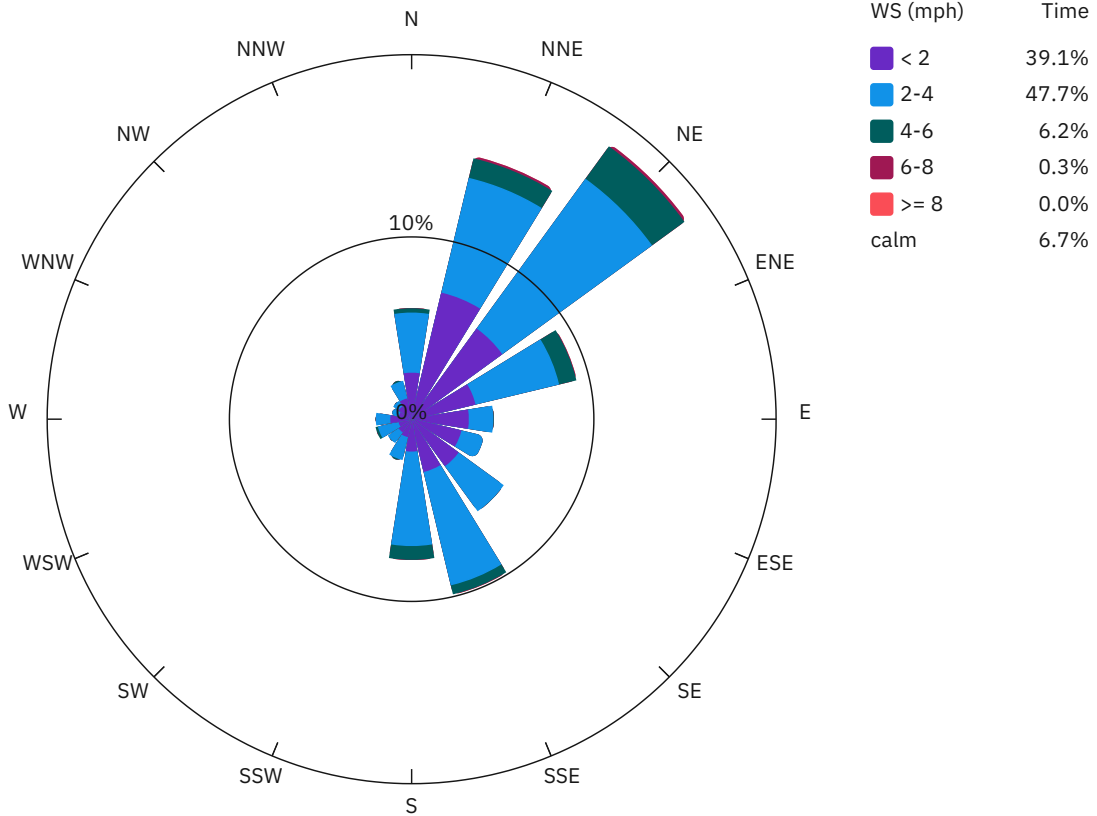

AM-32\_Reach 1\_3314\_WS

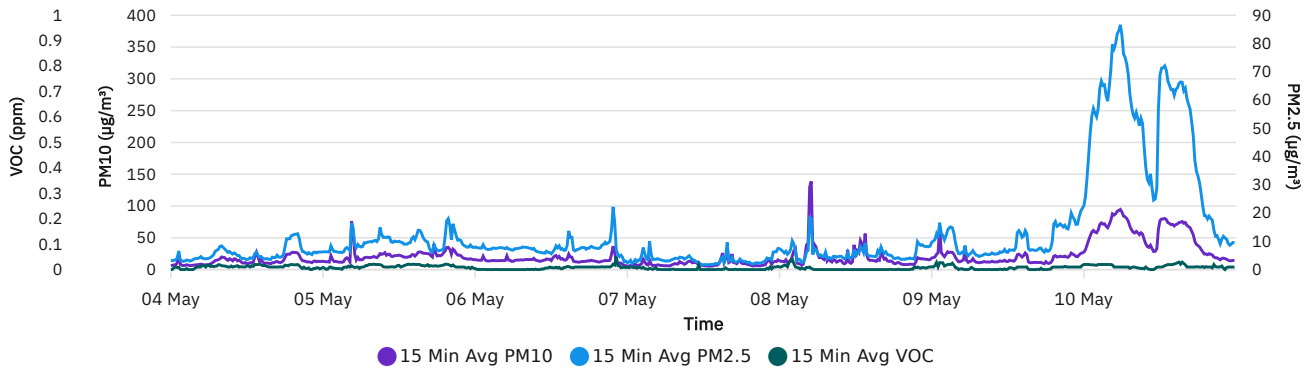

AM-33\_Reach 1\_3315

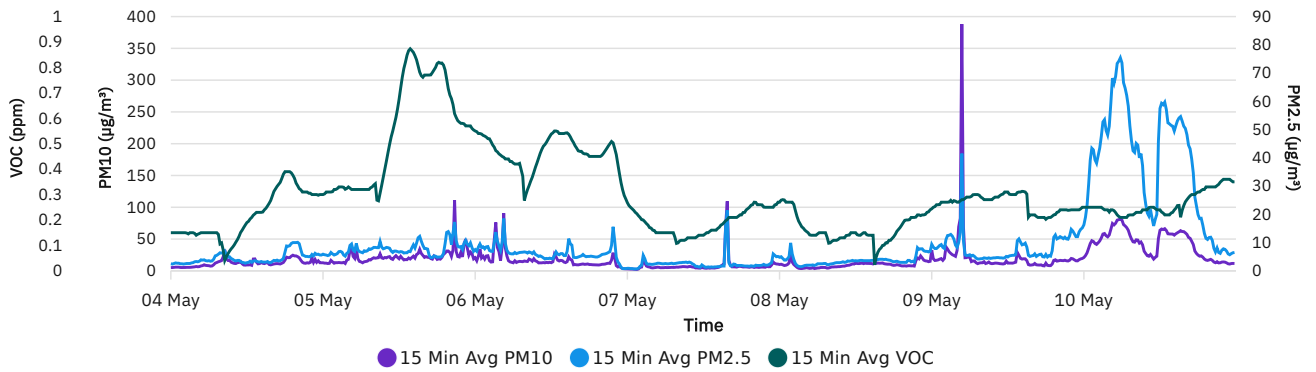

Exceedance Summary

Parameter	Action Level	Time Triggered	Cause	Mitigation
PM10	100.0 µg/m³	5/8/2026 04:41	Elevated readings were attributable to construction activities within the project area.	Contractor deemed mitigation methods were not warranted.
PM10	100.0 µg/m³	5/9/2026 04:33	Elevated readings were attributable to construction activities within the project area.	Contractor deemed mitigation methods were not warranted.
PM2.5	25.0 µg/m³	5/9/2026 04:36	Elevated readings were attributable to construction activities within the project area.	Contractor deemed mitigation methods were not warranted.
PM2.5	35.0 µg/m³	5/9/2026 04:39	Elevated readings were attributable to construction activities within the project area.	Contractor deemed mitigation methods were not warranted.




Reach 1\_EWP\_AQS Report

Battery Park_AQS	
Report Period	
From:	05/11/2026 00:00
To:	05/17/2026 23:59
PM10 Action Level:	100 µg/m³
PM2.5 Action Level:	25 µg/m³
VOC Action Level:	5 ppm

Daily Environmental Summary	Temp (°F)	Relative Humidity (%)	Barometer (inHg)	Wind Speed (mph)	Prevailing Wind Direction
05/11/2026	53.1 - 63.7	0.0 - 0.0	29.8 - 35.3	0.5 - 11.6	NE
05/12/2026	46.2 - 68.5	0.0 - 0.0	30.0 - 34.0	0.8 - 9.3	ENE
05/13/2026	53.4 - 75.9	0.0 - 0.0	29.8 - 33.2	0.5 - 6.5	S
05/14/2026	54.0 - 68.2	0.0 - 0.0	29.5 - 35.7	0.4 - 5.5	NE
05/15/2026	51.3 - 65.7	0.0 - 0.0	29.6 - 35.5	0.5 - 5.6	NE
05/16/2026	54.1 - 81.7	0.0 - 0.0	29.9 - 35.2	0.3 - 5.3	ENE
05/17/2026	66.6 - 91.4	0.0 - 0.0	29.8 - 32.7	0.3 - 5.3	NNE


Daily Monitoring Summary	PM2.5 (µg/m³)	Time	PM10 (µg/m³)	Time	VOC (ppm)	Time
Min Contribution (15 min avg.) - 5/11/2026	0.0	07:15	0.0	07:15	0.0000	00:00
Max Contribution (15 min avg.) - 5/11/2026	3.4	00:45	6.9	01:45	0.3567	20:15
Daily Avg. Contribution (15 min avg.) - 5/11/2026	0.4	-	0.7	-	0.0270	-
Min Contribution (15 min avg.) - 5/12/2026	0.0	15:15	0.0	02:30	0.0000	00:00
Max Contribution (15 min avg.) - 5/12/2026	8.3	04:45	63.5	04:45	0.2633	18:30
Daily Avg. Contribution (15 min avg.) - 5/12/2026	1.1	-	6.8	-	0.0726	-
Min Contribution (15 min avg.) - 5/13/2026	0.0	00:45	0.0	00:45	0.0000	00:15
Max Contribution (15 min avg.) - 5/13/2026	21.4	05:00	249.6	05:00	0.4933	15:45
Daily Avg. Contribution (15 min avg.) - 5/13/2026	0.8	-	8.4	-	0.2362	-
Min Contribution (15 min avg.) - 5/14/2026	0.0	00:00	0.0	00:00	0.0000	02:30
Max Contribution (15 min avg.) - 5/14/2026	5.1	02:00	40.9	02:00	0.2773	00:30
Daily Avg. Contribution (15 min avg.) - 5/14/2026	0.9	-	2.7	-	0.0221	-
Min Contribution (15 min avg.) - 5/15/2026	0.0	20:45	0.0	19:00	0.0000	00:00
Max Contribution (15 min avg.) - 5/15/2026	24.6	05:00	158.1	05:00	0.0000	00:00
Daily Avg. Contribution (15 min avg.) - 5/15/2026	1.8	-	8.7	-	0.0000	-
Min Contribution (15 min avg.) - 5/16/2026	0.0	13:00	0.0	13:00	0.0000	00:00
Max Contribution (15 min avg.) - 5/16/2026	32.5	03:45	178.7	05:00	0.6387	22:00
Daily Avg. Contribution (15 min avg.) - 5/16/2026	2.3	-	9.1	-	0.1220	-
Min Contribution (15 min avg.) - 5/17/2026	0.0	13:00	0.0	10:00	0.0000	00:00
Max Contribution (15 min avg.) - 5/17/2026	5.0	18:45	11.8	15:30	0.8573	16:00
Daily Avg. Contribution (15 min avg.) - 5/17/2026	1.3	-	1.1	-	0.0981	-

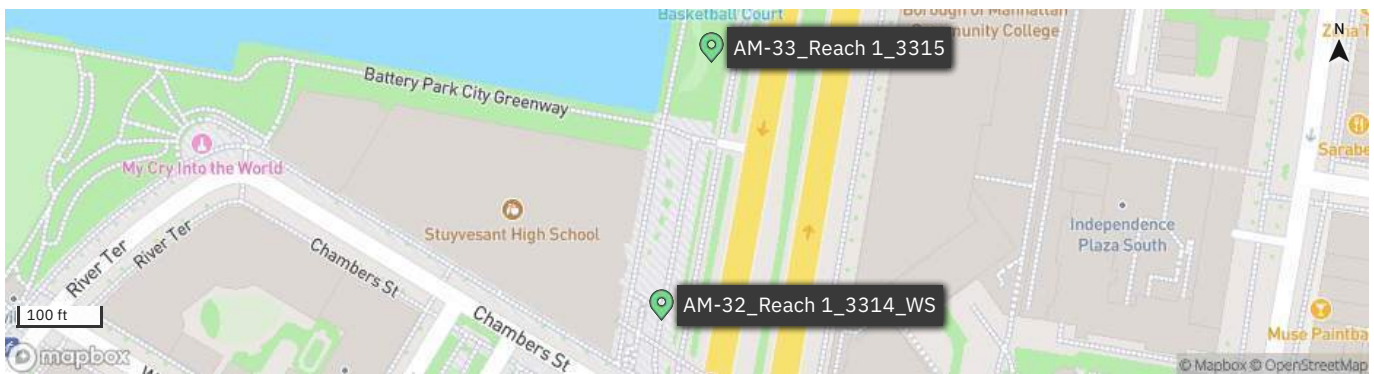


Stopped 
  Initial Avg 
  Rolling Avg

Stopped 
  Initial Avg 
  Rolling Avg

PM2.5 Average Contribution ( $\mu\text{g}/\text{m}^3$ )

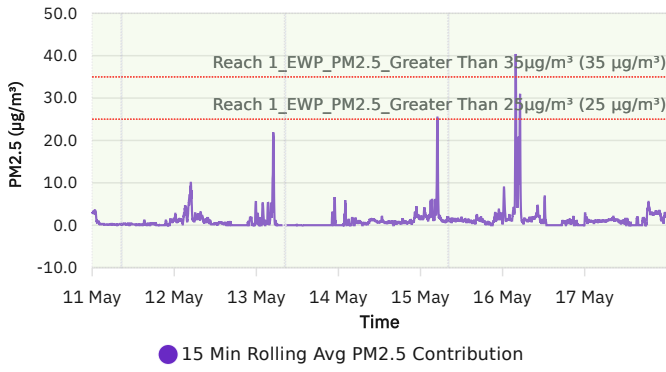


PM10 Average Contribution ( $\mu\text{g}/\text{m}^3$ )

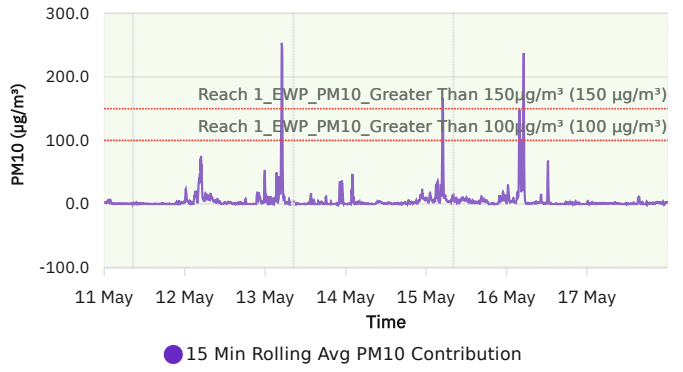


Stopped Initial Avg Rolling Avg


VOC Average Contribution (ppm)

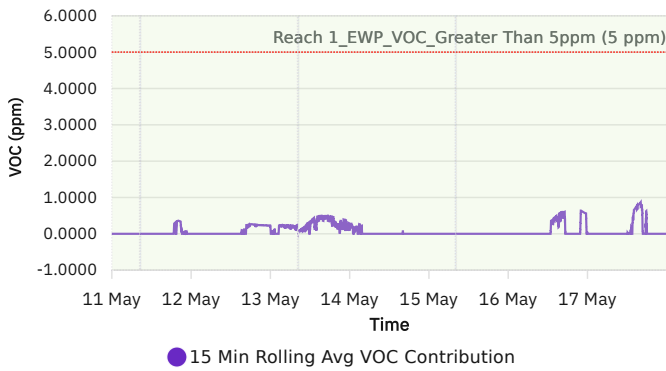


Wind rose (mph)

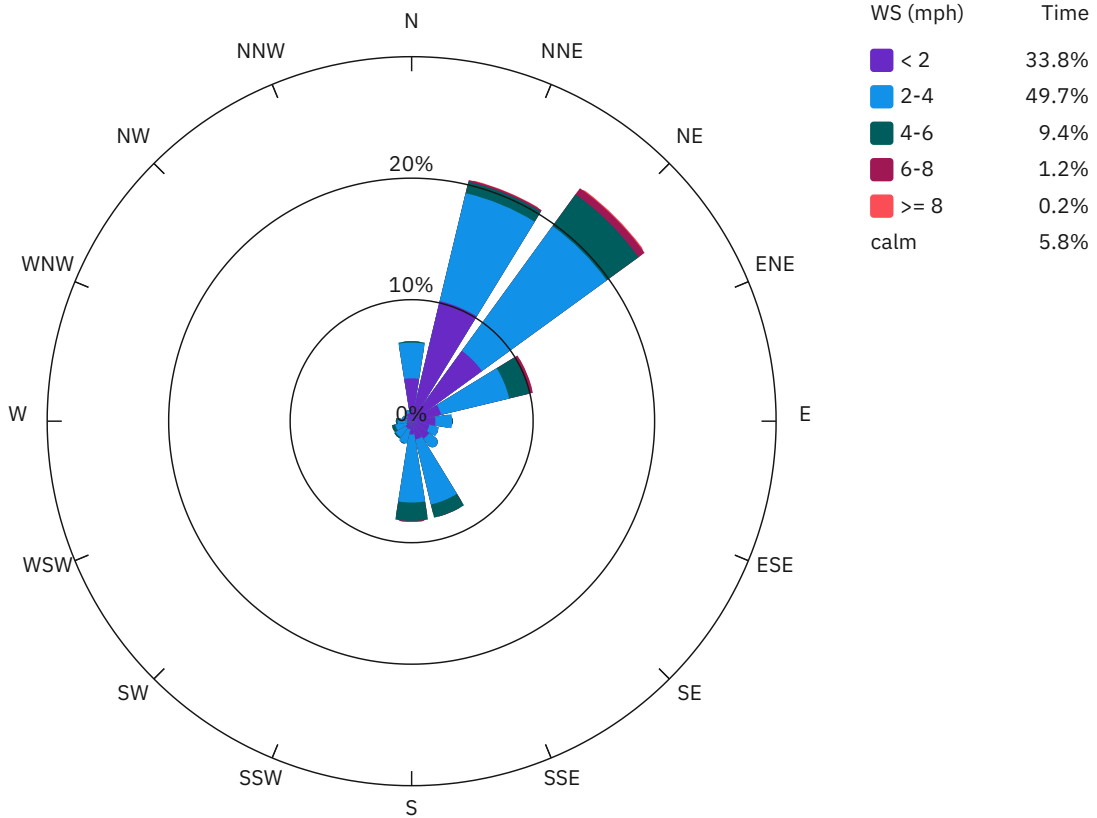

AM-32\_Reach 1\_3314\_WS

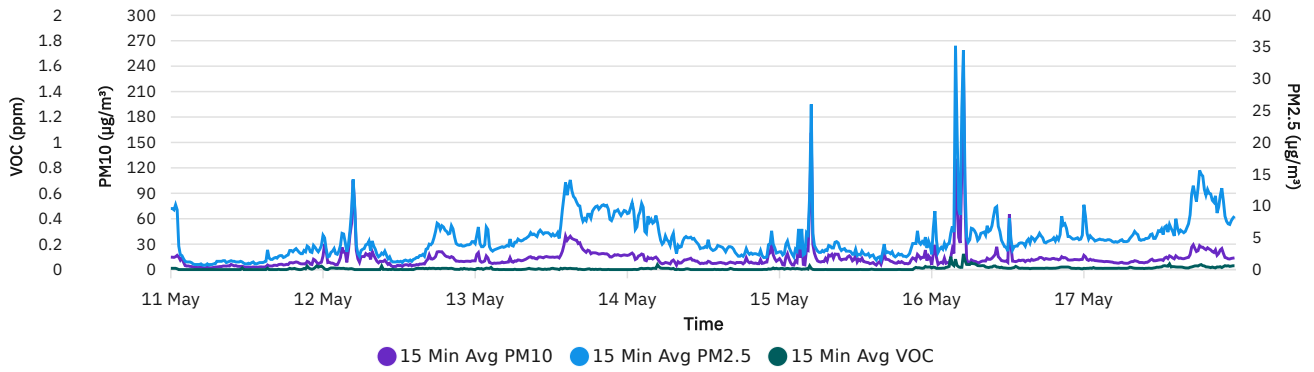

AM-33\_Reach 1\_3315

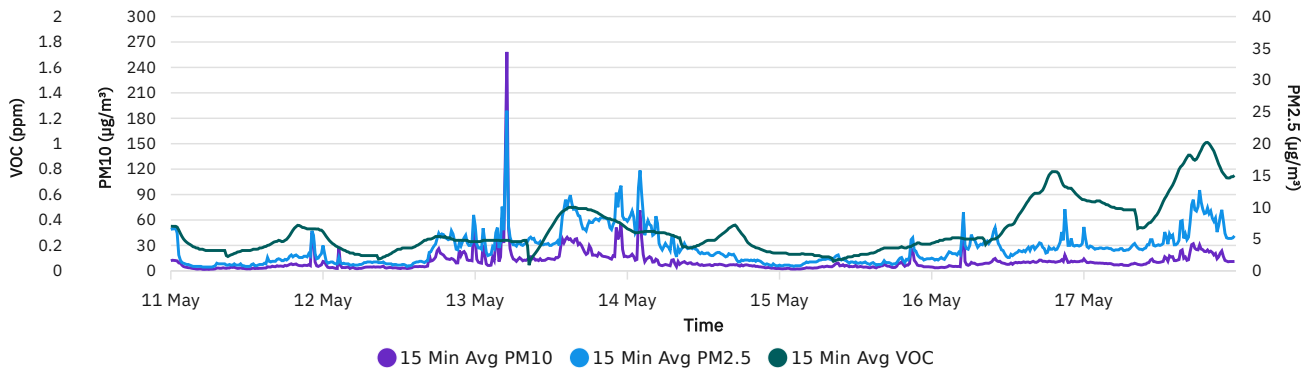

Exceedance Summary

Parameter	Action Level	Time Triggered	Cause	Mitigation
PM10	100.0 µg/m³	5/13/2026 04:44	Elevated readings were attributable to construction activities within the project area.	Contractor deemed mitigation methods were not warranted.
PM10	150.0 µg/m³	5/15/2026 04:48	Elevated readings were attributable to construction activities within the project area.	Contractor deemed mitigation methods were not warranted.
PM10	100.0 µg/m³	5/16/2026 03:43	Elevated readings were attributable to construction activities within the project area.	Contractor deemed mitigation methods were not warranted.
PM10	100.0 µg/m³	5/16/2026 04:42	Elevated readings were attributable to construction activities within the project area.	Contractor deemed mitigation methods were not warranted.
PM10	100.0 µg/m³	5/16/2026 04:56	Elevated readings were attributable to construction activities within the project area.	Contractor deemed mitigation methods were not warranted.
PM2.5	25.0 µg/m³	5/15/2026 04:55	Elevated readings were attributable to construction activities within the project area.	Contractor deemed mitigation methods were not warranted.
PM2.5	25.0 µg/m³	5/16/2026 03:43	Elevated readings were attributable to construction activities within the project area.	Contractor deemed mitigation methods were not warranted.
PM2.5	25.0 µg/m³	5/16/2026 05:00	Elevated readings were attributable to construction activities within the project area.	Contractor deemed mitigation methods were not warranted.




Reach 1\_EWP\_AQS Report

Battery Park_AQS	
Report Period	
From:	05/18/2026 00:00
To:	05/24/2026 23:59
PM10 Action Level:	100 µg/m³
PM2.5 Action Level:	25 µg/m³
VOC Action Level:	5 ppm

Daily Environmental Summary	Temp (°F)	Relative Humidity (%)	Barometer (inHg)	Wind Speed (mph)	Prevailing Wind Direction
05/18/2026	65.8 - 90.3	0.0 - 0.0	29.8 - 32.7	0.3 - 7.0	WNW
05/19/2026	73.2 - 97.7	0.0 - 0.0	29.9 - 33.0	0.3 - 4.9	N
05/20/2026	67.6 - 95.0	0.0 - 0.0	29.7 - 32.9	0.4 - 5.8	NNE
05/21/2026	54.0 - 67.8	0.0 - 0.0	29.8 - 33.7	0.6 - 7.6	NE
05/22/2026	55.9 - 69.8	0.0 - 0.0	30.2 - 33.1	0.7 - 12.1	WNW
05/23/2026	48.2 - 58.5	0.0 - 0.0	30.2 - 33.6	0.8 - 9.2	WNW
05/24/2026	48.7 - 55.0	0.0 - 0.0	30.2 - 33.8	0.7 - 8.3	WNW


Daily Monitoring Summary	PM2.5 (µg/m³)	Time	PM10 (µg/m³)	Time	VOC (ppm)	Time
Min Contribution (15 min avg.) - 5/18/2026	0.0	10:00	0.0	10:00	0.0000	00:00
Max Contribution (15 min avg.) - 5/18/2026	12.3	12:45	42.9	22:15	0.7873	19:45
Daily Avg. Contribution (15 min avg.) - 5/18/2026	3.3	-	5.6	-	0.2109	-
Min Contribution (15 min avg.) - 5/19/2026	0.0	07:45	0.0	07:45	0.0000	07:45
Max Contribution (15 min avg.) - 5/19/2026	10.9	10:45	37.7	19:00	1.3040	15:15
Daily Avg. Contribution (15 min avg.) - 5/19/2026	2.8	-	5.5	-	0.1161	-
Min Contribution (15 min avg.) - 5/20/2026	0.0	05:15	0.0	05:15	0.0000	00:00
Max Contribution (15 min avg.) - 5/20/2026	12.1	18:30	99.9	18:30	0.0653	05:15
Daily Avg. Contribution (15 min avg.) - 5/20/2026	2.9	-	8.7	-	0.0011	-
Min Contribution (15 min avg.) - 5/21/2026	0.0	22:15	0.0	12:45	0.0000	00:00
Max Contribution (15 min avg.) - 5/21/2026	6.6	00:15	39.4	05:15	0.0000	00:00
Daily Avg. Contribution (15 min avg.) - 5/21/2026	1.1	-	4.2	-	0.0000	-
Min Contribution (15 min avg.) - 5/22/2026	0.0	00:45	0.0	00:00	0.0000	00:00
Max Contribution (15 min avg.) - 5/22/2026	2.2	23:30	23.3	23:30	0.3600	17:45
Daily Avg. Contribution (15 min avg.) - 5/22/2026	0.1	-	0.7	-	0.0684	-
Min Contribution (15 min avg.) - 5/23/2026	0.0	00:15	0.0	01:15	0.0000	00:00
Max Contribution (15 min avg.) - 5/23/2026	0.7	21:45	2.4	00:15	0.2427	01:00
Daily Avg. Contribution (15 min avg.) - 5/23/2026	0.1	-	0.2	-	0.0484	-
Min Contribution (15 min avg.) - 5/24/2026	0.0	00:00	0.0	00:00	0.0000	00:30
Max Contribution (15 min avg.) - 5/24/2026	0.8	22:30	0.9	18:45	0.1073	09:30
Daily Avg. Contribution (15 min avg.) - 5/24/2026	0.1	-	0.1	-	0.0209	-

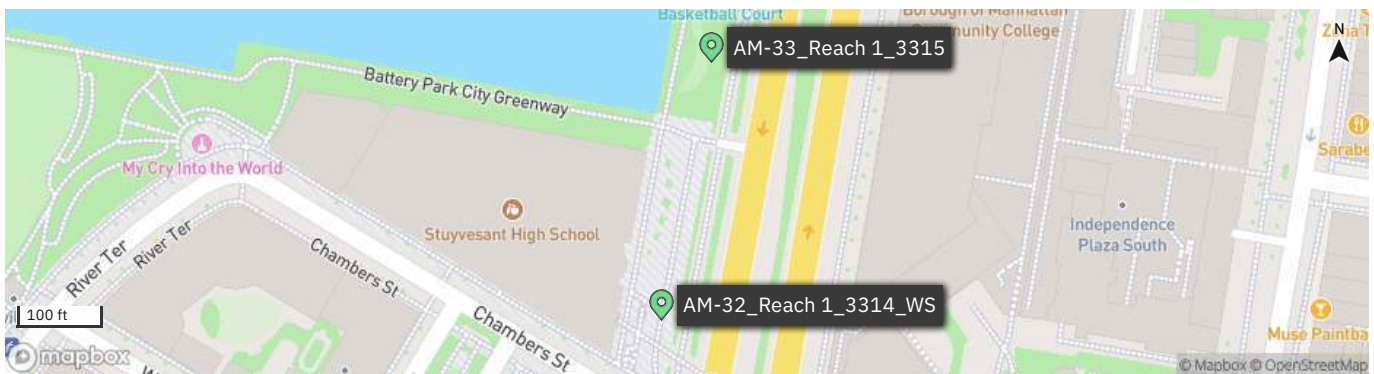


Stopped 
  Initial Avg 
  Rolling Avg

Stopped 
  Initial Avg 
  Rolling Avg

PM2.5 Average Contribution ( $\mu\text{g}/\text{m}^3$ )

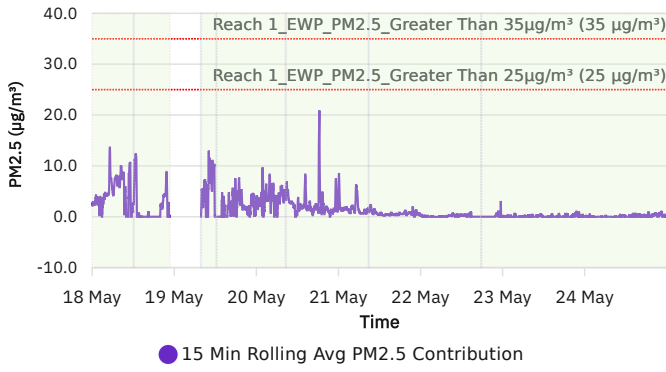


PM10 Average Contribution ( $\mu\text{g}/\text{m}^3$ )

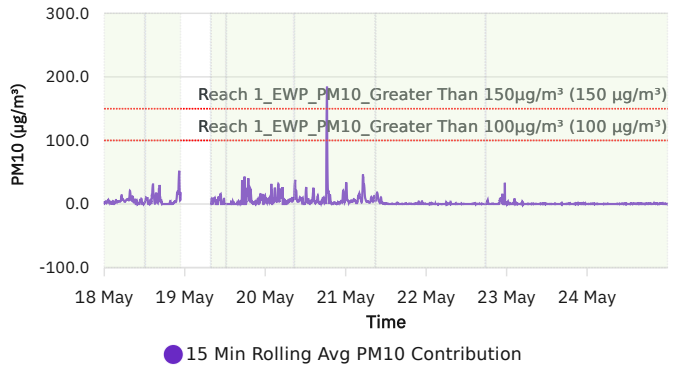


Stopped Initial Avg Rolling Avg


VOC Average Contribution (ppm)

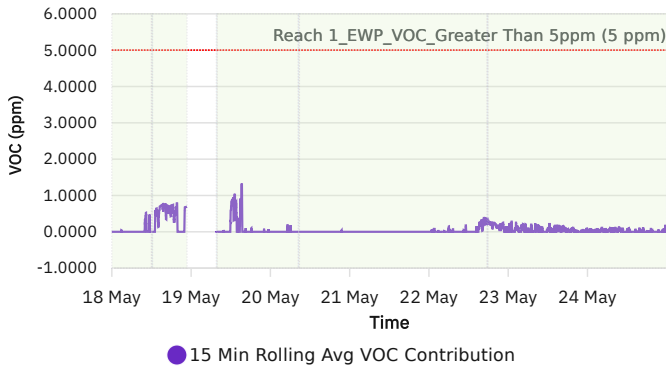


Wind rose (mph)

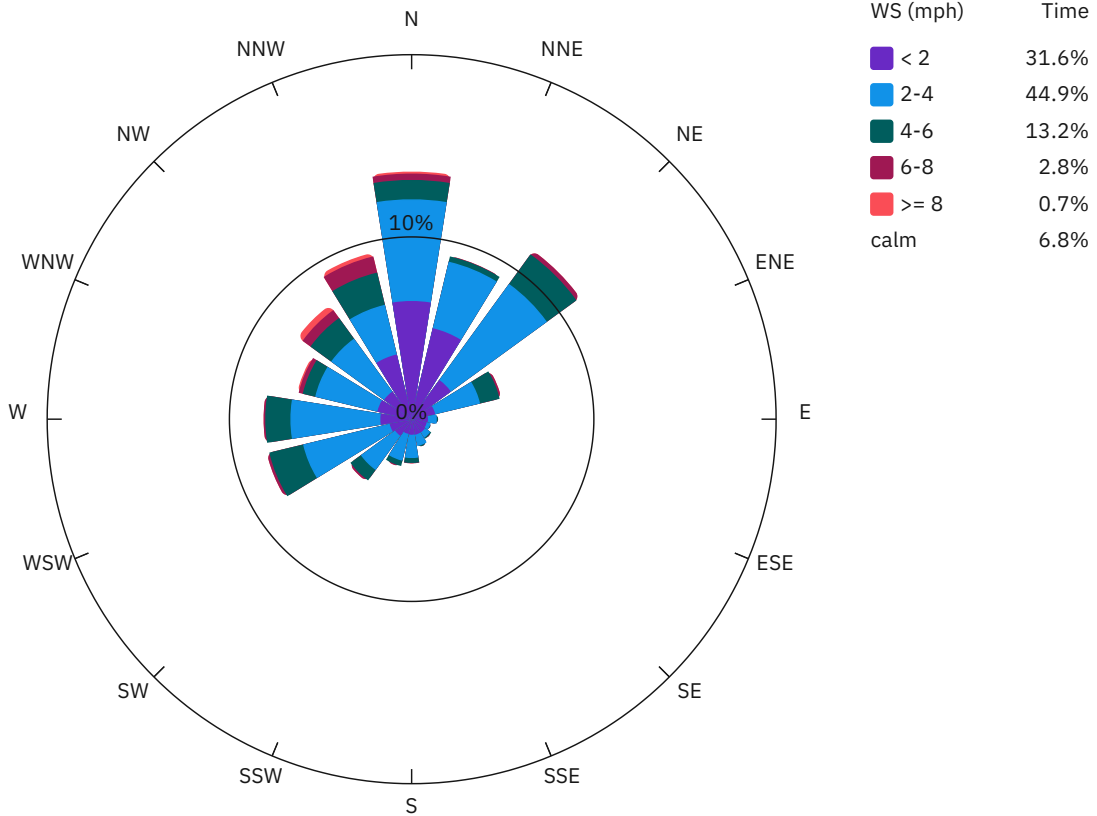

AM-32\_Reach 1\_3314\_WS

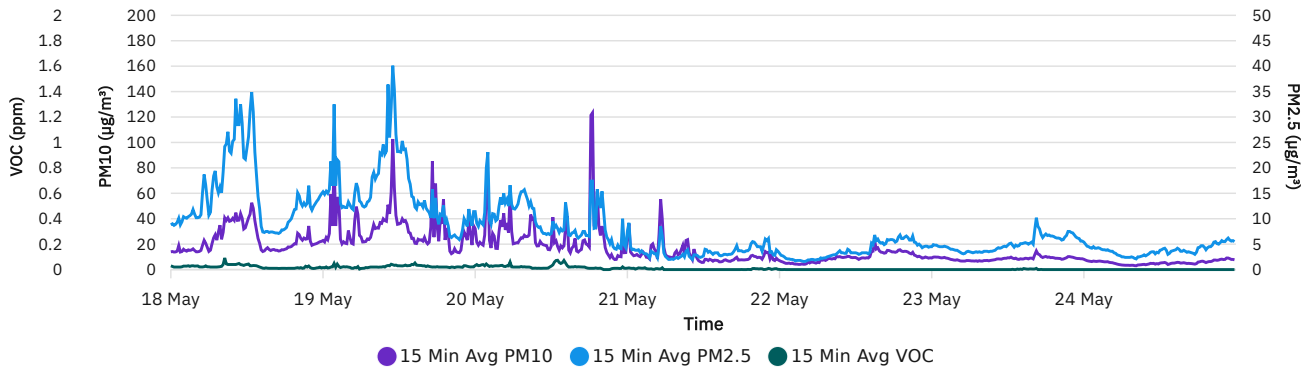

AM-33\_Reach 1\_3315

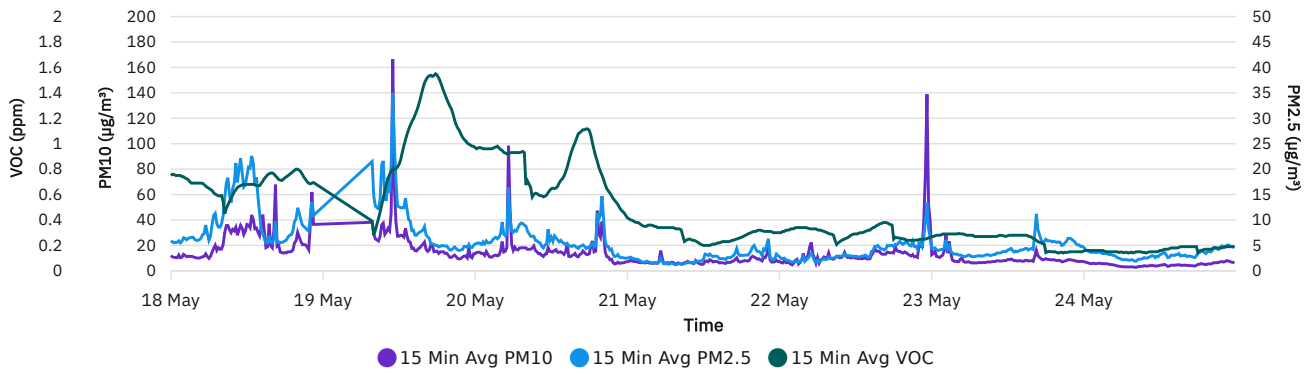

Exceedance Summary

Parameter	Action Level	Time Triggered	Cause	Mitigation
PM10	150.0 µg/m³	5/20/2026 18:16	Elevated readings were attributable to wind-blown dust across the site.	Contractor wetted the area to mitigate dust levels and fugitive dust.




Reach 1\_EWP\_AQS Report

Battery Park_AQS	
Report Period	
From:	05/25/2026 00:00
To:	05/31/2026 23:59
PM10 Action Level:	100 µg/m³
PM2.5 Action Level:	25 µg/m³
VOC Action Level:	5 ppm

Daily Environmental Summary	Temp (°F)	Relative Humidity (%)	Barometer (inHg)	Wind Speed (mph)	Prevailing Wind Direction
05/25/2026	54.5 - 72.9	0.0 - 0.0	29.8 - 33.8	0.3 - 6.1	ENE
05/26/2026	61.2 - 84.4	0.0 - 0.0	30.0 - 33.5	0.5 - 4.8	ESE
05/27/2026	67.8 - 80.8	0.0 - 0.0	29.7 - 34.2	0.4 - 3.9	NE
05/28/2026	62.4 - 78.1	0.0 - 0.0	29.6 - 32.7	1.0 - 8.3	ENE
05/29/2026	58.1 - 80.2	0.0 - 0.0	29.7 - 32.6	0.4 - 6.9	NE
05/30/2026	53.8 - 70.7	0.0 - 0.0	29.4 - 32.7	0.3 - 12.4	ENE
05/31/2026	51.4 - 78.8	0.0 - 0.0	29.9 - 33.3	0.3 - 5.2	NNE


Daily Monitoring Summary	PM2.5 (µg/m³)	Time	PM10 (µg/m³)	Time	VOC (ppm)	Time
Min Contribution (15 min avg.) - 5/25/2026	0.0	00:00	0.0	00:00	0.0000	00:30
Max Contribution (15 min avg.) - 5/25/2026	12.7	07:45	12.9	07:00	0.4700	19:00
Daily Avg. Contribution (15 min avg.) - 5/25/2026	2.0	-	2.1	-	0.0900	-
Min Contribution (15 min avg.) - 5/26/2026	0.0	13:00	0.0	12:45	0.0000	08:15
Max Contribution (15 min avg.) - 5/26/2026	3.3	08:15	5.3	10:30	0.7020	18:15
Daily Avg. Contribution (15 min avg.) - 5/26/2026	0.4	-	0.8	-	0.3057	-
Min Contribution (15 min avg.) - 5/27/2026	0.0	03:00	0.0	03:00	0.0000	00:00
Max Contribution (15 min avg.) - 5/27/2026	6.6	08:45	32.0	22:30	0.4593	06:00
Daily Avg. Contribution (15 min avg.) - 5/27/2026	1.8	-	4.0	-	0.0318	-
Min Contribution (15 min avg.) - 5/28/2026	0.0	00:30	0.0	05:00	0.0000	00:00
Max Contribution (15 min avg.) - 5/28/2026	31.0	23:30	96.0	23:30	0.1120	15:45
Daily Avg. Contribution (15 min avg.) - 5/28/2026	2.2	-	8.8	-	0.0023	-
Min Contribution (15 min avg.) - 5/29/2026	0.0	21:45	0.0	18:30	0.0000	00:00
Max Contribution (15 min avg.) - 5/29/2026	36.2	01:15	133.0	01:15	0.0000	00:00
Daily Avg. Contribution (15 min avg.) - 5/29/2026	4.8	-	22.0	-	0.0000	-
Min Contribution (15 min avg.) - 5/30/2026	0.0	03:00	0.0	03:00	0.0000	00:00
Max Contribution (15 min avg.) - 5/30/2026	26.3	12:00	227.7	12:00	0.2600	22:00
Daily Avg. Contribution (15 min avg.) - 5/30/2026	2.1	-	15.2	-	0.0112	-
Min Contribution (15 min avg.) - 5/31/2026	0.0	05:45	0.0	00:00	0.0000	00:00
Max Contribution (15 min avg.) - 5/31/2026	7.4	22:30	6.8	22:30	0.1333	12:30
Daily Avg. Contribution (15 min avg.) - 5/31/2026	0.8	-	0.6	-	0.0019	-

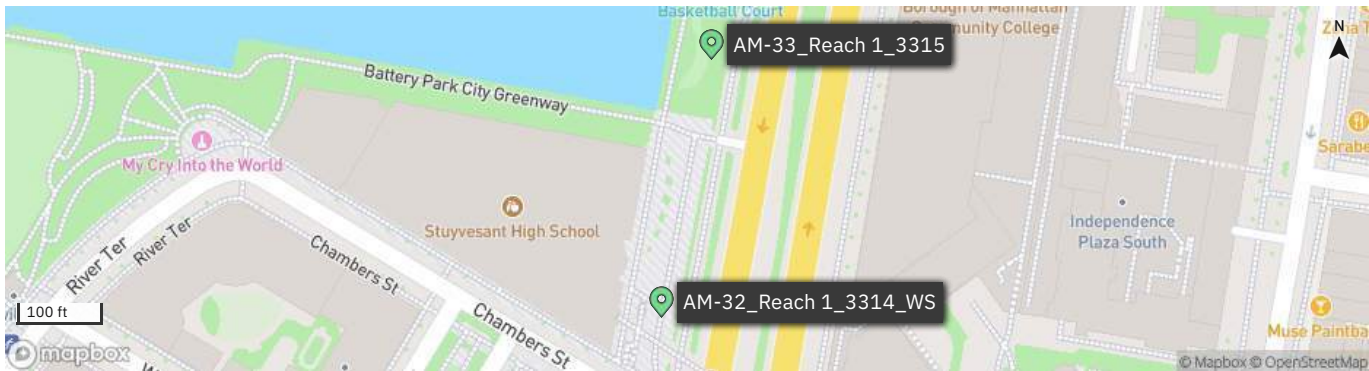


Stopped 
  Initial Avg 
  Rolling Avg

Stopped 
  Initial Avg 
  Rolling Avg

PM2.5 Average Contribution ( $\mu\text{g}/\text{m}^3$ )

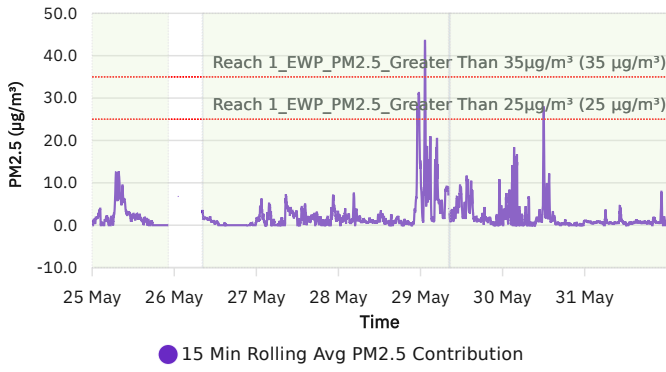


PM10 Average Contribution ( $\mu\text{g}/\text{m}^3$ )

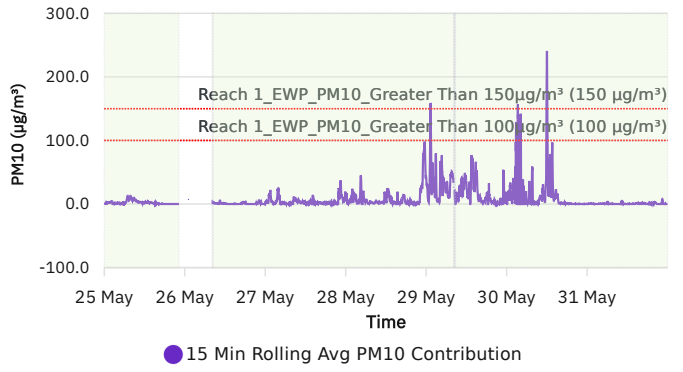


Stopped Initial Avg Rolling Avg


VOC Average Contribution (ppm)

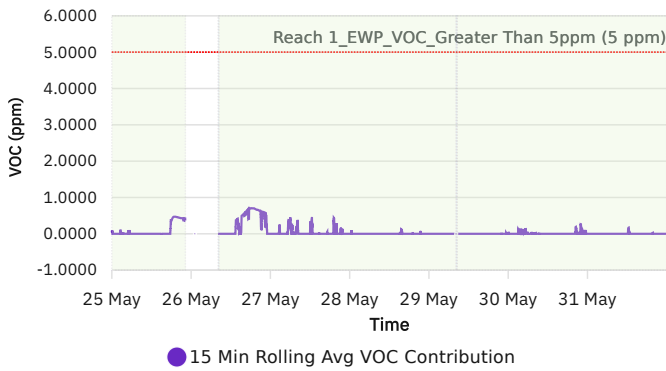


Wind rose (mph)

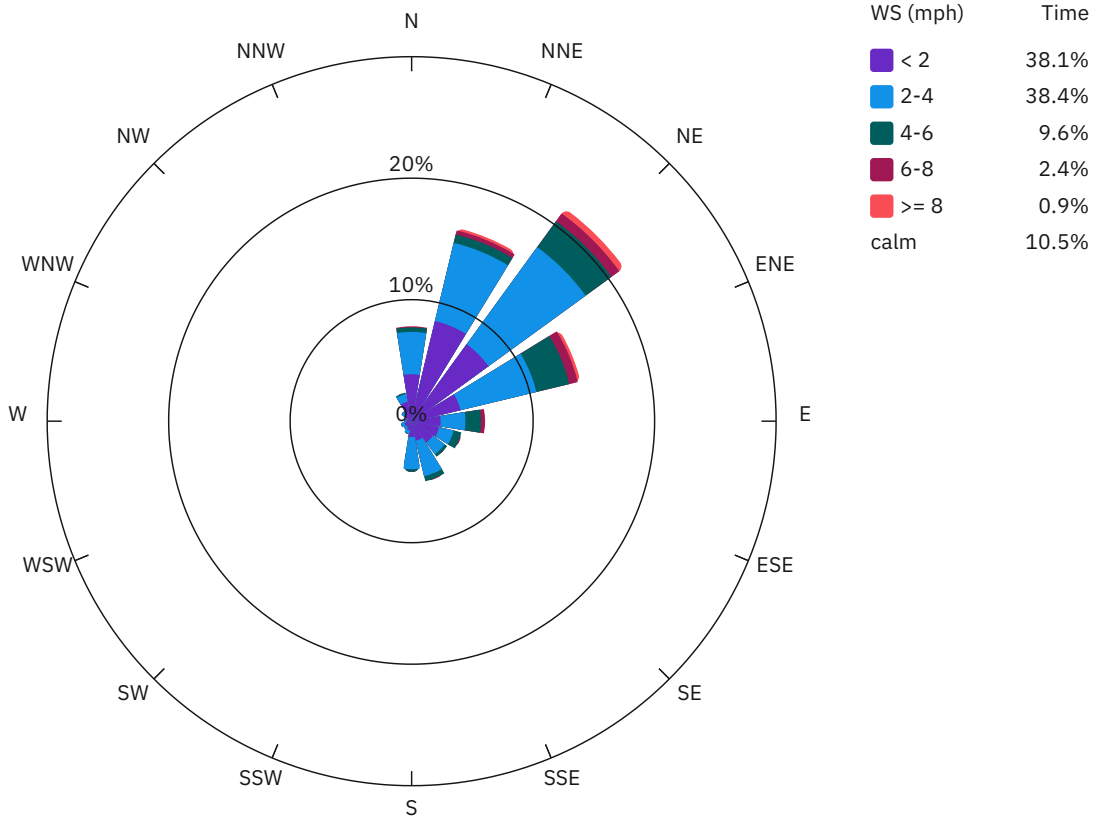

AM-32\_Reach 1\_3314\_WS

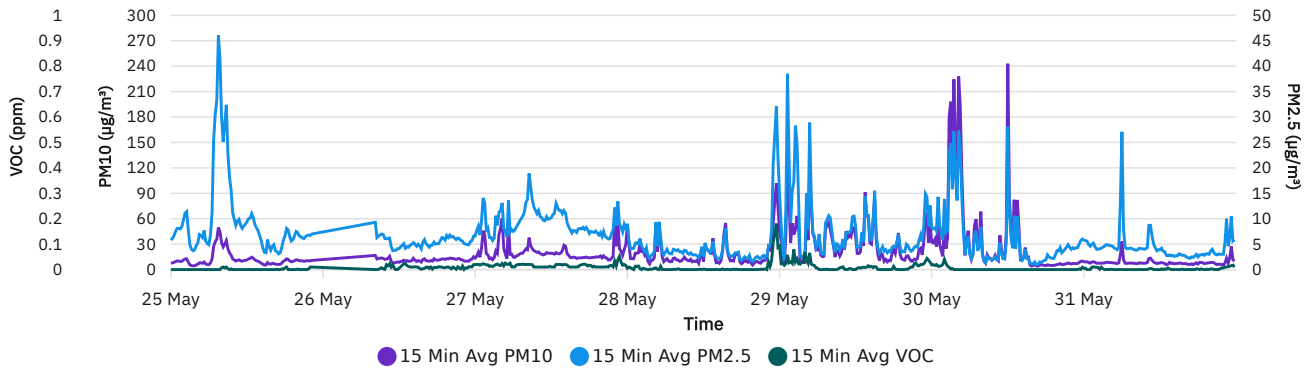

AM-33\_Reach 1\_3315

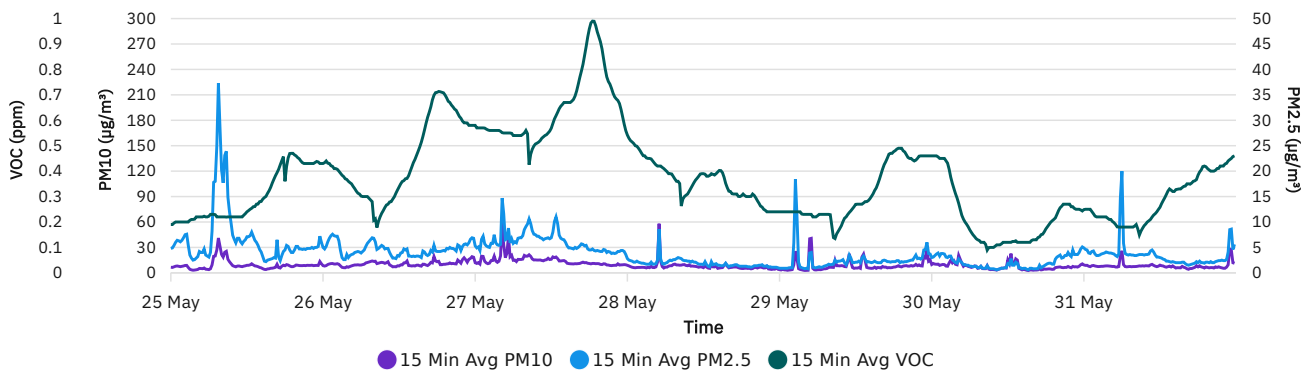

Exceedance Summary

Parameter	Action Level	Time Triggered	Cause	Mitigation
PM10	150.0 µg/m³	5/29/2026 01:12	Elevated readings were attributable to wind-blown dust across the site.	Contractor wetted the area to mitigate dust levels and fugitive dust.
PM10	100.0 µg/m³	5/30/2026 02:48	Elevated readings were attributable to wind-blown dust across the site.	Contractor wetted the area to mitigate dust levels and fugitive dust.
PM10	150.0 µg/m³	5/30/2026 03:19	Elevated readings were attributable to wind-blown dust across the site.	Contractor wetted the area to mitigate dust levels and fugitive dust.
PM10	100.0 µg/m³	5/30/2026 04:05	Elevated readings were attributable to wind-blown dust across the site.	Contractor wetted the area to mitigate dust levels and fugitive dust.
PM10	150.0 µg/m³	5/30/2026 11:51	Elevated readings were attributable to wind-blown dust across the site.	Contractor wetted the area to mitigate dust levels and fugitive dust.
PM2.5	25.0 µg/m³	5/28/2026 23:03	Elevated readings were attributable to wind-blown dust across the site.	Contractor wetted the area to mitigate dust levels and fugitive dust.
PM2.5	25.0 µg/m³	5/28/2026 23:21	Elevated readings were attributable to wind-blown dust across the site.	Contractor wetted the area to mitigate dust levels and fugitive dust.
PM2.5	35.0 µg/m³	5/29/2026 01:11	Elevated readings were attributable to wind-blown dust across the site.	Contractor wetted the area to mitigate dust levels and fugitive dust.
PM2.5	25.0 µg/m³	5/30/2026 12:00	Elevated readings were attributable to wind-blown dust across the site.	Contractor wetted the area to mitigate dust levels and fugitive dust.







Reach 3\_EWP\_AQS Report


Battery Park_AQS	
Report Period	
From:	05/01/2026 00:00
To:	05/03/2026 23:59
PM10 Action Level:	100 µg/m³
PM2.5 Action Level:	25 µg/m³
VOC Action Level:	5 ppm

Daily Environmental Summary	Temp (°F)	Relative Humidity (%)	Barometer (inHg)	Wind Speed (mph)	Prevailing Wind Direction
05/01/2026	46.0 - 66.0	32.6 - 60.8	29.7 - 32.2	0.5 - 11.4	ENE
05/02/2026	50.2 - 61.2	29.4 - 70.3	29.7 - 31.0	0.3 - 12.0	NE
05/03/2026	43.5 - 59.5	23.9 - 53.5	29.7 - 31.2	0.9 - 16.3	NNE


Daily Monitoring Summary	PM2.5 (µg/m³)	Time	PM10 (µg/m³)	Time	VOC (ppm)	Time
Min Contribution (15 min avg.) - 5/1/2026	0.0	00:00	0.0	00:00	0.0000	00:00
Max Contribution (15 min avg.) - 5/1/2026	3.1	20:30	2.7	20:30	0.0307	10:45
Daily Avg. Contribution (15 min avg.) - 5/1/2026	0.2	-	0.2	-	0.0014	-
Min Contribution (15 min avg.) - 5/2/2026	0.0	00:00	0.0	00:00	0.0000	00:00
Max Contribution (15 min avg.) - 5/2/2026	1.2	05:30	1.0	05:15	0.0073	05:30
Daily Avg. Contribution (15 min avg.) - 5/2/2026	0.0	-	0.0	-	0.0003	-
Min Contribution (15 min avg.) - 5/3/2026	0.0	00:00	0.0	00:00	0.0000	00:30
Max Contribution (15 min avg.) - 5/3/2026	3.2	18:15	3.1	18:15	0.0073	21:45
Daily Avg. Contribution (15 min avg.) - 5/3/2026	0.2	-	0.2	-	0.0003	-

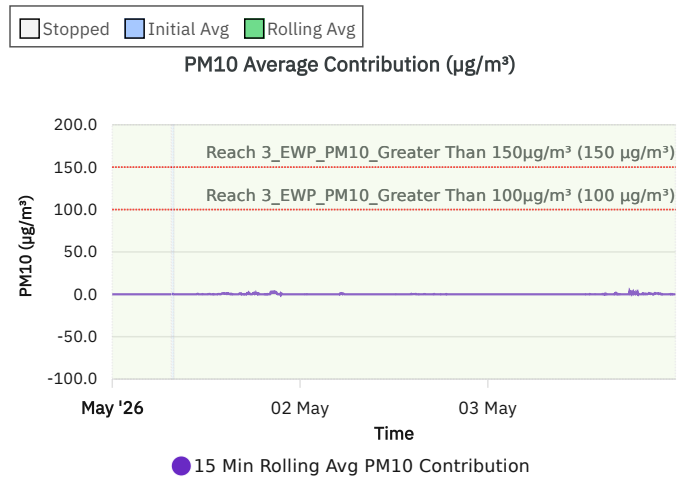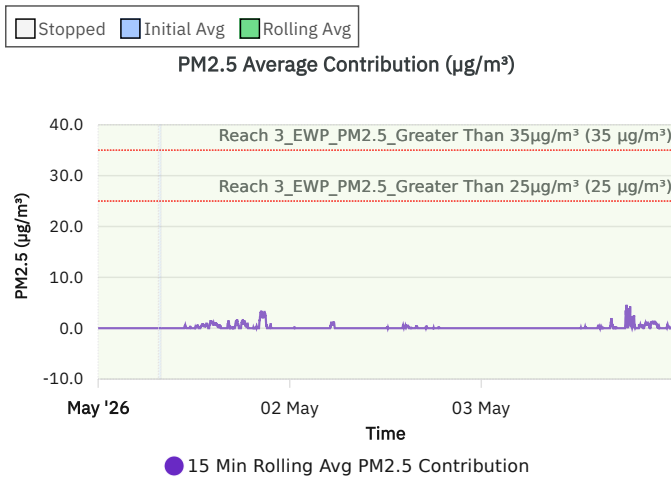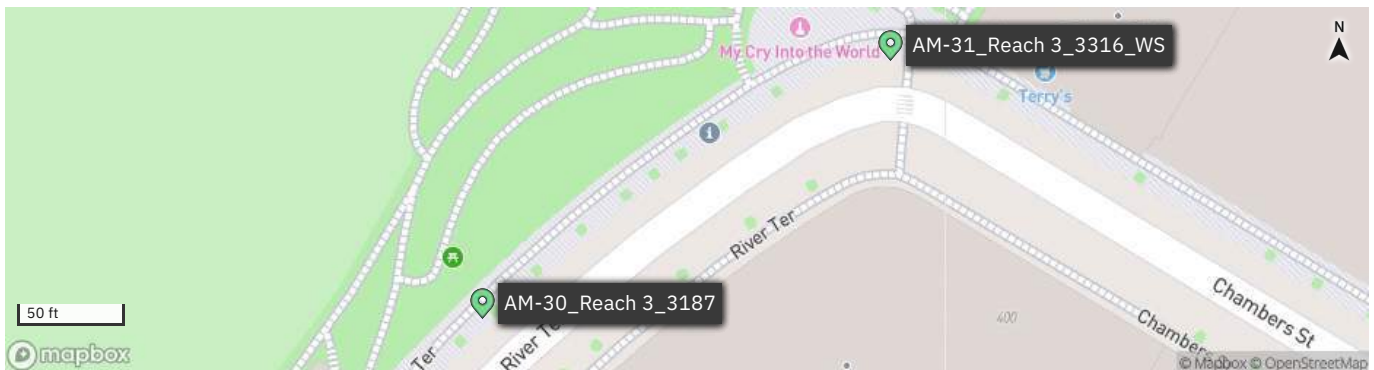


### VOC Average Contribution (ppm)

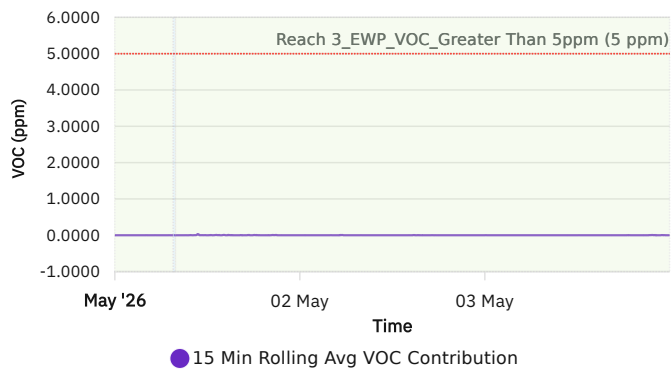


### Wind rose (mph)

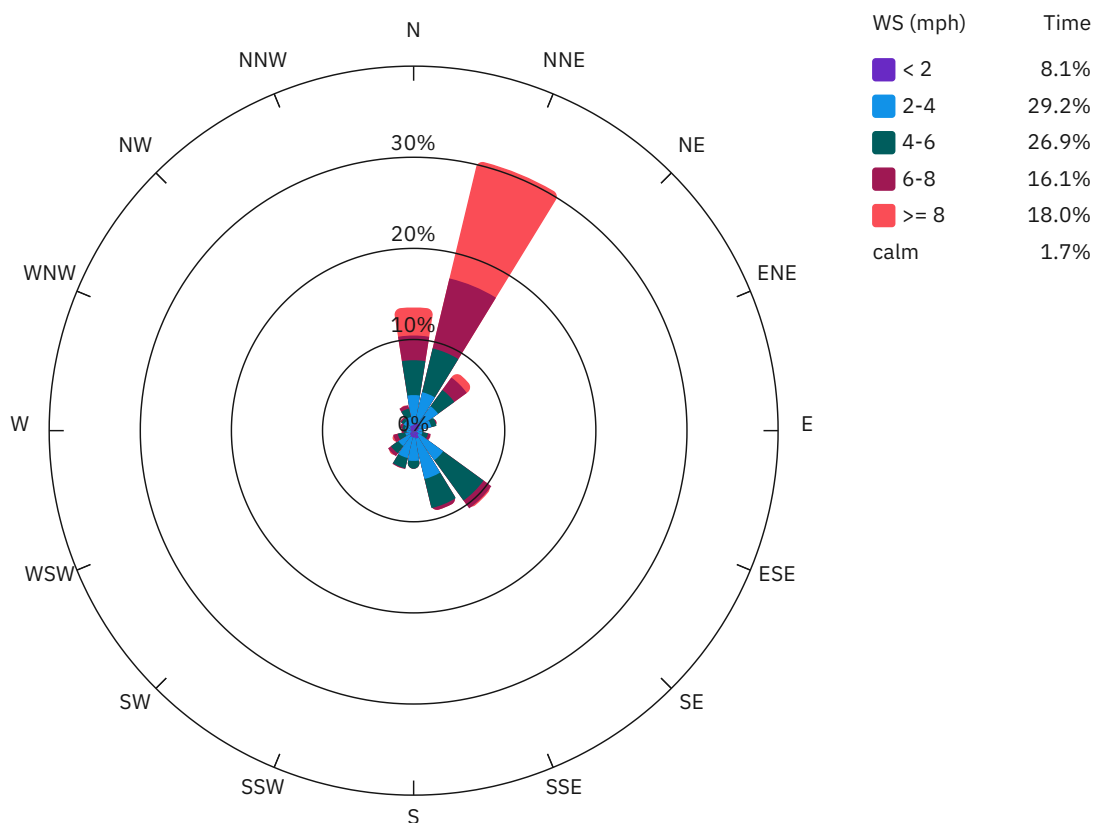

### AM-30\_Reach 3\_3187

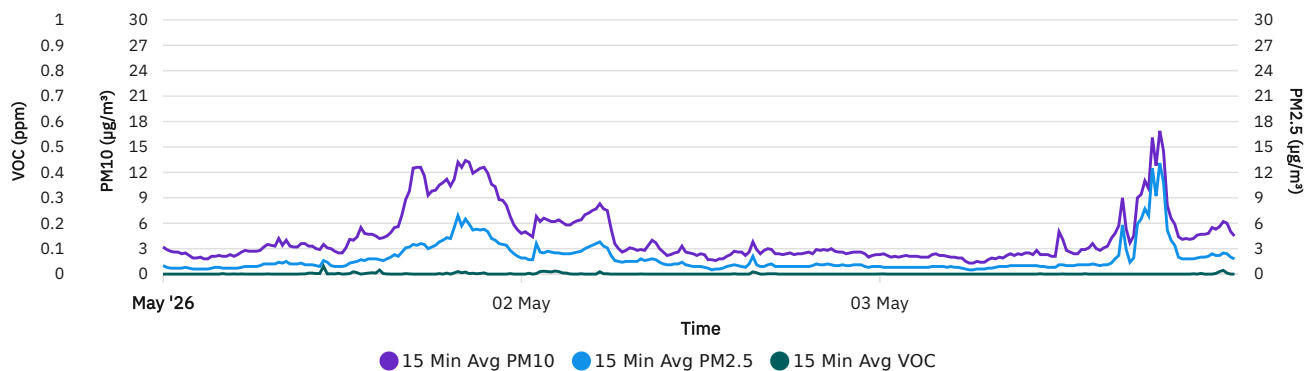

AM-31\_Reach 3\_3316\_WS

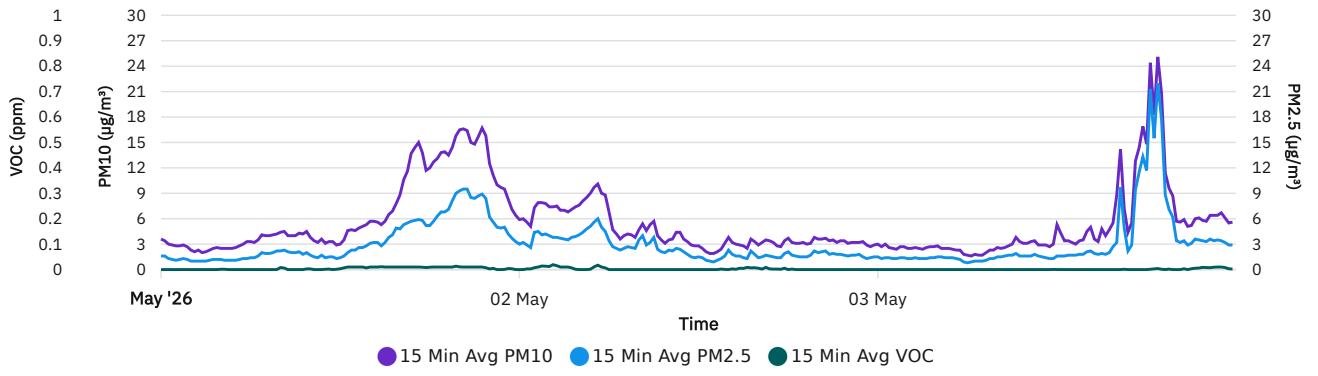




Reach 3\_EWP\_AQS Report

Battery Park_AQS	
Report Period	
From:	05/04/2026 00:00
To:	05/10/2026 23:59
PM10 Action Level:	100 µg/m³
PM2.5 Action Level:	25 µg/m³
VOC Action Level:	5 ppm

Daily Environmental Summary	Temp (°F)	Relative Humidity (%)	Barometer (inHg)	Wind Speed (mph)	Prevailing Wind Direction
05/04/2026	49.1 - 74.5	28.2 - 56.8	29.6 - 31.2	1.1 - 11.0	SE
05/05/2026	59.0 - 82.9	28.4 - 61.7	29.6 - 31.1	0.6 - 11.1	SE
05/06/2026	55.6 - 69.3	53.8 - 85.0	29.6 - 31.2	0.8 - 14.0	SE
05/07/2026	47.5 - 65.8	27.7 - 81.8	29.6 - 32.0	0.4 - 12.8	N
05/08/2026	47.3 - 63.1	32.0 - 66.4	29.3 - 32.0	0.3 - 17.5	NNE
05/09/2026	54.3 - 64.2	49.1 - 82.5	29.7 - 31.7	0.3 - 5.9	SSE
05/10/2026	52.2 - 68.5	58.0 - 84.3	29.7 - 31.2	0.3 - 6.6	S


Daily Monitoring Summary	PM2.5 (µg/m³)	Time	PM10 (µg/m³)	Time	VOC (ppm)	Time
Min Contribution (15 min avg.) - 5/4/2026	0.0	00:00	0.0	00:00	0.0000	00:00
Max Contribution (15 min avg.) - 5/4/2026	1.3	08:15	5.4	09:30	0.0080	10:15
Daily Avg. Contribution (15 min avg.) - 5/4/2026	0.1	-	0.2	-	0.0006	-
Min Contribution (15 min avg.) - 5/5/2026	0.0	00:00	0.0	00:00	0.0000	00:00
Max Contribution (15 min avg.) - 5/5/2026	3.2	18:15	43.9	18:15	0.0067	12:45
Daily Avg. Contribution (15 min avg.) - 5/5/2026	0.1	-	2.7	-	0.0004	-
Min Contribution (15 min avg.) - 5/6/2026	0.0	00:00	0.0	00:00	0.0000	00:00
Max Contribution (15 min avg.) - 5/6/2026	1.7	18:45	3.2	14:00	0.0080	08:45
Daily Avg. Contribution (15 min avg.) - 5/6/2026	0.1	-	0.1	-	0.0005	-
Min Contribution (15 min avg.) - 5/7/2026	0.0	00:00	0.0	00:00	0.0000	00:00
Max Contribution (15 min avg.) - 5/7/2026	1.9	23:15	1.4	23:15	0.0040	15:15
Daily Avg. Contribution (15 min avg.) - 5/7/2026	0.1	-	0.0	-	0.0002	-
Min Contribution (15 min avg.) - 5/8/2026	0.0	02:15	0.0	02:15	0.0000	00:00
Max Contribution (15 min avg.) - 5/8/2026	2.4	23:15	1.8	23:00	0.0100	08:15
Daily Avg. Contribution (15 min avg.) - 5/8/2026	0.3	-	0.2	-	0.0009	-
Min Contribution (15 min avg.) - 5/9/2026	0.0	02:30	0.0	02:30	0.0000	00:45
Max Contribution (15 min avg.) - 5/9/2026	6.7	00:30	6.6	00:30	0.0087	00:15
Daily Avg. Contribution (15 min avg.) - 5/9/2026	0.9	-	0.8	-	0.0010	-
Min Contribution (15 min avg.) - 5/10/2026	0.0	01:45	0.0	01:45	0.0000	01:45
Max Contribution (15 min avg.) - 5/10/2026	26.9	13:00	25.1	01:30	0.0207	15:45
Daily Avg. Contribution (15 min avg.) - 5/10/2026	8.9	-	8.1	-	0.0056	-

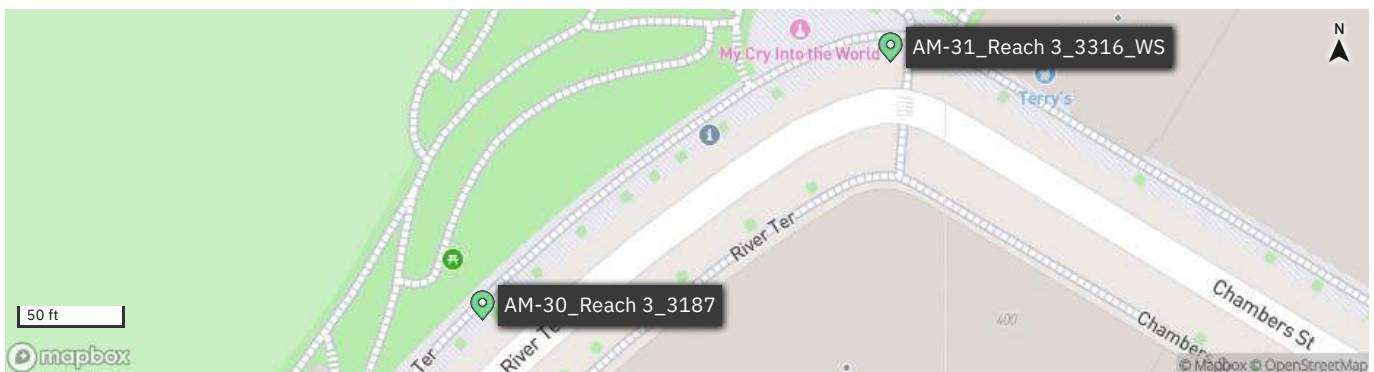


Stopped 
  Initial Avg 
  Rolling Avg

Stopped 
  Initial Avg 
  Rolling Avg

PM2.5 Average Contribution ( $\mu\text{g}/\text{m}^3$ )

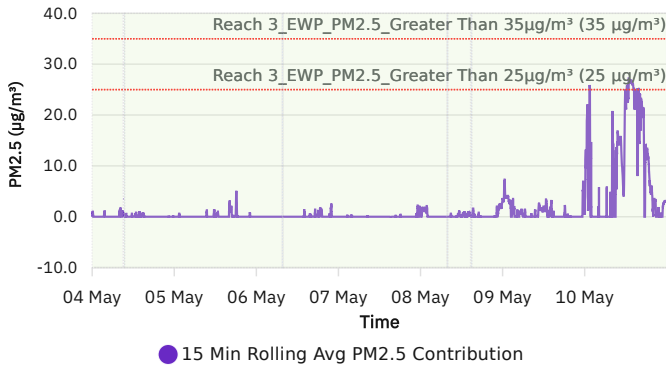


PM10 Average Contribution ( $\mu\text{g}/\text{m}^3$ )

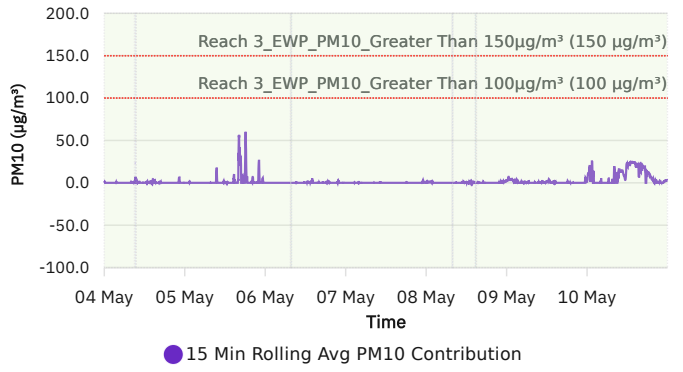


Stopped Initial Avg Rolling Avg


VOC Average Contribution (ppm)

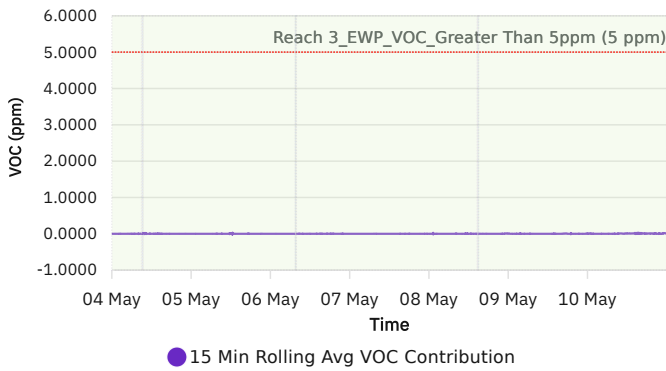


Wind rose (mph)

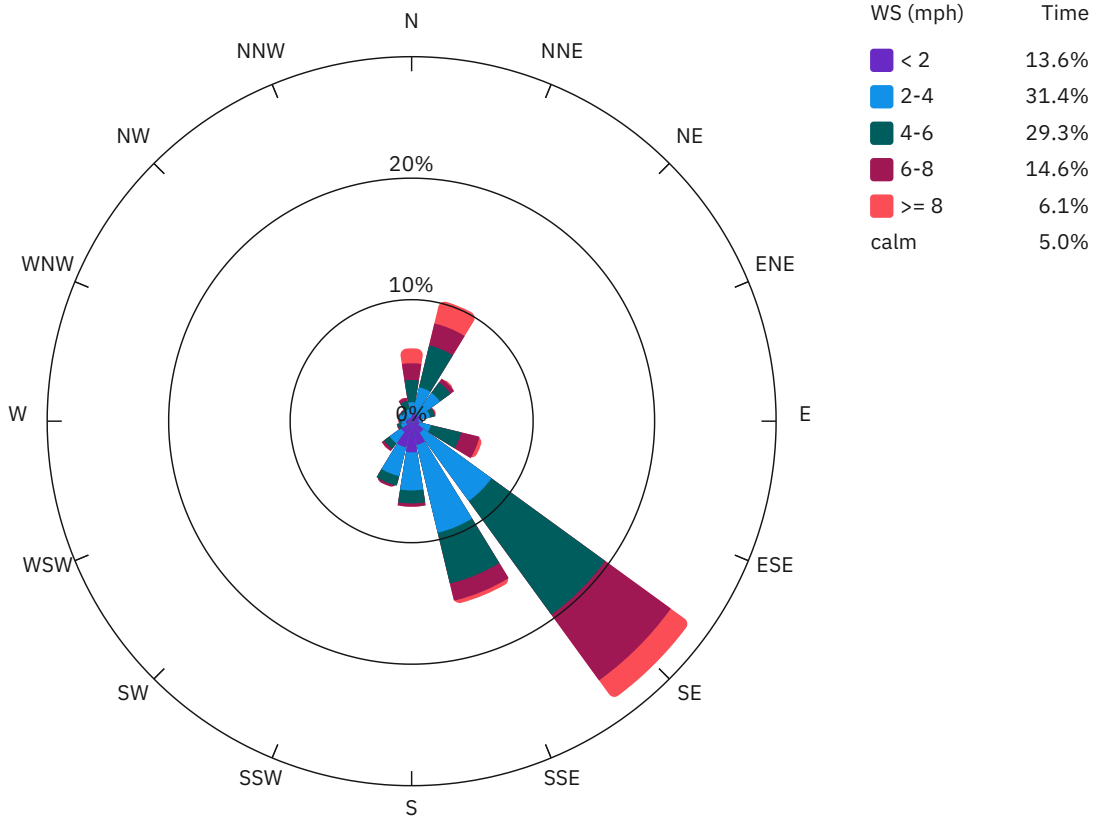

AM-30\_Reach 3\_3187

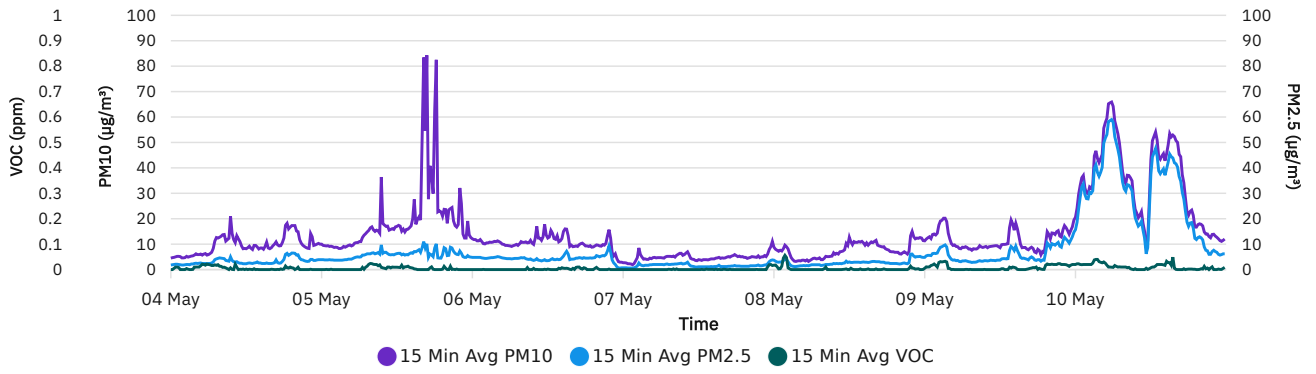

AM-31\_Reach 3\_3316\_WS

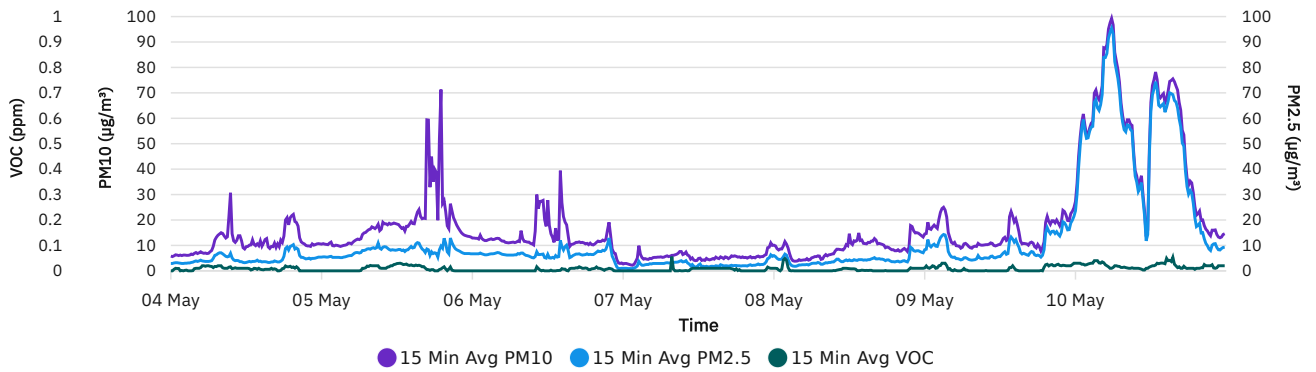

Exceedance Summary

Parameter	Action Level	Time Triggered	Cause	Mitigation
PM2.5	25.0 µg/m <sup>3</sup>	5/10/2026 01:26	Elevated readings were attributable to construction activities within the project area.	Contractor deemed mitigation methods were not warranted.
PM2.5	25.0 µg/m <sup>3</sup>	5/10/2026 12:16	Elevated readings were attributable to construction activities within the project area.	Contractor deemed mitigation methods were not warranted.
PM2.5	25.0 µg/m <sup>3</sup>	5/10/2026 12:52	Elevated readings were attributable to construction activities within the project area.	Contractor deemed mitigation methods were not warranted.
PM2.5	25.0 µg/m <sup>3</sup>	5/10/2026 15:18	Elevated readings were attributable to construction activities within the project area.	Contractor deemed mitigation methods were not warranted.
PM2.5	25.0 µg/m <sup>3</sup>	5/10/2026 15:38	Elevated readings were attributable to construction activities within the project area.	Contractor deemed mitigation methods were not warranted.




Reach 3\_EWP\_AQS Report

Battery Park_AQS	
Report Period	
From:	05/11/2026 00:00
To:	05/17/2026 23:59
PM10 Action Level:	100 µg/m³
PM2.5 Action Level:	25 µg/m³
VOC Action Level:	5 ppm

Daily Environmental Summary	Temp (°F)	Relative Humidity (%)	Barometer (inHg)	Wind Speed (mph)	Prevailing Wind Direction
05/11/2026	52.0 - 63.7	28.6 - 69.1	29.9 - 31.9	0.3 - 12.5	NE
05/12/2026	45.9 - 70.5	24.2 - 61.7	29.8 - 31.9	0.6 - 11.0	ENE
05/13/2026	53.4 - 71.4	35.6 - 66.2	29.5 - 32.1	0.6 - 7.7	SE
05/14/2026	53.2 - 69.3	38.1 - 77.7	29.5 - 31.4	0.3 - 8.5	ESE
05/15/2026	50.2 - 67.3	44.7 - 66.1	29.7 - 31.5	0.8 - 8.7	NNE
05/16/2026	55.0 - 83.5	28.7 - 71.4	29.8 - 31.3	0.4 - 8.3	SSE
05/17/2026	67.5 - 89.1	33.0 - 63.1	29.8 - 31.7	0.4 - 8.4	SSE


Daily Monitoring Summary	PM2.5 (µg/m³)	Time	PM10 (µg/m³)	Time	VOC (ppm)	Time
Min Contribution (15 min avg.) - 5/11/2026	0.0	00:45	0.0	00:45	0.0000	00:45
Max Contribution (15 min avg.) - 5/11/2026	3.1	00:00	2.2	00:00	0.0120	00:00
Daily Avg. Contribution (15 min avg.) - 5/11/2026	0.3	-	0.2	-	0.0013	-
Min Contribution (15 min avg.) - 5/12/2026	0.0	00:00	0.0	00:00	0.0000	04:15
Max Contribution (15 min avg.) - 5/12/2026	2.1	11:30	2.2	11:30	0.1207	09:15
Daily Avg. Contribution (15 min avg.) - 5/12/2026	0.1	-	0.1	-	0.0028	-
Min Contribution (15 min avg.) - 5/13/2026	0.0	00:00	0.0	00:00	0.0000	00:00
Max Contribution (15 min avg.) - 5/13/2026	1.7	20:30	1.6	20:30	0.0040	09:15
Daily Avg. Contribution (15 min avg.) - 5/13/2026	0.1	-	0.1	-	0.0002	-
Min Contribution (15 min avg.) - 5/14/2026	0.0	00:00	0.0	00:00	0.0000	00:00
Max Contribution (15 min avg.) - 5/14/2026	2.0	14:15	1.3	14:00	0.0253	17:45
Daily Avg. Contribution (15 min avg.) - 5/14/2026	0.3	-	0.2	-	0.0029	-
Min Contribution (15 min avg.) - 5/15/2026	0.0	00:00	0.0	00:00	0.0000	00:00
Max Contribution (15 min avg.) - 5/15/2026	1.0	21:30	2.3	07:45	0.0100	21:15
Daily Avg. Contribution (15 min avg.) - 5/15/2026	0.1	-	0.1	-	0.0008	-
Min Contribution (15 min avg.) - 5/16/2026	0.0	00:00	0.0	00:00	0.0000	00:00
Max Contribution (15 min avg.) - 5/16/2026	2.8	02:00	5.1	18:30	0.0147	11:30
Daily Avg. Contribution (15 min avg.) - 5/16/2026	0.6	-	0.6	-	0.0012	-
Min Contribution (15 min avg.) - 5/17/2026	0.0	00:00	0.0	00:00	0.0000	00:15
Max Contribution (15 min avg.) - 5/17/2026	4.6	20:00	13.8	20:00	0.0260	15:15
Daily Avg. Contribution (15 min avg.) - 5/17/2026	0.8	-	1.0	-	0.0042	-

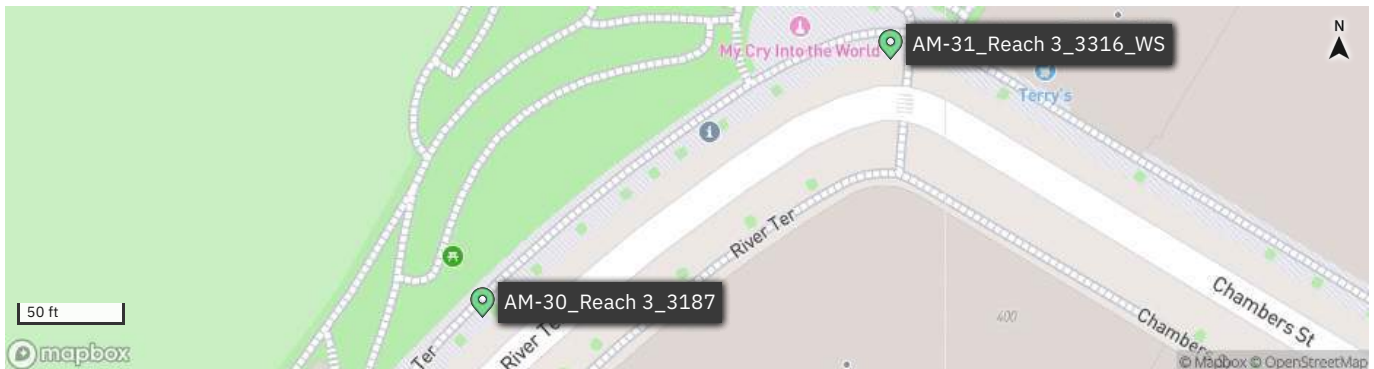


Stopped 
  Initial Avg 
  Rolling Avg

Stopped 
  Initial Avg 
  Rolling Avg

PM2.5 Average Contribution ( $\mu\text{g}/\text{m}^3$ )

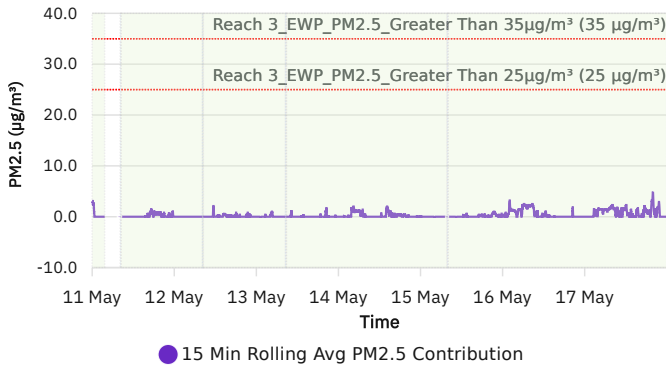


PM10 Average Contribution ( $\mu\text{g}/\text{m}^3$ )

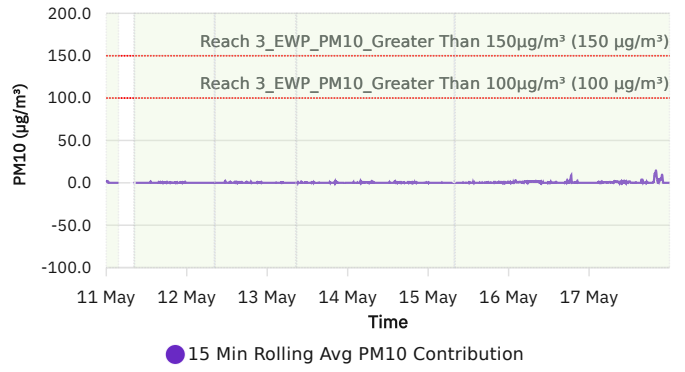


Stopped Initial Avg Rolling Avg


VOC Average Contribution (ppm)

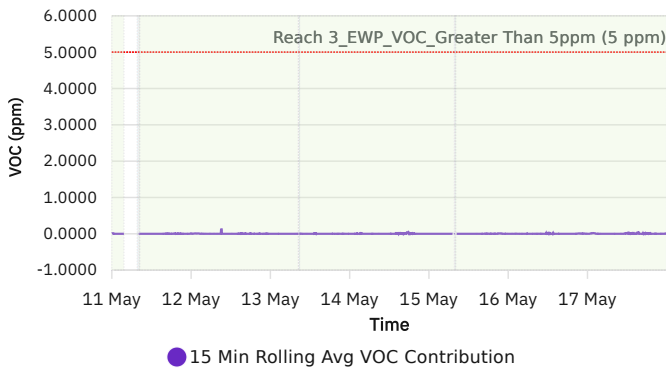


Wind rose (mph)

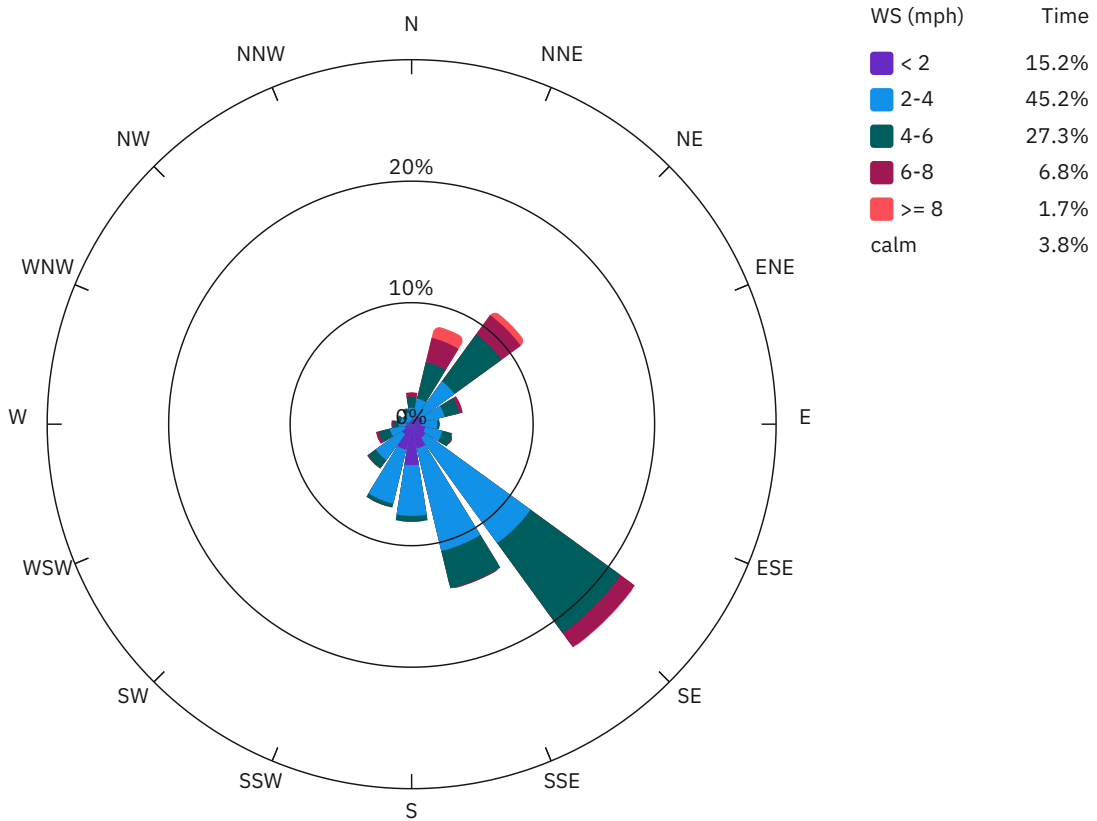

AM-30\_Reach 3\_3187

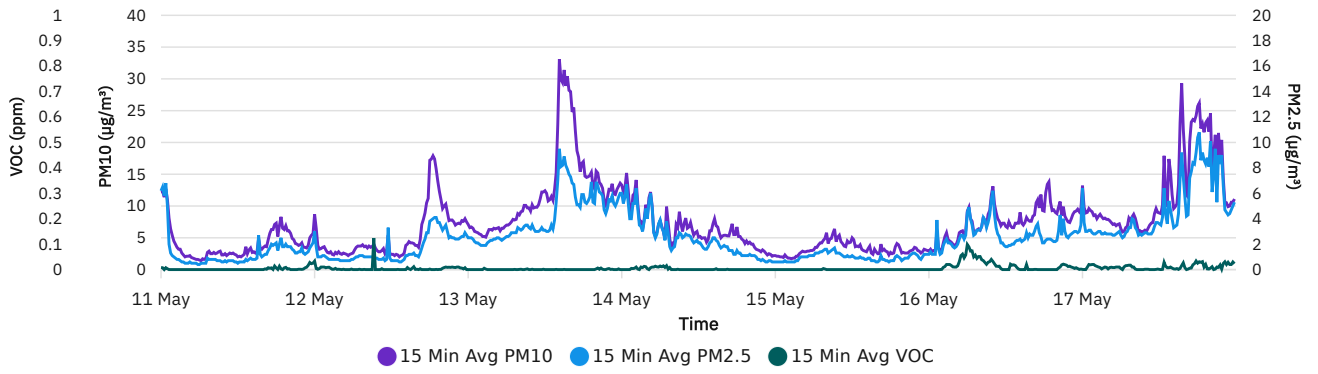

AM-31\_Reach 3\_3316\_WS

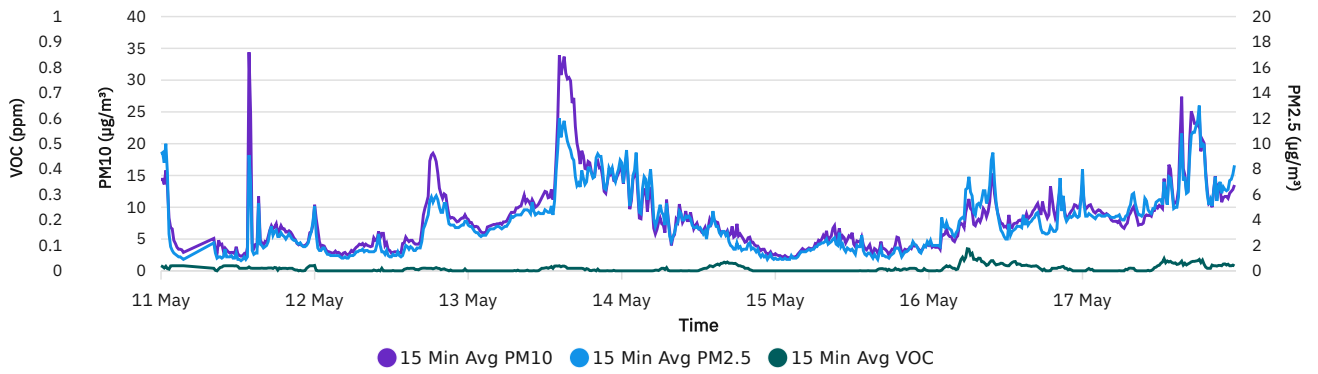




Reach 3\_EWP\_AQS Report

Battery Park_AQS	
Report Period	
From:	05/18/2026 00:00
To:	05/24/2026 23:59
PM10 Action Level:	100 µg/m³
PM2.5 Action Level:	25 µg/m³
VOC Action Level:	5 ppm

Daily Environmental Summary	Temp (°F)	Relative Humidity (%)	Barometer (inHg)	Wind Speed (mph)	Prevailing Wind Direction
05/18/2026	66.7 - 89.6	39.3 - 68.0	29.9 - 32.1	0.5 - 6.8	SSE
05/19/2026	73.2 - 95.7	34.2 - 70.2	29.8 - 31.5	0.7 - 7.5	SE
05/20/2026	66.2 - 93.7	38.7 - 80.0	29.8 - 31.0	0.4 - 10.8	ESE
05/21/2026	52.2 - 66.2	47.5 - 81.4	30.0 - 31.5	0.4 - 11.9	NE
05/22/2026	55.9 - 69.3	34.9 - 49.8	30.2 - 31.7	0.7 - 8.1	SE
05/23/2026	48.4 - 58.8	42.2 - 85.6	30.3 - 31.7	0.5 - 7.1	SE
05/24/2026	49.3 - 55.2	82.8 - 88.1	30.1 - 31.8	0.7 - 7.5	SE


Daily Monitoring Summary	PM2.5 (µg/m³)	Time	PM10 (µg/m³)	Time	VOC (ppm)	Time
Min Contribution (15 min avg.) - 5/18/2026	0.0	00:00	0.0	00:00	0.0000	00:30
Max Contribution (15 min avg.) - 5/18/2026	16.8	10:15	17.6	10:15	0.0200	12:45
Daily Avg. Contribution (15 min avg.) - 5/18/2026	2.6	-	2.2	-	0.0035	-
Min Contribution (15 min avg.) - 5/19/2026	0.0	00:00	0.0	00:00	0.0000	00:00
Max Contribution (15 min avg.) - 5/19/2026	8.3	10:45	15.2	16:45	0.0140	14:30
Daily Avg. Contribution (15 min avg.) - 5/19/2026	0.6	-	0.8	-	0.0016	-
Min Contribution (15 min avg.) - 5/20/2026	0.0	00:00	0.0	00:00	0.0000	00:00
Max Contribution (15 min avg.) - 5/20/2026	3.9	08:30	21.5	19:15	0.0200	08:30
Daily Avg. Contribution (15 min avg.) - 5/20/2026	0.4	-	0.5	-	0.0021	-
Min Contribution (15 min avg.) - 5/21/2026	0.0	00:00	0.0	00:00	0.0000	00:00
Max Contribution (15 min avg.) - 5/21/2026	4.7	20:00	5.2	20:00	0.0093	20:00
Daily Avg. Contribution (15 min avg.) - 5/21/2026	0.1	-	0.2	-	0.0004	-
Min Contribution (15 min avg.) - 5/22/2026	0.0	00:00	0.0	00:00	0.0000	00:00
Max Contribution (15 min avg.) - 5/22/2026	0.8	23:00	1.3	07:00	0.0047	00:45
Daily Avg. Contribution (15 min avg.) - 5/22/2026	0.0	-	0.1	-	0.0002	-
Min Contribution (15 min avg.) - 5/23/2026	0.0	00:15	0.0	00:15	0.0000	00:15
Max Contribution (15 min avg.) - 5/23/2026	1.2	20:30	1.1	20:30	0.0213	06:15
Daily Avg. Contribution (15 min avg.) - 5/23/2026	0.0	-	0.0	-	0.0041	-
Min Contribution (15 min avg.) - 5/24/2026	0.0	00:00	0.0	00:00	0.0000	00:00
Max Contribution (15 min avg.) - 5/24/2026	0.7	10:15	0.7	10:15	0.0033	00:15
Daily Avg. Contribution (15 min avg.) - 5/24/2026	0.0	-	0.0	-	0.0001	-

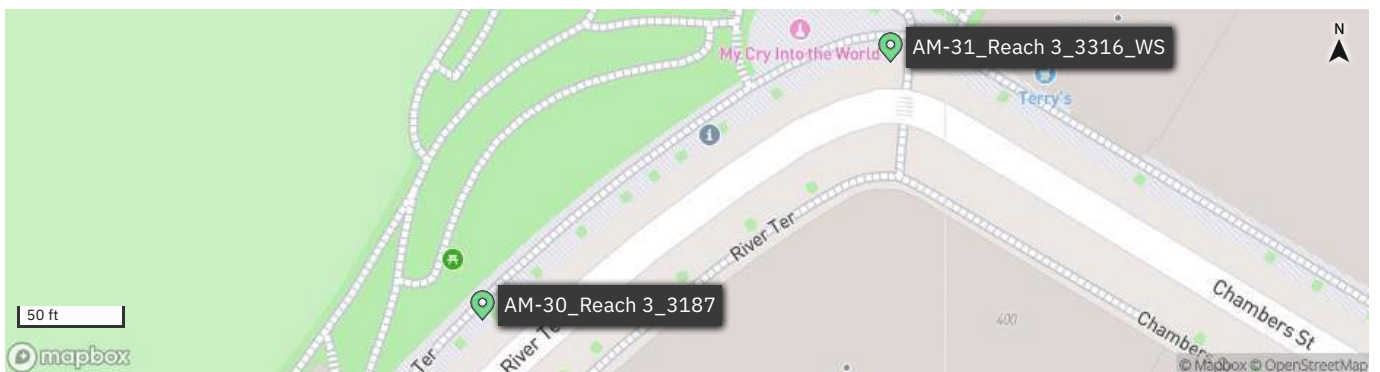


Stopped 
  Initial Avg 
  Rolling Avg

Stopped 
  Initial Avg 
  Rolling Avg

PM2.5 Average Contribution ( $\mu\text{g}/\text{m}^3$ )

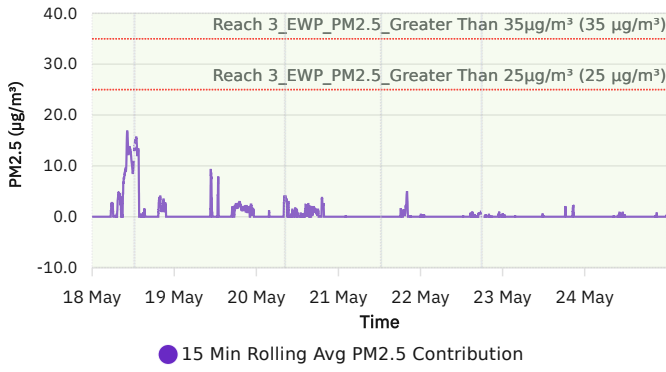


PM10 Average Contribution ( $\mu\text{g}/\text{m}^3$ )

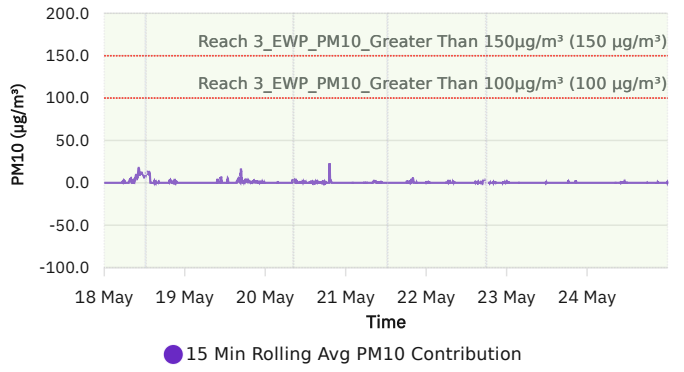


Stopped Initial Avg Rolling Avg


VOC Average Contribution (ppm)

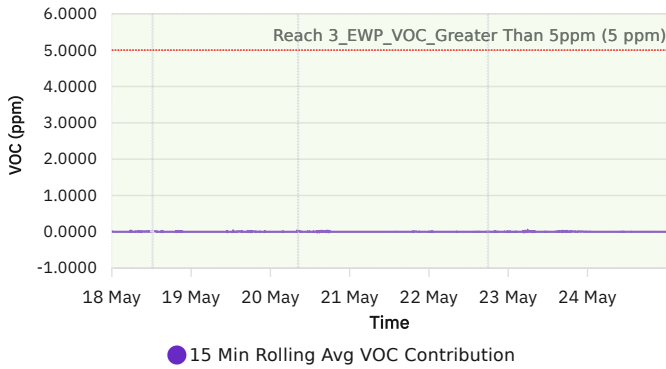


Wind rose (mph)

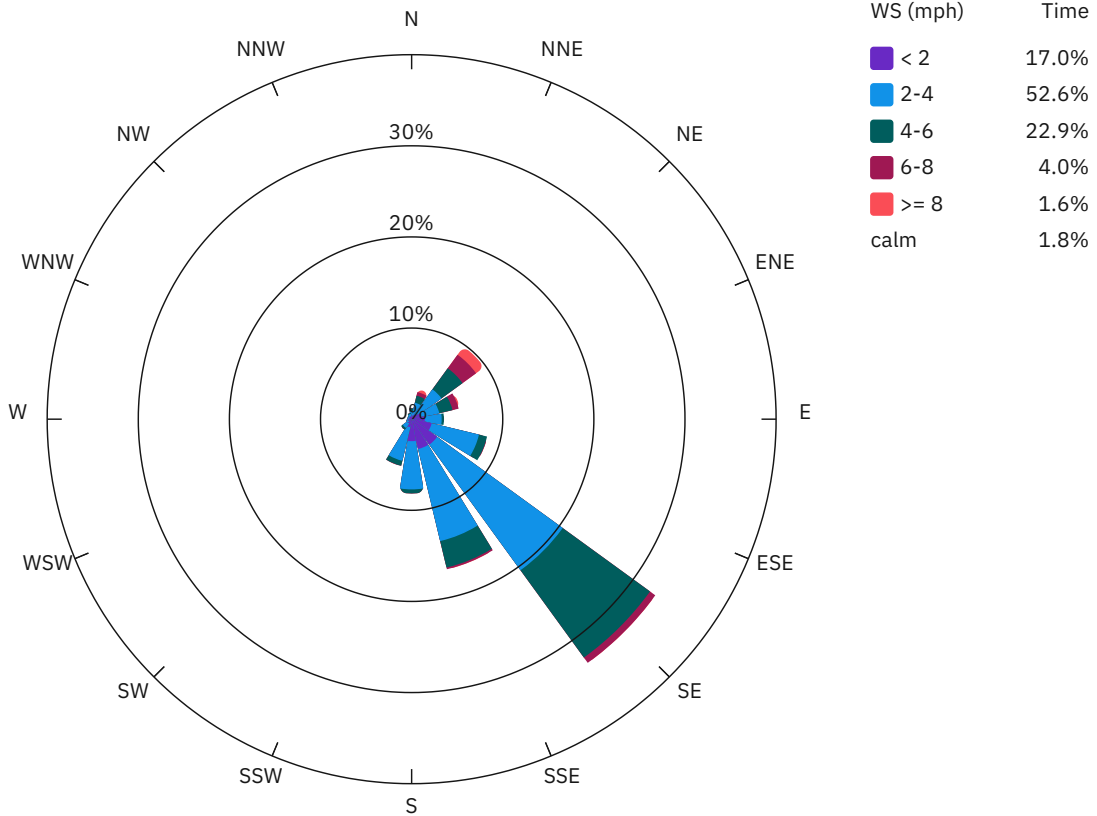

AM-30\_Reach 3\_3187

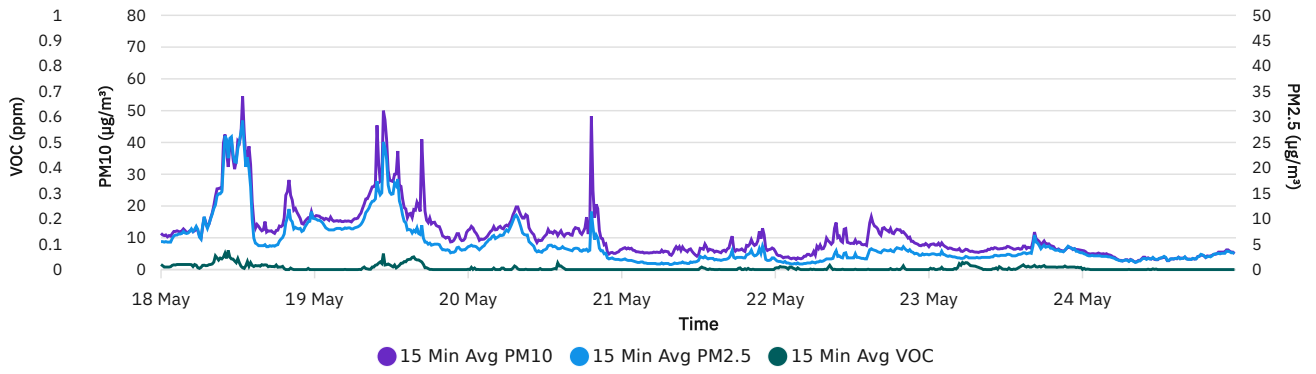

AM-31\_Reach 3\_3316\_WS

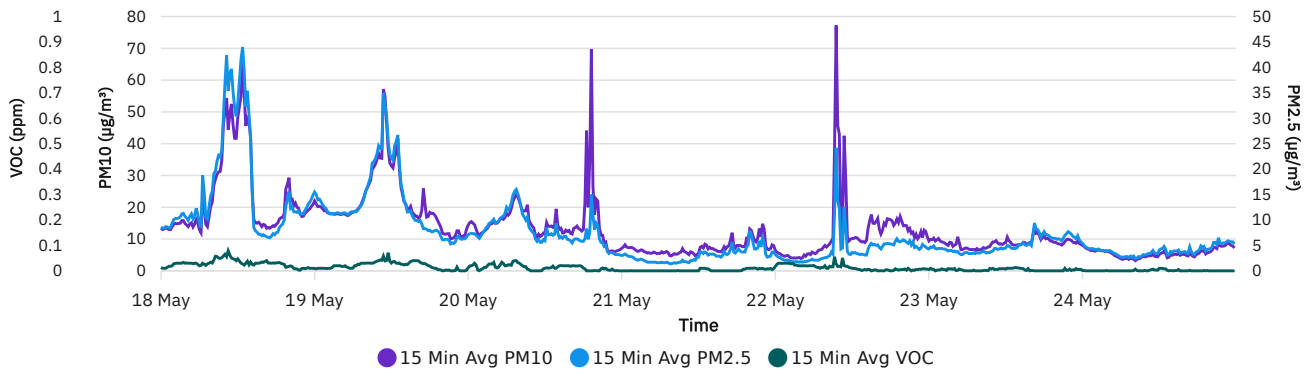




Reach 3\_EWP\_AQS Report

Battery Park_AQS	
Report Period	
From:	05/25/2026 00:00
To:	05/31/2026 23:59
PM10 Action Level:	100 µg/m³
PM2.5 Action Level:	25 µg/m³
VOC Action Level:	5 ppm

Daily Environmental Summary	Temp (°F)	Relative Humidity (%)	Barometer (inHg)	Wind Speed (mph)	Prevailing Wind Direction
05/25/2026	54.3 - 77.2	57.5 - 88.0	29.9 - 31.4	0.4 - 8.4	SSE
05/26/2026	61.2 - 82.9	36.1 - 75.6	27.0 - 31.3	0.1 - 6.4	SE
05/27/2026	67.8 - 84.0	40.6 - 68.3	29.6 - 31.2	0.8 - 8.5	SSE
05/28/2026	62.1 - 76.5	37.2 - 55.4	29.7 - 31.1	0.9 - 14.5	NE
05/29/2026	57.7 - 80.1	29.6 - 60.0	29.6 - 31.4	0.6 - 10.3	ESE
05/30/2026	52.7 - 69.6	43.4 - 59.3	29.7 - 31.3	0.3 - 20.5	NNE
05/31/2026	51.3 - 76.1	29.3 - 64.3	28.8 - 32.7	0.3 - 9.0	SE


Daily Monitoring Summary	PM2.5 (µg/m³)	Time	PM10 (µg/m³)	Time	VOC (ppm)	Time
Min Contribution (15 min avg.) - 5/25/2026	0.0	00:15	0.0	00:15	0.0000	00:00
Max Contribution (15 min avg.) - 5/25/2026	20.3	07:30	19.7	07:30	0.0293	15:30
Daily Avg. Contribution (15 min avg.) - 5/25/2026	2.6	-	2.5	-	0.0031	-
Min Contribution (15 min avg.) - 5/26/2026	0.0	08:30	0.0	08:30	0.0000	08:30
Max Contribution (15 min avg.) - 5/26/2026	2.3	15:15	8.5	15:15	0.0300	17:00
Daily Avg. Contribution (15 min avg.) - 5/26/2026	0.7	-	0.8	-	0.0076	-
Min Contribution (15 min avg.) - 5/27/2026	0.0	00:00	0.0	00:00	0.0000	00:00
Max Contribution (15 min avg.) - 5/27/2026	4.4	10:45	17.5	13:30	0.0253	11:00
Daily Avg. Contribution (15 min avg.) - 5/27/2026	0.8	-	1.4	-	0.0034	-
Min Contribution (15 min avg.) - 5/28/2026	0.0	00:00	0.0	00:00	0.0000	02:15
Max Contribution (15 min avg.) - 5/28/2026	1.4	10:15	9.0	10:15	0.0193	00:00
Daily Avg. Contribution (15 min avg.) - 5/28/2026	0.0	-	0.1	-	0.0010	-
Min Contribution (15 min avg.) - 5/29/2026	0.0	00:00	0.0	00:00	0.0000	00:00
Max Contribution (15 min avg.) - 5/29/2026	0.0	00:00	0.0	00:00	0.0027	07:00
Daily Avg. Contribution (15 min avg.) - 5/29/2026	0.0	-	0.0	-	0.0001	-
Min Contribution (15 min avg.) - 5/30/2026	-	-	-	-	-	-
Max Contribution (15 min avg.) - 5/30/2026	-	-	-	-	-	-
Daily Avg. Contribution (15 min avg.) - 5/30/2026	-	-	-	-	-	-
Min Contribution (15 min avg.) - 5/31/2026	-	-	-	-	-	-
Max Contribution (15 min avg.) - 5/31/2026	-	-	-	-	-	-
Daily Avg. Contribution (15 min avg.) - 5/31/2026	-	-	-	-	-	-

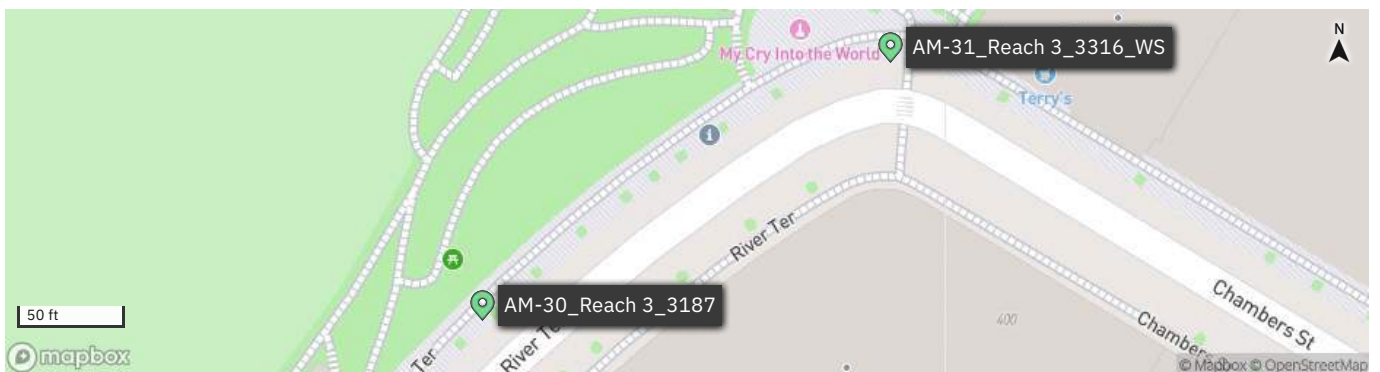


Stopped 
  Initial Avg 
  Rolling Avg

Stopped 
  Initial Avg 
  Rolling Avg

PM2.5 Average Contribution ( $\mu\text{g}/\text{m}^3$ )

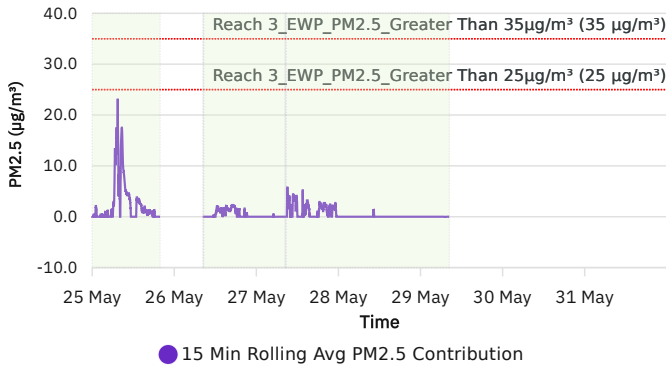


PM10 Average Contribution ( $\mu\text{g}/\text{m}^3$ )

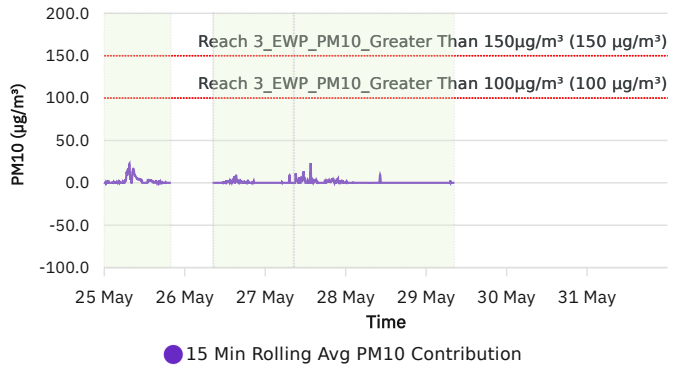


Stopped Initial Avg Rolling Avg


VOC Average Contribution (ppm)

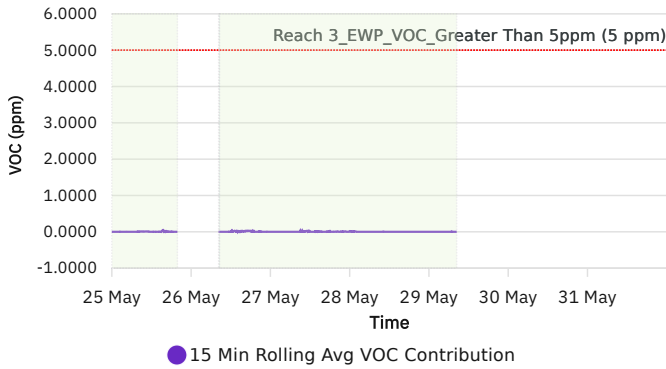


Wind rose (mph)

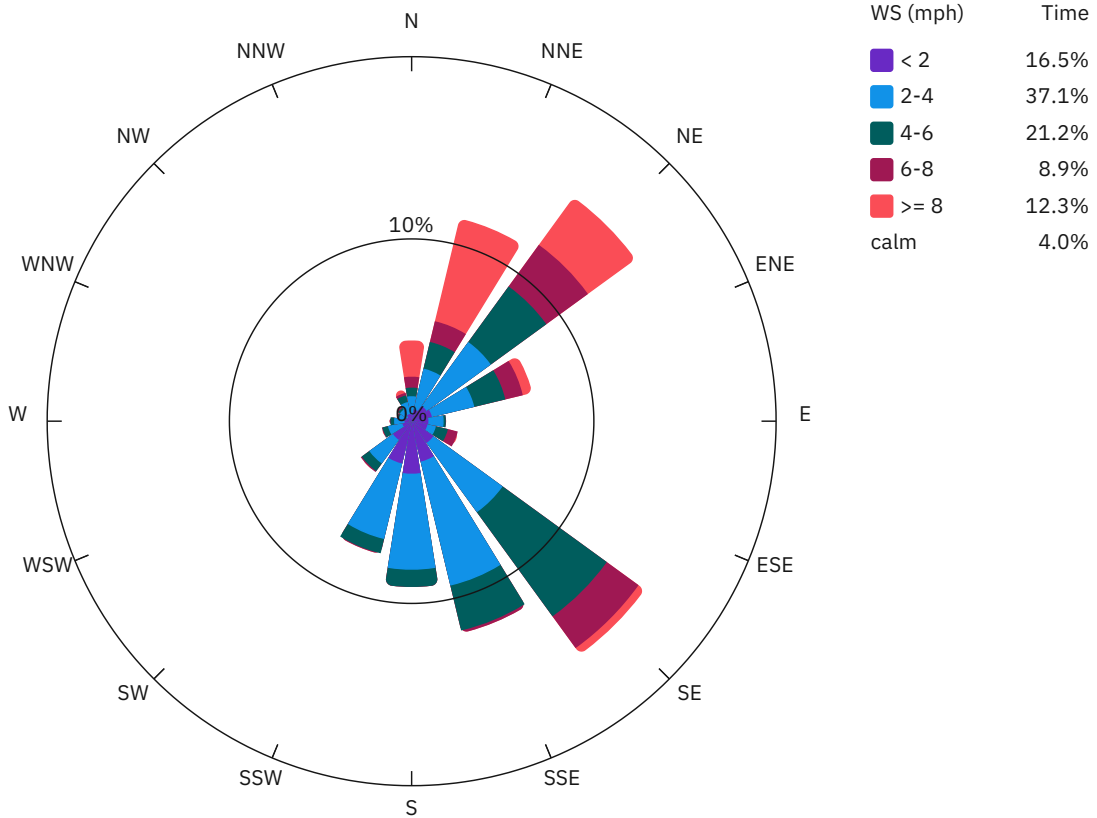

AM-30\_Reach 3\_3187

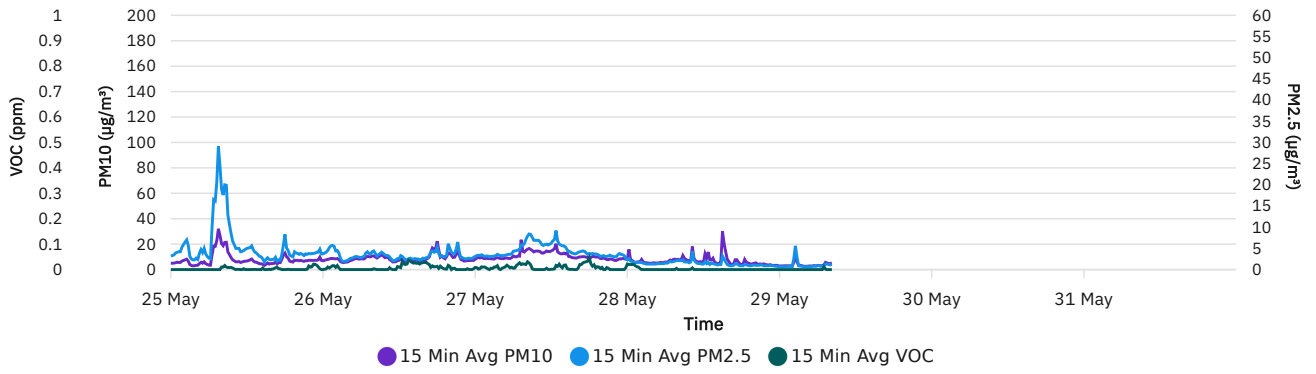

AM-31\_Reach 3\_3316\_WS

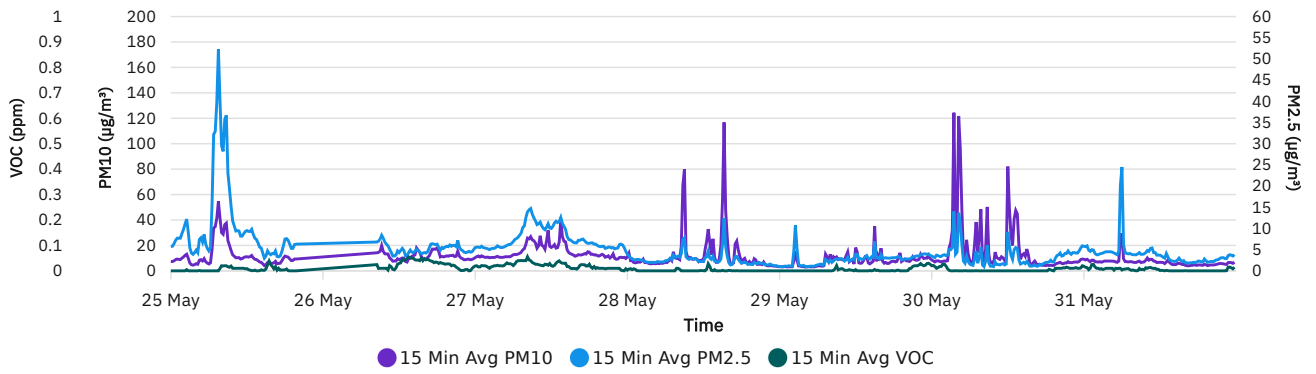



Reach 5\_EWP\_AQS Report


Battery Park\_AQS

Report Period

From:	05/01/2026 00:00
To:	05/03/2026 23:59
PM10 Action Level:	100 µg/m³
PM2.5 Action Level:	25 µg/m³
VOC Action Level:	5 ppm

Daily Environmental Summary	Temp (°F)	Relative Humidity (%)	Barometer (inHg)	Wind Speed (mph)	Prevailing Wind Direction
05/01/2026	46.2 - 62.4	0.0 - 52.8	27.2 - 32.8	0.5 - 8.2	SW
05/02/2026	50.4 - 60.1	0.0 - 65.1	26.7 - 32.3	0.3 - 7.9	N
05/03/2026	43.7 - 59.7	0.0 - 48.6	26.8 - 32.4	0.4 - 12.4	NNE


Daily Monitoring Summary	PM2.5 (µg/m³)	Time	PM10 (µg/m³)	Time	VOC (ppm)	Time
Min Contribution (15 min avg.) - 5/1/2026	0.0	10:00	0.1	17:30	0.0000	00:00
Max Contribution (15 min avg.) - 5/1/2026	11.7	13:45	156.6	13:45	0.0673	11:15
Daily Avg. Contribution (15 min avg.) - 5/1/2026	1.1	-	8.4	-	0.0042	-
Min Contribution (15 min avg.) - 5/2/2026	0.0	07:00	0.0	07:00	0.0000	00:00
Max Contribution (15 min avg.) - 5/2/2026	1.3	01:45	11.6	20:30	0.0113	05:15
Daily Avg. Contribution (15 min avg.) - 5/2/2026	0.4	-	0.8	-	0.0018	-
Min Contribution (15 min avg.) - 5/3/2026	0.0	19:30	0.0	02:45	0.0000	00:00
Max Contribution (15 min avg.) - 5/3/2026	15.7	17:30	248.3	17:30	0.0107	23:15
Daily Avg. Contribution (15 min avg.) - 5/3/2026	1.7	-	18.7	-	0.0038	-

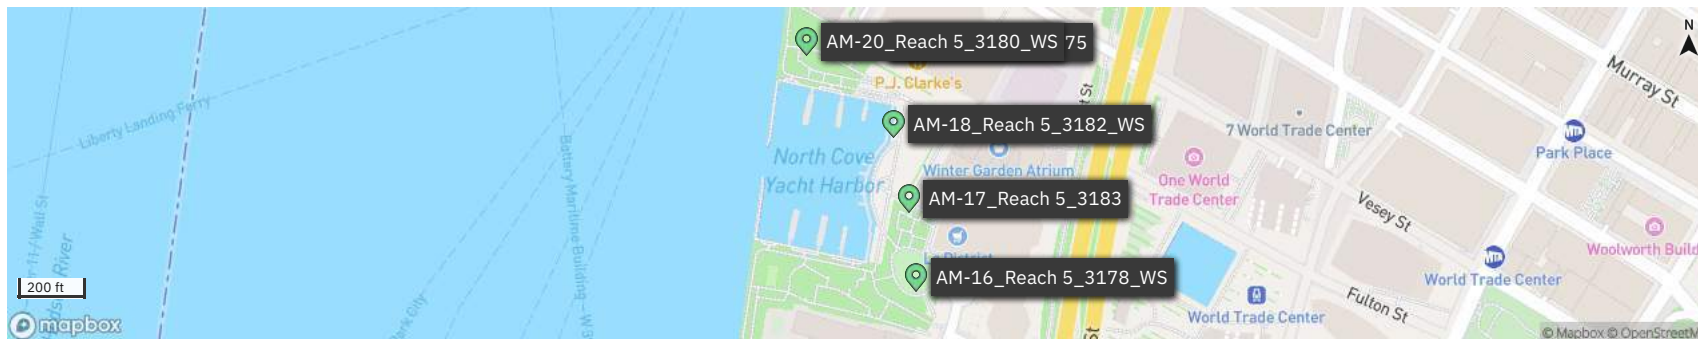


Stopped  Rolling Avg

Stopped  Rolling Avg

PM2.5 Average Contribution ( $\mu\text{g}/\text{m}^3$ )

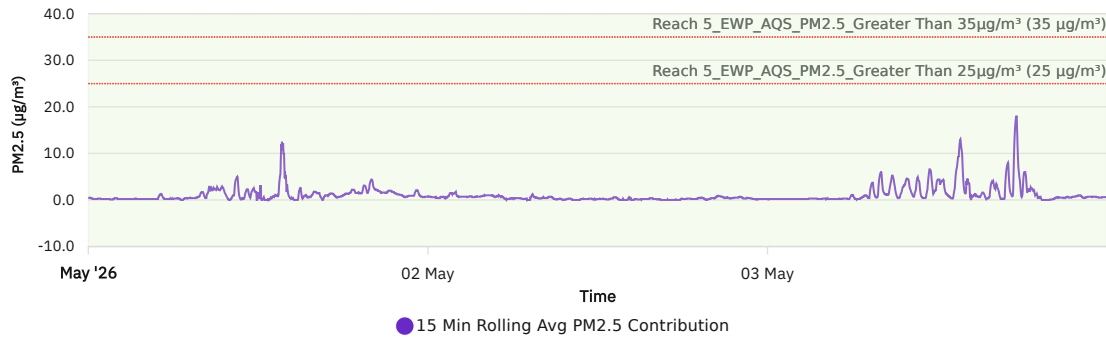


PM10 Average Contribution ( $\mu\text{g}/\text{m}^3$ )

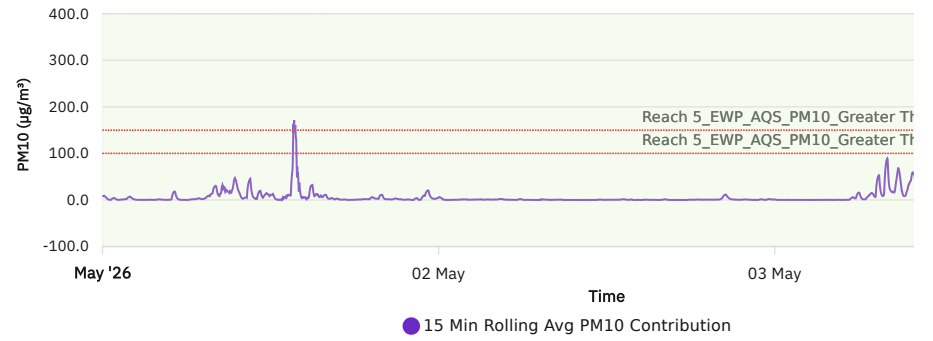


Stopped 
  Rolling Avg


VOC Average Contribution (ppm)

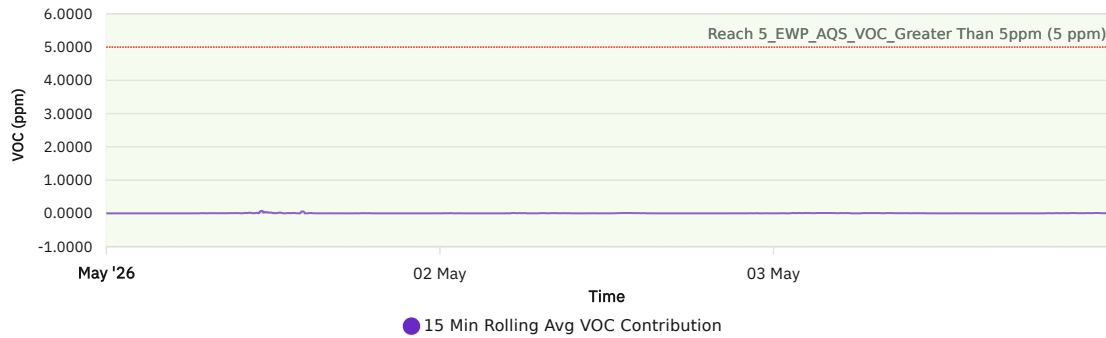


Wind rose (mph)

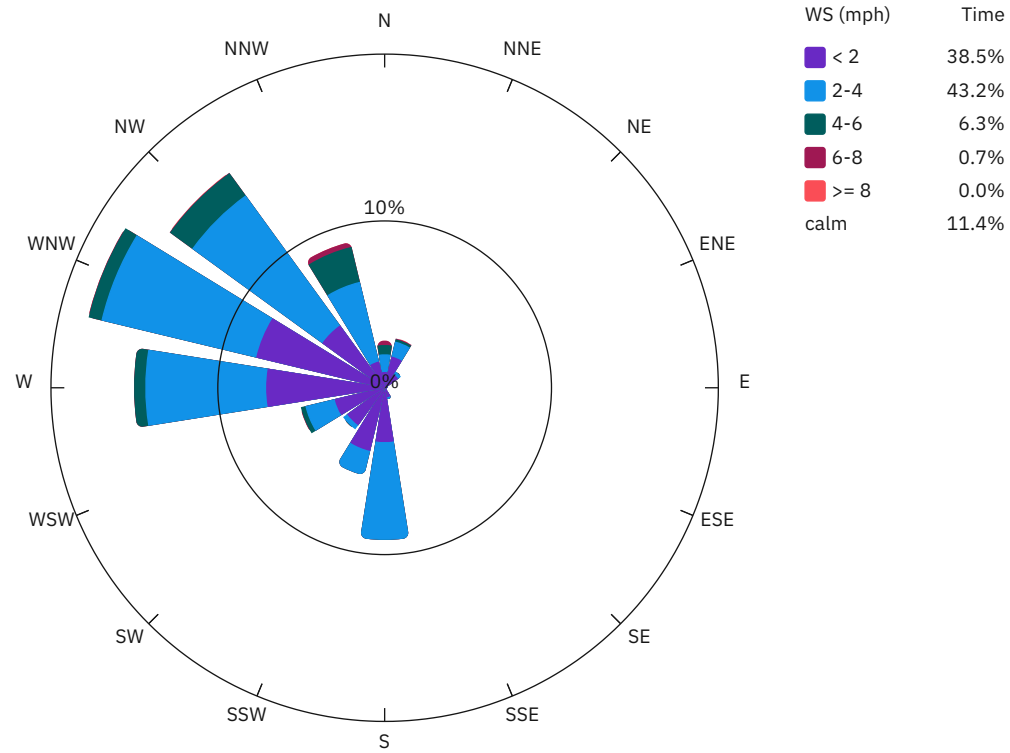


AM-16\_Reach 5\_3178\_WS

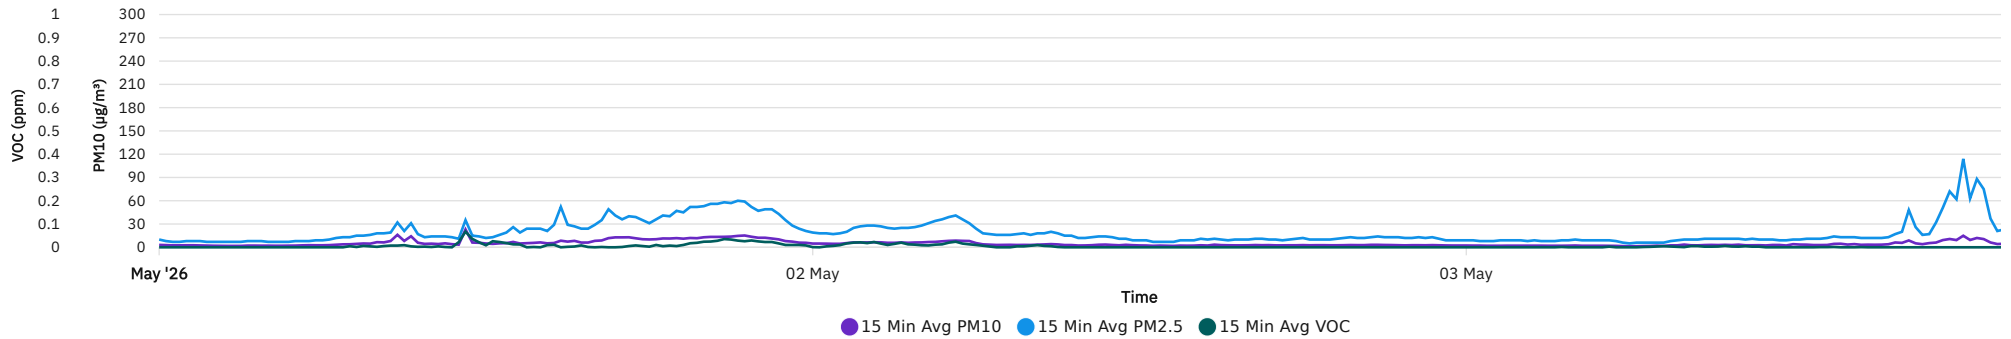


AM-17\_Reach 5\_3183

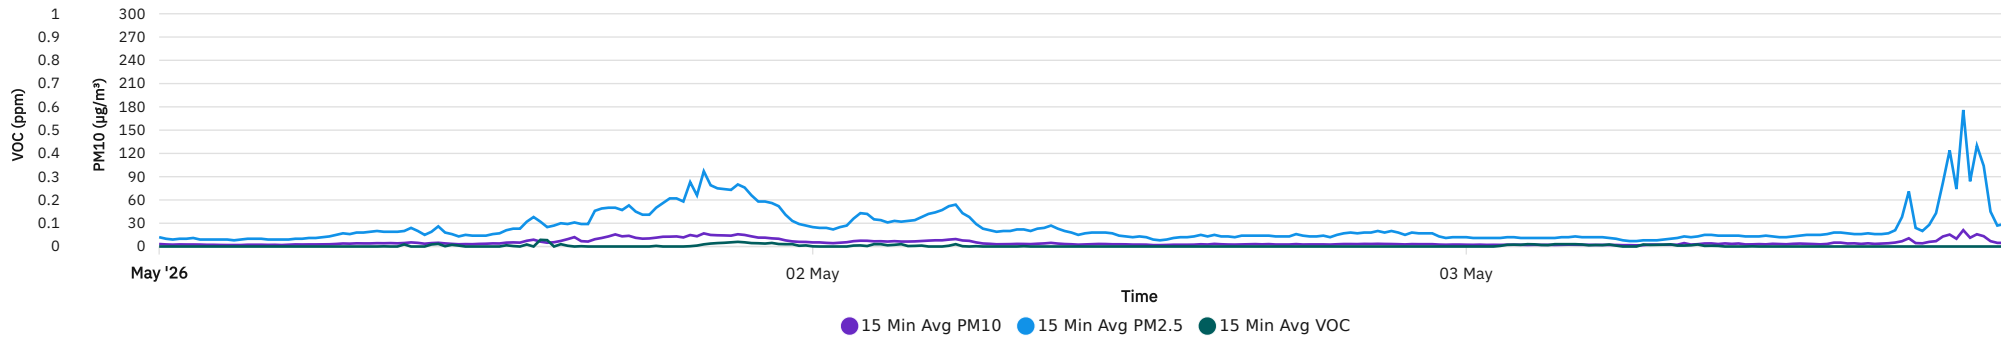


AM-18\_Reach 5\_3182\_WS

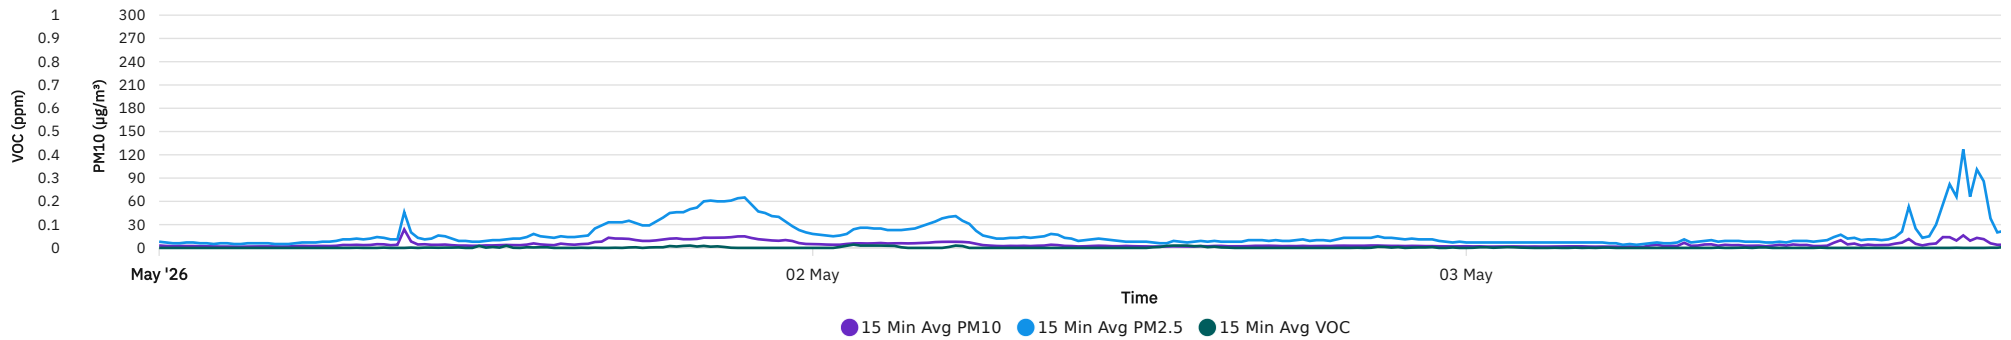

AM-19\_Reach 5\_3175

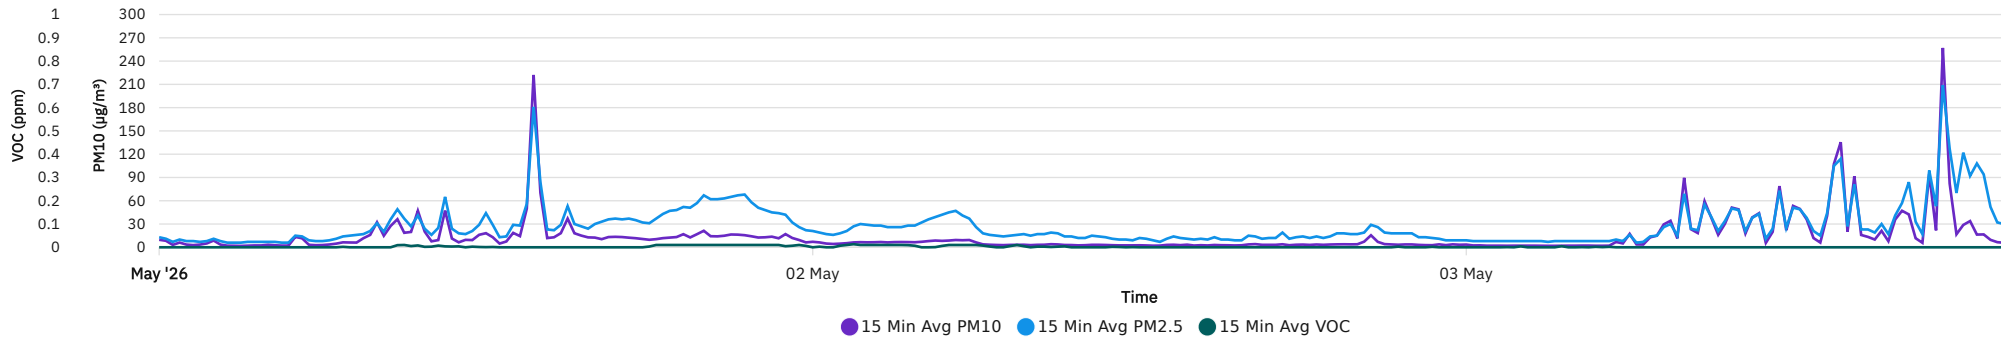

AM-20\_Reach 5\_3180\_WS

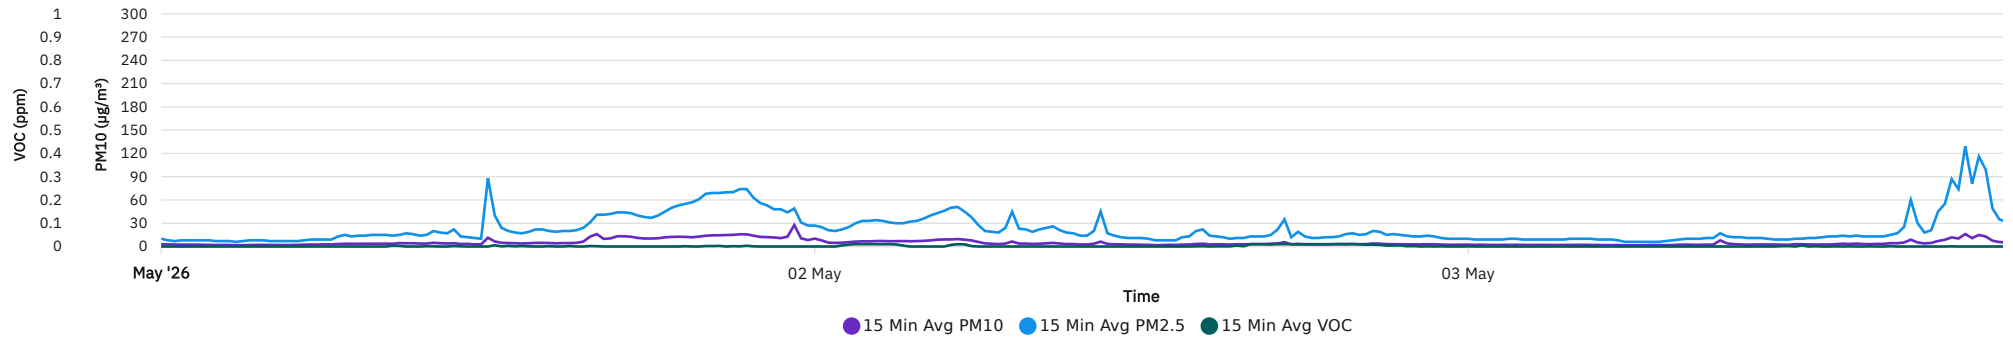

Exceedance Summary

Parameter	Action Level	Time Triggered	Cause	Mitigation
PM10	150.0 µg/m³	5/1/2026 13:36	Elevated readings were attributable to construction activities within the project area.	Contractor utilized a garden hose to mitigate dust levels and fugitive dust.
PM10	150.0 µg/m³	5/3/2026 13:27	Elevated readings were attributable to construction activities within the project area.	Contractor utilized a garden hose to mitigate dust levels and fugitive dust.
PM10	150.0 µg/m³	5/3/2026 17:24	Elevated readings were attributable to construction activities within the project area.	Contractor utilized a garden hose to mitigate dust levels and fugitive dust.

Reach 5_EWP_AQS Report		Battery Park_AQS	
		Report Period	
		From:	05/04/2026 00:00
		To:	05/10/2026 23:59
		PM10 Action Level:	100 µg/m³
		VOC Action Level:	5 ppm

Daily Environmental Summary	Temp (°F)	Relative Humidity (%)	Barometer (inHg)	Wind Speed (mph)	Prevailing Wind Direction
05/04/2026	49.3 - 70.9	0.0 - 41.3	26.5 - 32.6	0.5 - 9.0	S
05/05/2026	59.2 - 80.4	0.0 - 47.7	28.7 - 32.4	0.7 - 11.0	SE
05/06/2026	54.1 - 68.4	0.0 - 56.1	27.3 - 32.4	0.4 - 9.9	SE
05/07/2026	47.1 - 63.1	0.0 - 34.8	27.7 - 32.4	0.4 - 6.9	NNE
05/08/2026	48.2 - 65.5	0.0 - 40.2	27.0 - 32.5	0.3 - 7.6	NW
05/09/2026	54.3 - 63.7	0.0 - 74.6	26.5 - 32.7	0.2 - 4.8	SE
05/10/2026	52.7 - 67.1	0.0 - 65.7	28.2 - 32.6	0.2 - 8.6	SW

Daily Monitoring Summary	PM2.5 (µg/m³)	Time	PM10 (µg/m³)	Time	VOC (ppm)	Time
Min Contribution (15 min avg.) - 5/4/2026	0.0	13:45	0.0	13:45	0.0000	02:30
Max Contribution (15 min avg.) - 5/4/2026	16.3	21:15	169.2	21:15	0.0233	08:15
Daily Avg. Contribution (15 min avg.) - 5/4/2026	1.9	-	12.6	-	0.0035	-
Min Contribution (15 min avg.) - 5/5/2026	0.0	11:30	0.0	01:30	0.0000	00:30
Max Contribution (15 min avg.) - 5/5/2026	23.0	16:00	206.9	16:00	0.0867	14:45
Daily Avg. Contribution (15 min avg.) - 5/5/2026	3.9	-	24.7	-	0.0025	-
Min Contribution (15 min avg.) - 5/6/2026	0.0	13:30	0.0	12:30	0.0000	00:15
Max Contribution (15 min avg.) - 5/6/2026	7.5	07:45	96.7	07:45	0.1180	09:00
Daily Avg. Contribution (15 min avg.) - 5/6/2026	1.9	-	9.1	-	0.0089	-
Min Contribution (15 min avg.) - 5/7/2026	0.1	00:00	0.0	03:45	0.0000	00:00
Max Contribution (15 min avg.) - 5/7/2026	33.6	07:30	235.2	15:00	0.1427	09:15
Daily Avg. Contribution (15 min avg.) - 5/7/2026	2.9	-	19.0	-	0.0120	-
Min Contribution (15 min avg.) - 5/8/2026	0.0	02:15	0.0	03:15	0.0000	00:00
Max Contribution (15 min avg.) - 5/8/2026	18.3	16:15	223.8	16:15	0.0960	12:45
Daily Avg. Contribution (15 min avg.) - 5/8/2026	1.0	-	5.7	-	0.0106	-
Min Contribution (15 min avg.) - 5/9/2026	0.0	11:00	0.0	06:15	0.0000	00:00
Max Contribution (15 min avg.) - 5/9/2026	6.6	23:30	6.6	23:30	0.0153	16:15
Daily Avg. Contribution (15 min avg.) - 5/9/2026	1.9	-	1.7	-	0.0013	-
Min Contribution (15 min avg.) - 5/10/2026	0.0	19:00	0.0	19:00	0.0000	00:00
Max Contribution (15 min avg.) - 5/10/2026	25.1	12:00	27.0	12:00	0.0147	14:00
Daily Avg. Contribution (15 min avg.) - 5/10/2026	10.8	-	11.8	-	0.0019	-

AM-20\_Reach 5\_3180\_WS 75



AM-18\_Reach 5\_3182\_WS


AM-17\_Reach 5\_3183

AM-16\_Reach 5\_3178\_WS

200 ft

Stopped Rolling Avg


PM2.5 Average Contribution ( $\mu\text{g}/\text{m}^3$ )

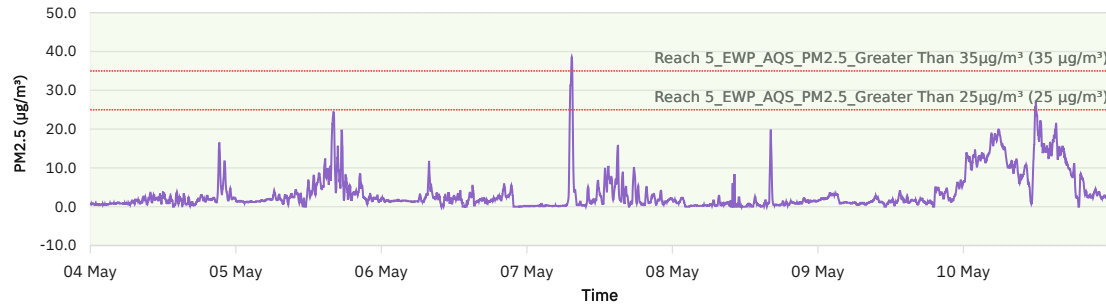

● 15 Min Rolling Avg PM2.5 Contribution

Stopped Rolling Avg


PM10 Average Contribution ( $\mu\text{g}/\text{m}^3$ )

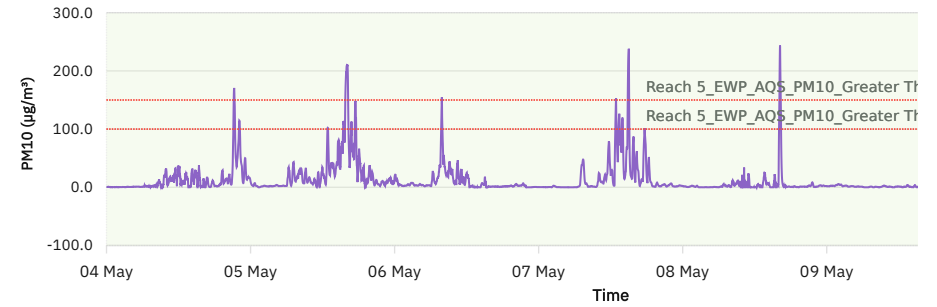

● 15 Min Rolling Avg PM10 Contribution


Stopped Rolling Avg

VOC Average Contribution (ppm)

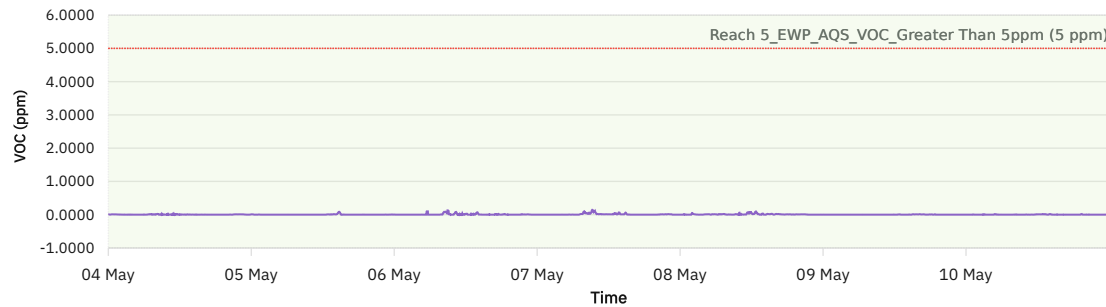


● 15 Min Rolling Avg VOC Contribution


Wind rose (mph)

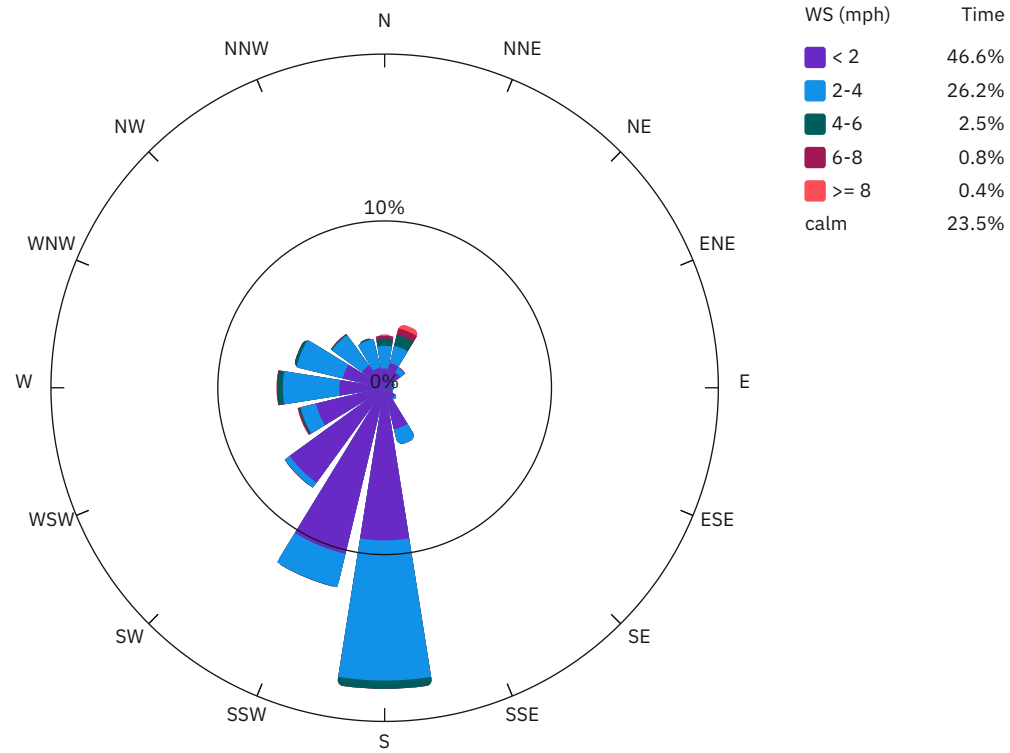


AM-16\_Reach 5\_3178\_WS

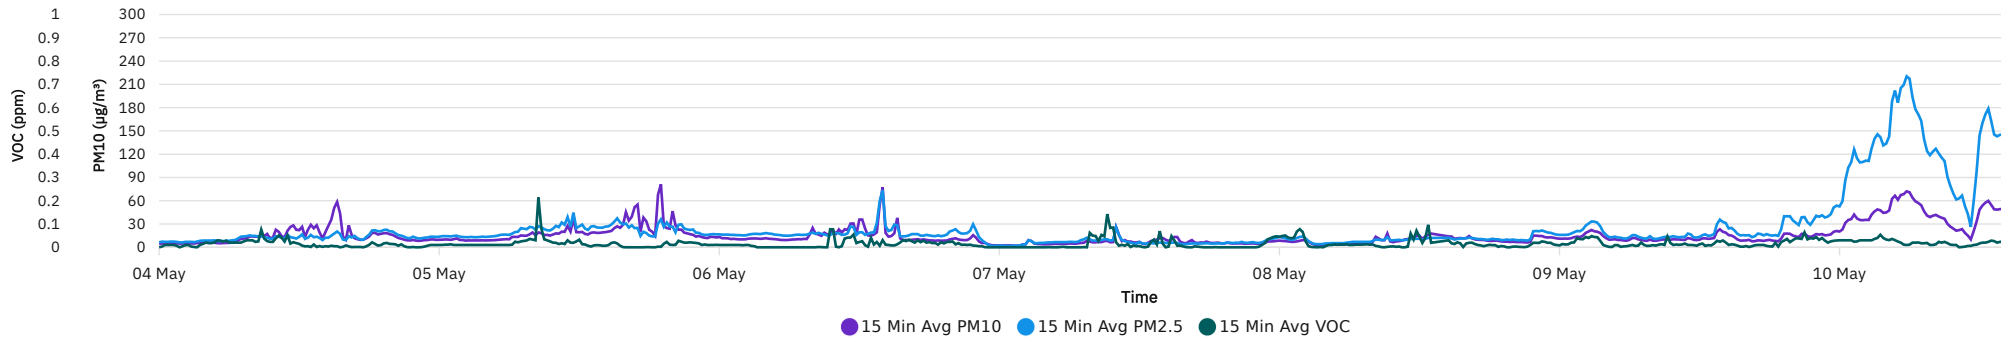


AM-17\_Reach 5\_3183

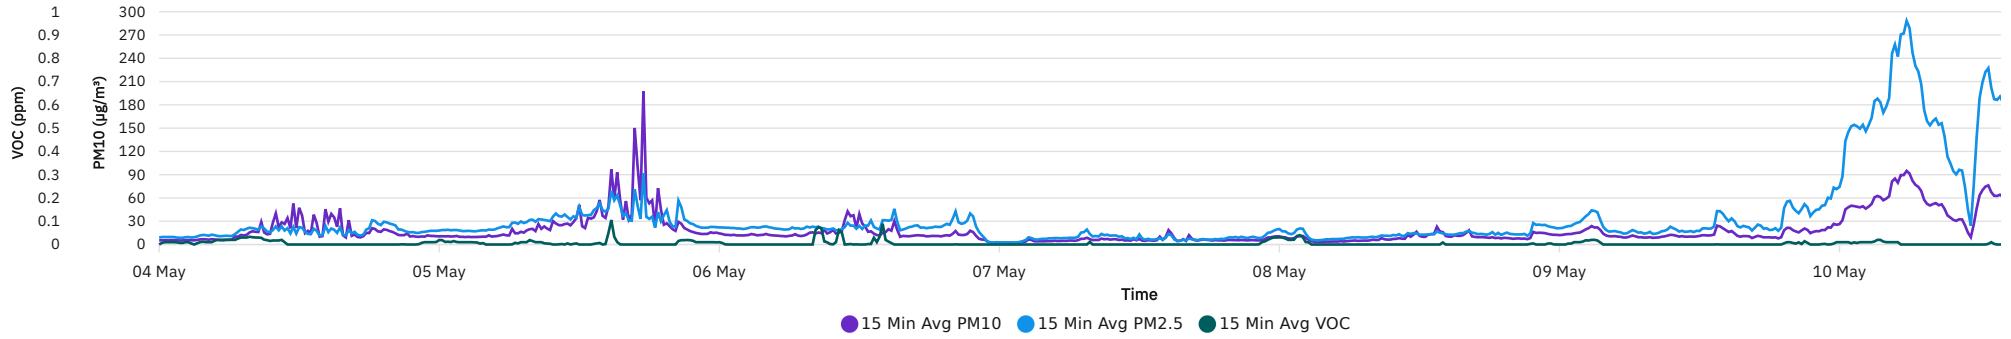


AM-18\_Reach 5\_3182\_WS

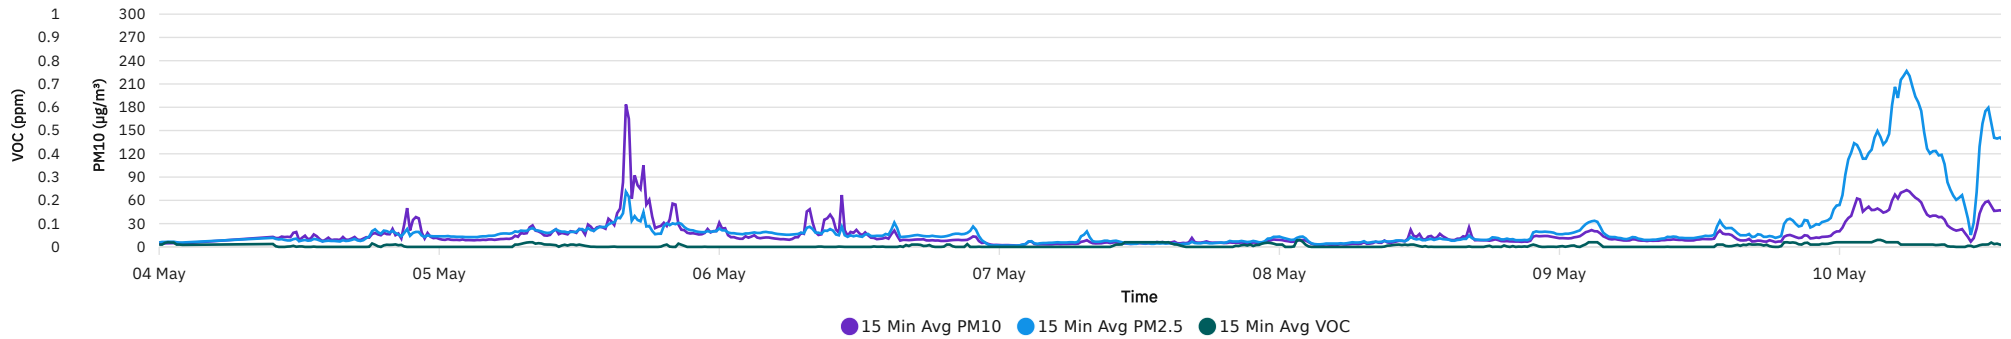

AM-19\_Reach 5\_3175

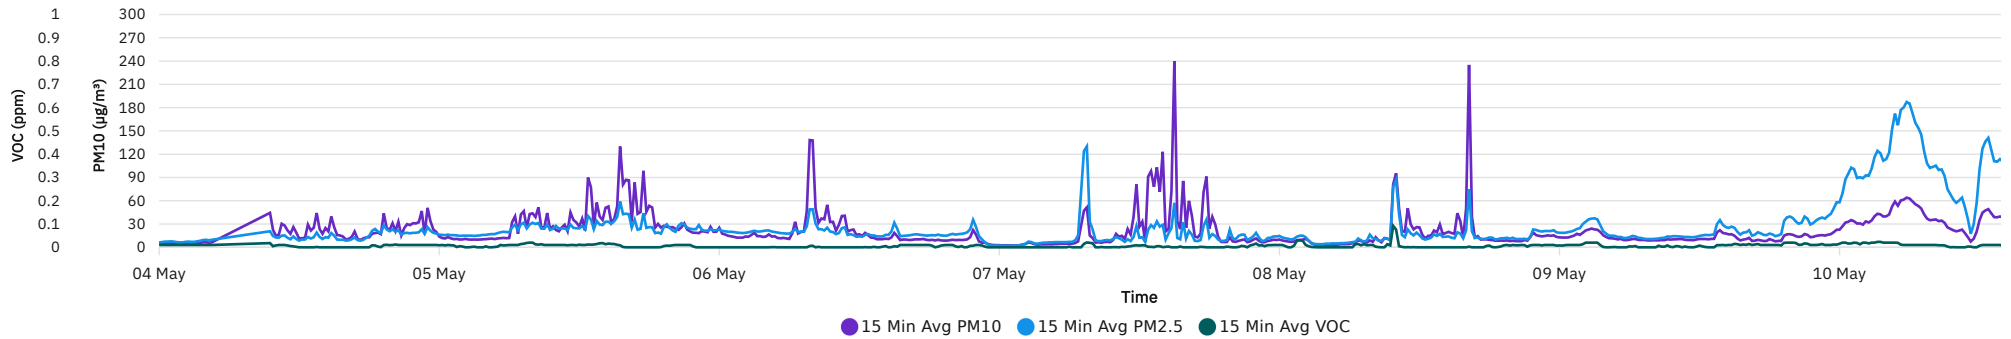

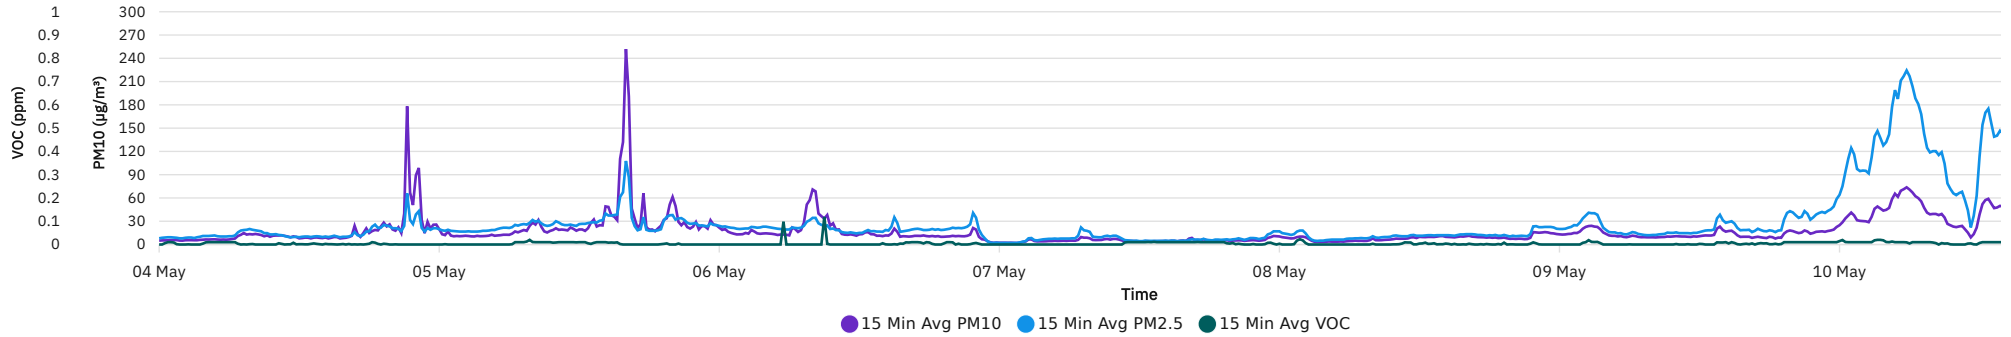

**Exceedance Summary**

Parameter	Action Level	Time Triggered	Cause	Mitigation
PM10	150.0 µg/m³	5/4/2026 21:08	Elevated readings were attributable to wind-blown dust across the site.	Contractor utilized a garden hose to mitigate dust levels and fugitive dust.
PM10	100.0 µg/m³	5/4/2026 22:04	Elevated readings were attributable to wind-blown dust across the site.	Contractor utilized a garden hose to mitigate dust levels and fugitive dust.
PM10	100.0 µg/m³	5/5/2026 12:50	Elevated readings were attributable to construction activities within the project area.	Contractor utilized a garden hose to mitigate dust levels and fugitive dust.
PM10	150.0 µg/m³	5/5/2026 15:25	Elevated readings were attributable to construction activities within the project area.	Contractor utilized a garden hose to mitigate dust levels and fugitive dust.
PM10	150.0 µg/m³	5/5/2026 15:44	Elevated readings were attributable to construction activities within the project area.	Contractor utilized a garden hose to mitigate dust levels and fugitive dust.
PM10	100.0 µg/m³	5/5/2026 16:48	Elevated readings were attributable to wind-blown dust across the site.	Contractor utilized a garden hose to mitigate dust levels and fugitive dust.
PM10	100.0 µg/m³	5/5/2026 17:22	Elevated readings were attributable to wind-blown dust across the site.	Contractor utilized a garden hose to mitigate dust levels and fugitive dust.
PM10	150.0 µg/m³	5/6/2026 07:46	Elevated readings were attributable to construction activities within the project area.	Contractor utilized a garden hose to mitigate dust levels and fugitive dust.
PM10	150.0 µg/m³	5/7/2026 12:47	Elevated readings were attributable to construction activities within the project area.	Contractor utilized a garden hose to mitigate dust levels and fugitive dust.
PM10	100.0 µg/m³	5/7/2026 13:19	Elevated readings were attributable to construction activities within the project area.	Contractor utilized a garden hose to mitigate dust levels and fugitive dust.
PM10	100.0 µg/m³	5/7/2026 13:52	Elevated readings were attributable to construction activities within the project area.	Contractor utilized a garden hose to mitigate dust levels and fugitive dust.
PM10	150.0 µg/m³	5/7/2026 14:49	Elevated readings were attributable to construction activities within the project area.	Contractor utilized a garden hose to mitigate dust levels and fugitive dust.
PM10	100.0 µg/m³	5/7/2026 17:39	Elevated readings were attributable to wind-blown dust across the site.	Contractor utilized a garden hose to mitigate dust levels and fugitive dust.
PM10	150.0 µg/m³	5/8/2026 16:04	Elevated readings were attributable to construction activities within the project area.	Contractor utilized a garden hose to mitigate dust levels and fugitive dust.
PM2.5	35.0 µg/m³	5/7/2026 07:06	Elevated readings were attributable to construction activities within the project area.	Contractor utilized a garden hose to mitigate dust levels and fugitive dust.
PM2.5	25.0 µg/m³	5/10/2026 11:49	Elevated readings were attributable to construction activities within the project area.	Contractor utilized a garden hose to mitigate dust levels and fugitive dust.



Reach 5\_EWP\_AQS Report


Battery Park\_AQS

Report Period

From:	05/11/2026 00:00
To:	05/17/2026 23:59
PM10 Action Level:	100 µg/m³
PM2.5 Action Level:	25 µg/m³
VOC Action Level:	5 ppm

Daily Environmental Summary	Temp (°F)	Relative Humidity (%)	Barometer (inHg)	Wind Speed (mph)	Prevailing Wind Direction
05/11/2026	53.4 - 63.5	0.0 - 32.0	27.7 - 32.8	0.2 - 6.3	W
05/12/2026	46.8 - 63.0	0.0 - 48.0	28.3 - 32.8	0.4 - 8.3	WSW
05/13/2026	53.1 - 71.4	0.0 - 59.6	28.5 - 32.7	0.5 - 6.8	SSE
05/14/2026	53.2 - 64.4	0.0 - 72.6	28.2 - 32.2	0.2 - 9.0	NNE
05/15/2026	50.4 - 64.8	0.0 - 60.0	26.7 - 32.4	0.5 - 10.4	NE
05/16/2026	55.6 - 77.4	0.0 - 61.6	28.3 - 32.9	0.2 - 8.9	SSW
05/17/2026	66.7 - 84.2	0.0 - 62.1	28.4 - 32.3	0.2 - 6.4	SW


Daily Monitoring Summary	PM2.5 (µg/m³)	Time	PM10 (µg/m³)	Time	VOC (ppm)	Time
Min Contribution (15 min avg.) - 5/11/2026	0.0	01:15	0.0	00:30	0.0000	00:15
Max Contribution (15 min avg.) - 5/11/2026	13.0	13:00	136.4	07:45	0.0713	13:00
Daily Avg. Contribution (15 min avg.) - 5/11/2026	1.5	-	9.2	-	0.0057	-
Min Contribution (15 min avg.) - 5/12/2026	0.0	09:00	0.0	09:30	0.0000	04:00
Max Contribution (15 min avg.) - 5/12/2026	44.9	12:00	211.1	11:45	0.0893	13:15
Daily Avg. Contribution (15 min avg.) - 5/12/2026	2.1	-	15.3	-	0.0070	-
Min Contribution (15 min avg.) - 5/13/2026	0.0	06:15	0.0	06:00	0.0000	01:00
Max Contribution (15 min avg.) - 5/13/2026	16.8	13:45	175.2	13:45	0.0940	09:15
Daily Avg. Contribution (15 min avg.) - 5/13/2026	1.9	-	14.6	-	0.0021	-
Min Contribution (15 min avg.) - 5/14/2026	0.0	07:15	0.0	00:30	0.0000	00:00
Max Contribution (15 min avg.) - 5/14/2026	9.4	13:15	99.6	18:45	0.0307	10:30
Daily Avg. Contribution (15 min avg.) - 5/14/2026	1.2	-	9.7	-	0.0047	-
Min Contribution (15 min avg.) - 5/15/2026	0.0	17:30	0.0	19:30	0.0000	02:00
Max Contribution (15 min avg.) - 5/15/2026	17.7	13:45	145.1	13:45	0.0140	21:00
Daily Avg. Contribution (15 min avg.) - 5/15/2026	2.1	-	21.7	-	0.0029	-
Min Contribution (15 min avg.) - 5/16/2026	0.0	17:00	0.0	00:00	0.0000	01:15
Max Contribution (15 min avg.) - 5/16/2026	4.3	19:00	35.5	22:30	0.0707	11:00
Daily Avg. Contribution (15 min avg.) - 5/16/2026	1.2	-	4.0	-	0.0034	-
Min Contribution (15 min avg.) - 5/17/2026	0.0	06:00	0.0	04:15	0.0000	00:00
Max Contribution (15 min avg.) - 5/17/2026	7.1	17:30	10.3	18:00	0.0293	14:15
Daily Avg. Contribution (15 min avg.) - 5/17/2026	2.1	-	2.6	-	0.0052	-





Stopped Rolling Avg


PM2.5 Average Contribution ( $\mu\text{g}/\text{m}^3$ )

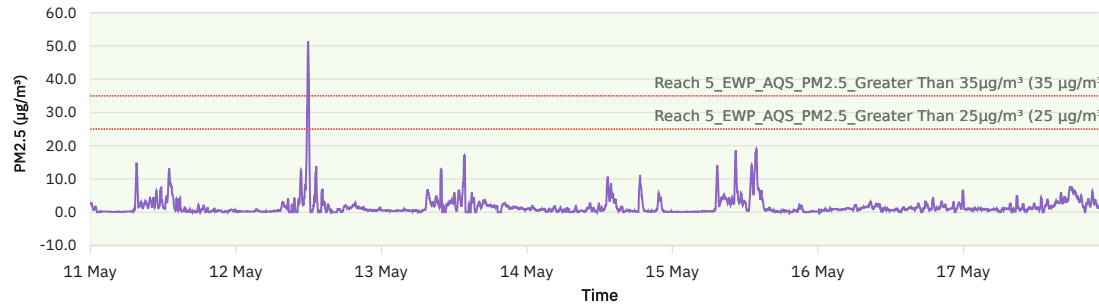

● 15 Min Rolling Avg PM2.5 Contribution

Stopped Rolling Avg


PM10 Average Contribution ( $\mu\text{g}/\text{m}^3$ )

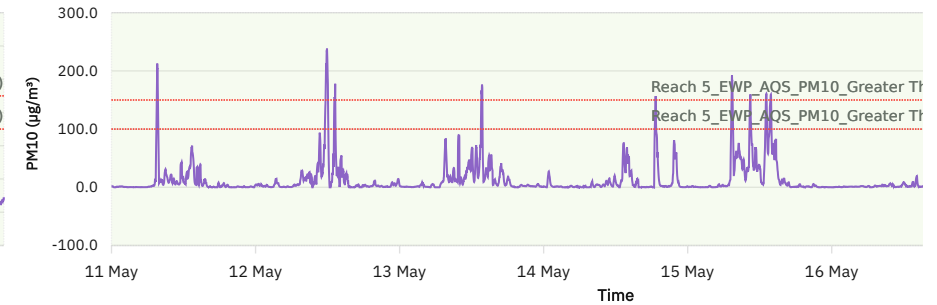

● 15 Min Rolling Avg PM10 Contribution


Stopped Rolling Avg

VOC Average Contribution (ppm)

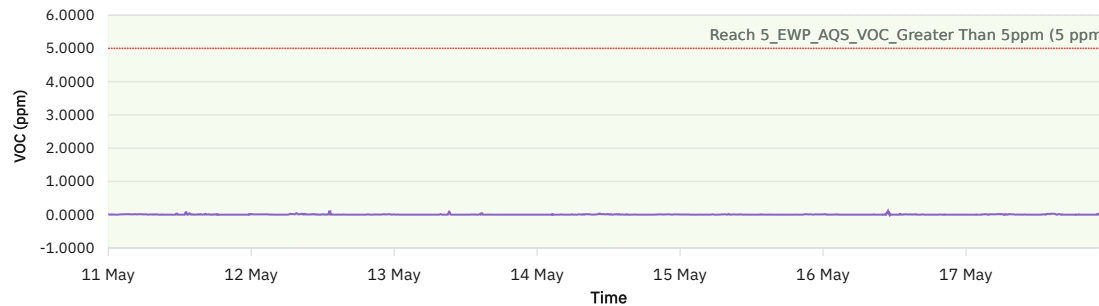


● 15 Min Rolling Avg VOC Contribution


Wind rose (mph)

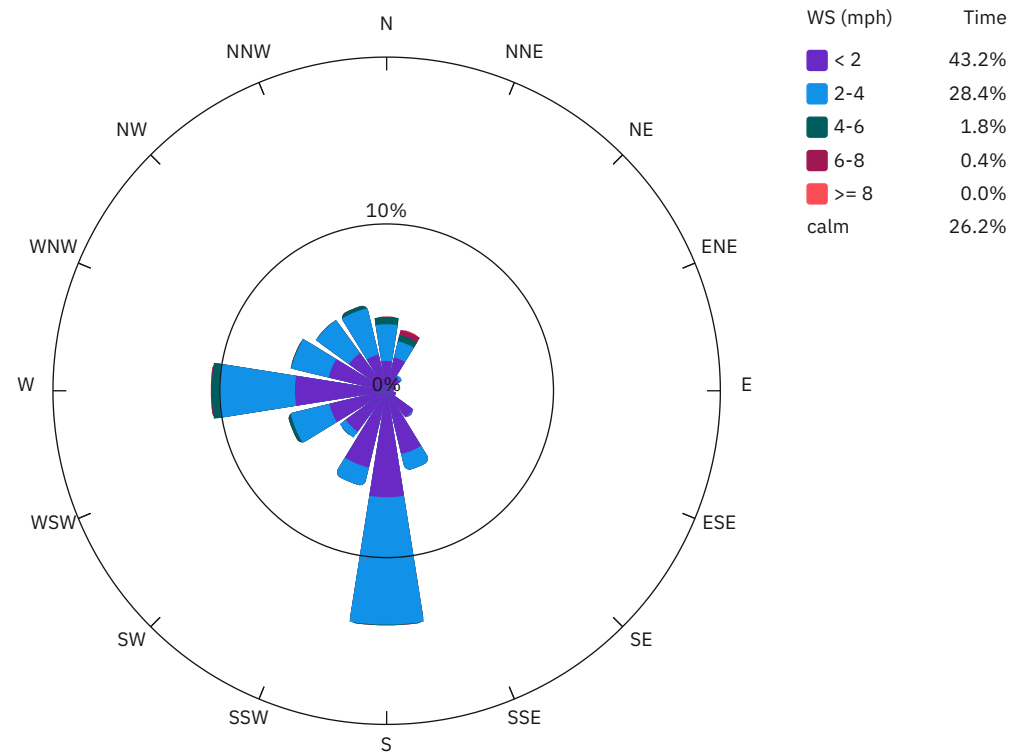


AM-16\_Reach 5\_3178\_WS

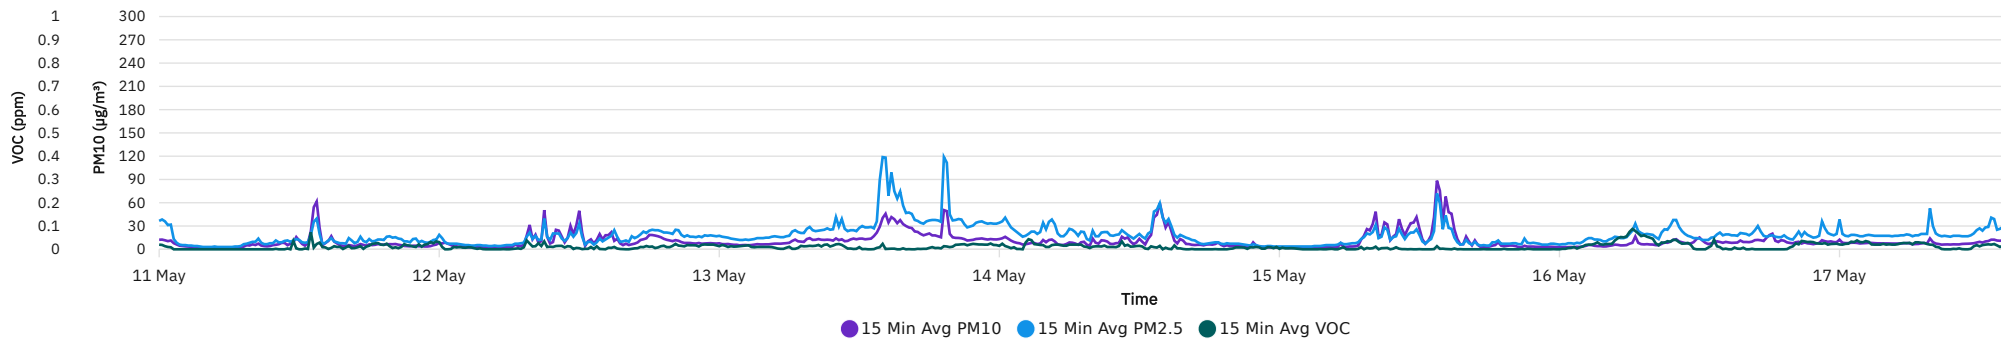


AM-17\_Reach 5\_3183

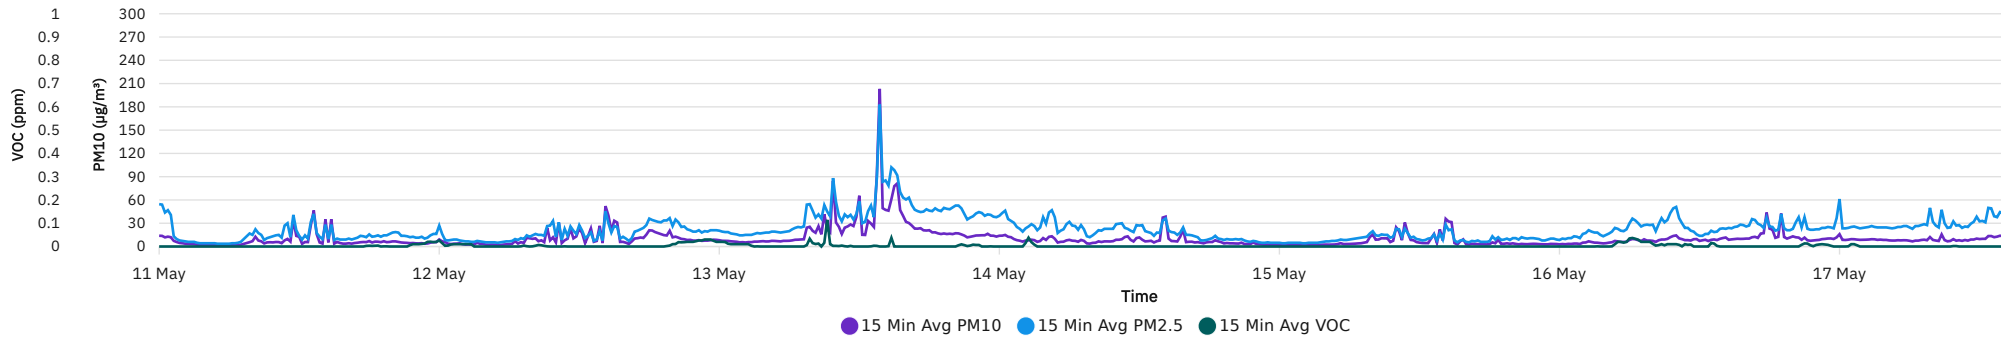


AM-18\_Reach 5\_3182\_WS

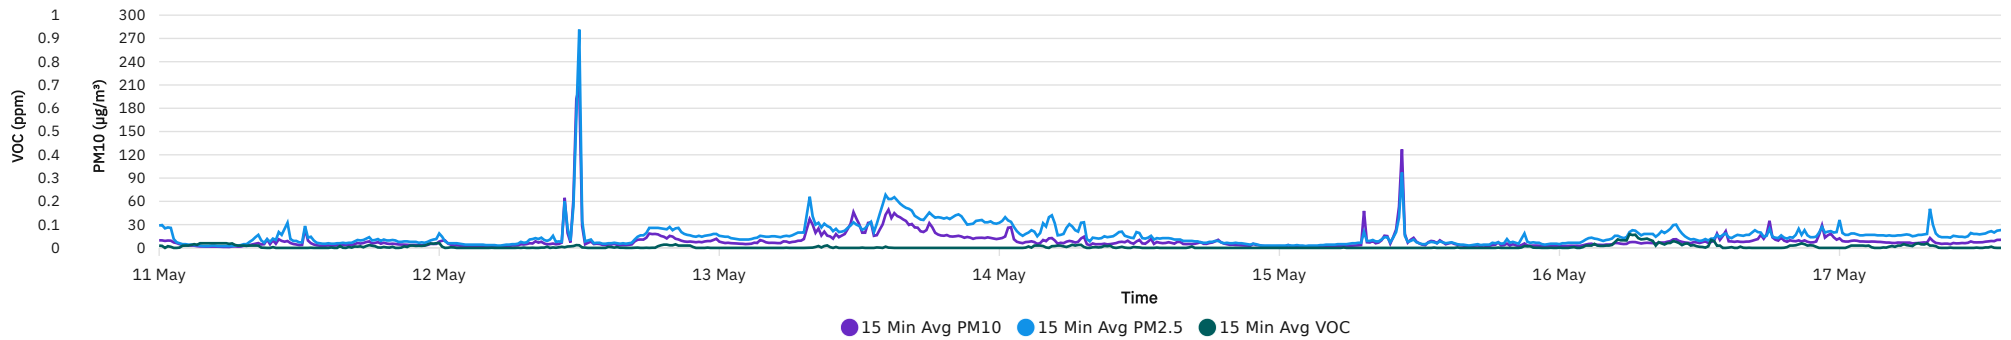

AM-19\_Reach 5\_3175

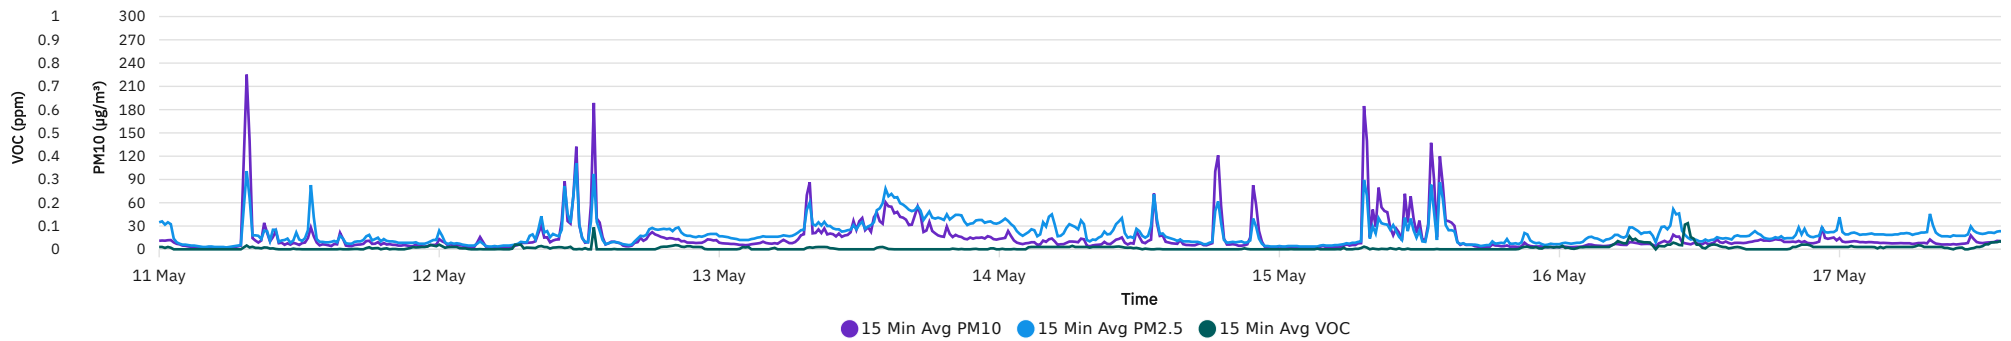

AM-20\_Reach 5\_3180\_WS

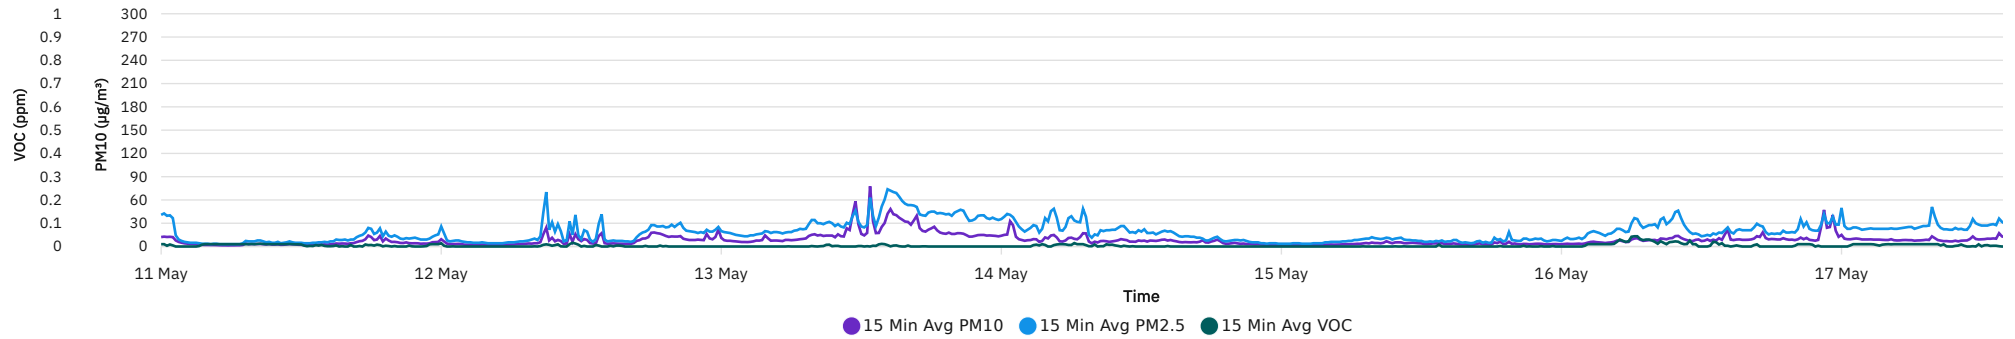

Exceedance Summary

Parameter	Action Level	Time Triggered	Cause	Mitigation
PM10	150.0 µg/m³	5/11/2026 07:29	Elevated readings were attributable to construction activities within the project area.	Contractor utilized a garden hose to mitigate dust levels and fugitive dust.
PM10	150.0 µg/m³	5/12/2026 11:33	Elevated readings were attributable to construction activities within the project area.	Contractor utilized a garden hose to mitigate dust levels and fugitive dust.
PM10	100.0 µg/m³	5/12/2026 13:04	Elevated readings were attributable to construction activities within the project area.	Contractor utilized a garden hose to mitigate dust levels and fugitive dust.
PM10	150.0 µg/m³	5/13/2026 13:33	Elevated readings were attributable to construction activities within the project area.	Contractor utilized a garden hose to mitigate dust levels and fugitive dust.
PM10	150.0 µg/m³	5/14/2026 18:31	Elevated readings were attributable to construction activities within the project area.	Contractor utilized a garden hose to mitigate dust levels and fugitive dust.
PM10	150.0 µg/m³	5/15/2026 07:15	Elevated readings were attributable to construction activities within the project area.	Contractor utilized a garden hose to mitigate dust levels and fugitive dust.
PM10	150.0 µg/m³	5/15/2026 10:18	Elevated readings were attributable to construction activities within the project area.	Contractor utilized a garden hose to mitigate dust levels and fugitive dust.
PM10	150.0 µg/m³	5/15/2026 12:57	Elevated readings were attributable to construction activities within the project area.	Contractor utilized a garden hose to mitigate dust levels and fugitive dust.
PM10	150.0 µg/m³	5/15/2026 13:39	Elevated readings were attributable to construction activities within the project area.	Contractor utilized a garden hose to mitigate dust levels and fugitive dust.
PM2.5	35.0 µg/m³	5/12/2026 11:43	Elevated readings were attributable to construction activities within the project area.	Contractor utilized a garden hose to mitigate dust levels and fugitive dust.



Reach 5\_EWP\_AQS Report


Battery Park\_AQS

Report Period

From:	05/18/2026 00:00
To:	05/24/2026 23:59
PM10 Action Level:	100 µg/m³
PM2.5 Action Level:	25 µg/m³
VOC Action Level:	5 ppm

Daily Environmental Summary	Temp (°F)	Relative Humidity (%)	Barometer (inHg)	Wind Speed (mph)	Prevailing Wind Direction
05/18/2026	63.7 - 82.8	0.0 - 64.6	27.9 - 41.5	0.3 - 6.7	SSW
05/19/2026	73.0 - 91.6	0.0 - 66.8	28.1 - 32.7	0.4 - 6.5	S
05/20/2026	66.4 - 90.0	0.0 - 56.8	28.5 - 32.3	0.3 - 7.7	NNE
05/21/2026	54.1 - 66.4	0.0 - 51.5	26.9 - 32.7	0.2 - 5.4	NNE
05/22/2026	55.9 - 66.4	0.0 - 44.5	28.6 - 32.8	0.3 - 8.8	E
05/23/2026	47.7 - 59.2	0.0 - 49.1	27.6 - 32.9	0.2 - 5.6	ENE
05/24/2026	48.9 - 55.0	0.0 - 86.8	26.9 - 33.1	0.3 - 5.7	ENE


Daily Monitoring Summary	PM2.5 (µg/m³)	Time	PM10 (µg/m³)	Time	VOC (ppm)	Time
Min Contribution (15 min avg.) - 5/18/2026	1.6	06:15	0.0	06:45	0.0000	00:00
Max Contribution (15 min avg.) - 5/18/2026	34.1	14:15	340.7	14:15	0.0580	10:45
Daily Avg. Contribution (15 min avg.) - 5/18/2026	7.2	-	23.1	-	0.0061	-
Min Contribution (15 min avg.) - 5/19/2026	0.4	07:45	0.0	07:45	0.0000	00:00
Max Contribution (15 min avg.) - 5/19/2026	20.7	14:00	127.9	17:00	0.0080	22:15
Daily Avg. Contribution (15 min avg.) - 5/19/2026	6.1	-	17.1	-	0.0007	-
Min Contribution (15 min avg.) - 5/20/2026	0.0	08:30	0.0	08:30	0.0000	00:15
Max Contribution (15 min avg.) - 5/20/2026	18.5	18:30	242.4	18:30	0.0553	20:45
Daily Avg. Contribution (15 min avg.) - 5/20/2026	2.9	-	15.1	-	0.0037	-
Min Contribution (15 min avg.) - 5/21/2026	0.0	10:15	0.0	00:15	0.0000	00:00
Max Contribution (15 min avg.) - 5/21/2026	3.9	09:45	21.1	09:45	0.0173	10:30
Daily Avg. Contribution (15 min avg.) - 5/21/2026	0.7	-	2.0	-	0.0054	-
Min Contribution (15 min avg.) - 5/22/2026	0.0	08:45	0.0	02:15	0.0000	00:00
Max Contribution (15 min avg.) - 5/22/2026	6.1	10:30	71.8	10:30	0.0113	12:00
Daily Avg. Contribution (15 min avg.) - 5/22/2026	1.1	-	6.0	-	0.0028	-
Min Contribution (15 min avg.) - 5/23/2026	0.1	09:30	0.0	06:30	0.0000	00:00
Max Contribution (15 min avg.) - 5/23/2026	2.1	04:15	7.8	04:30	0.0353	03:15
Daily Avg. Contribution (15 min avg.) - 5/23/2026	0.9	-	0.9	-	0.0014	-
Min Contribution (15 min avg.) - 5/24/2026	0.1	08:30	0.0	08:15	0.0000	00:00
Max Contribution (15 min avg.) - 5/24/2026	3.6	18:15	4.2	20:15	0.0080	02:30
Daily Avg. Contribution (15 min avg.) - 5/24/2026	1.1	-	1.2	-	0.0003	-





Stopped Rolling Avg


PM2.5 Average Contribution ( $\mu\text{g}/\text{m}^3$ )

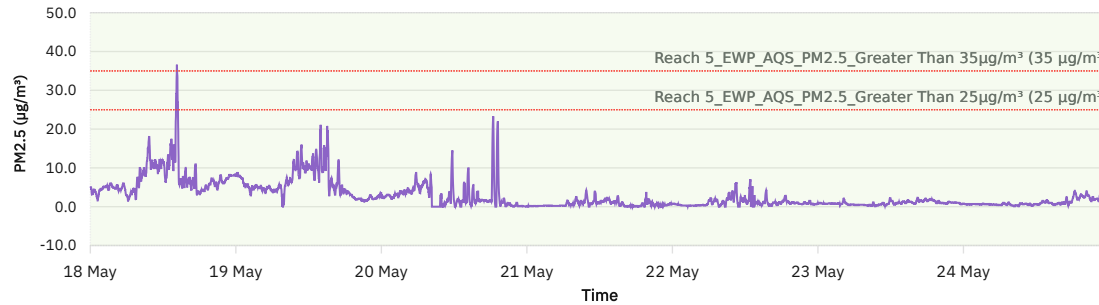

● 15 Min Rolling Avg PM2.5 Contribution

Stopped Rolling Avg


PM10 Average Contribution ( $\mu\text{g}/\text{m}^3$ )

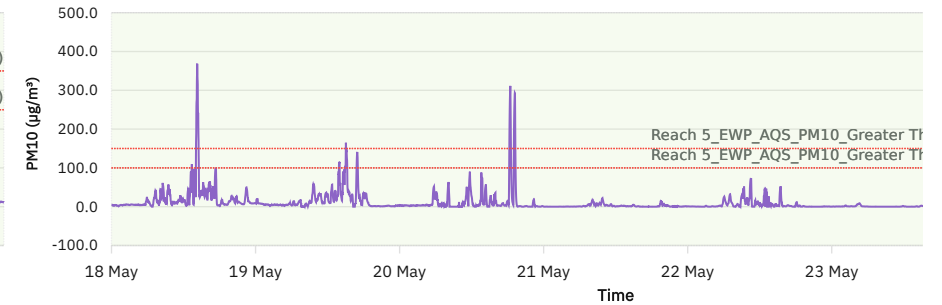

● 15 Min Rolling Avg PM10 Contribution


Stopped Rolling Avg

VOC Average Contribution (ppm)

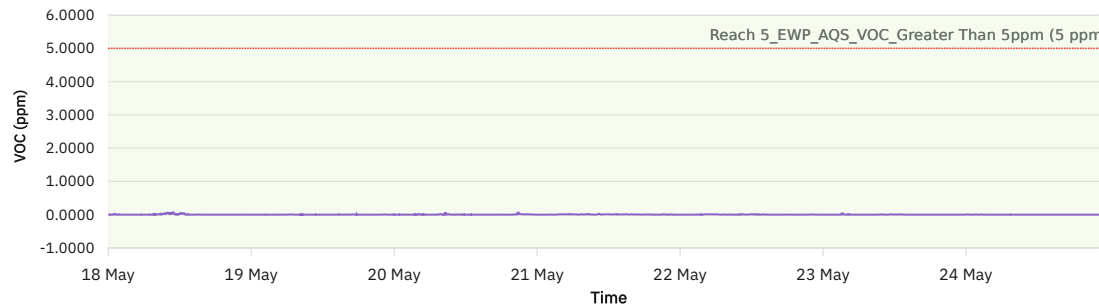


● 15 Min Rolling Avg VOC Contribution


Wind rose (mph)

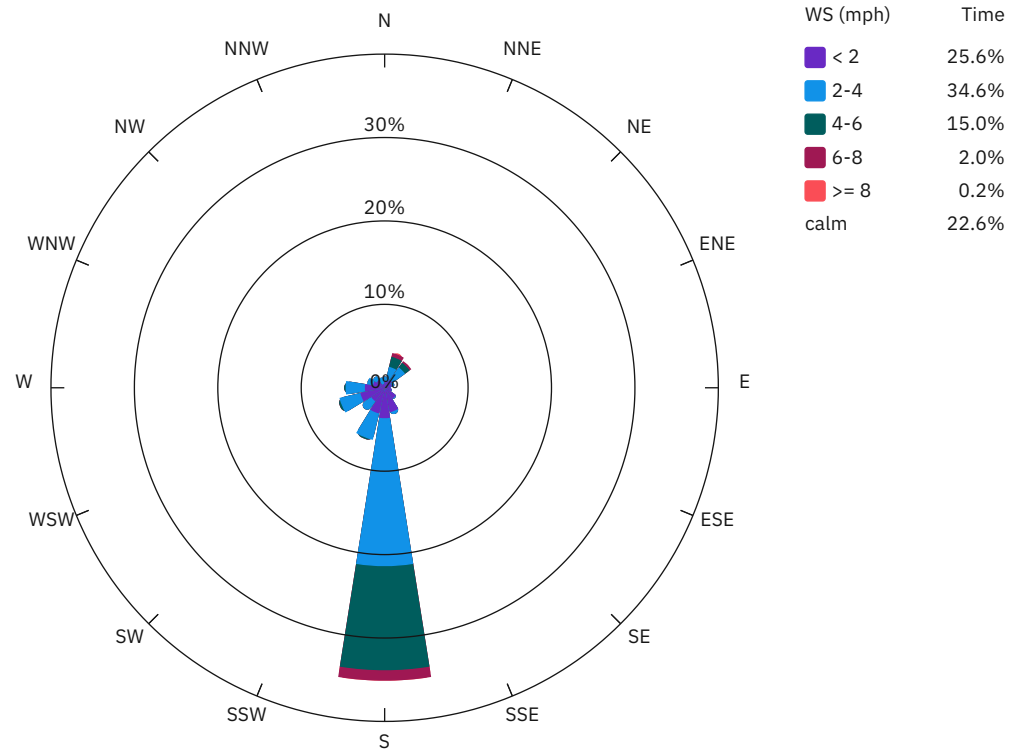


AM-16\_Reach 5\_3178\_WS

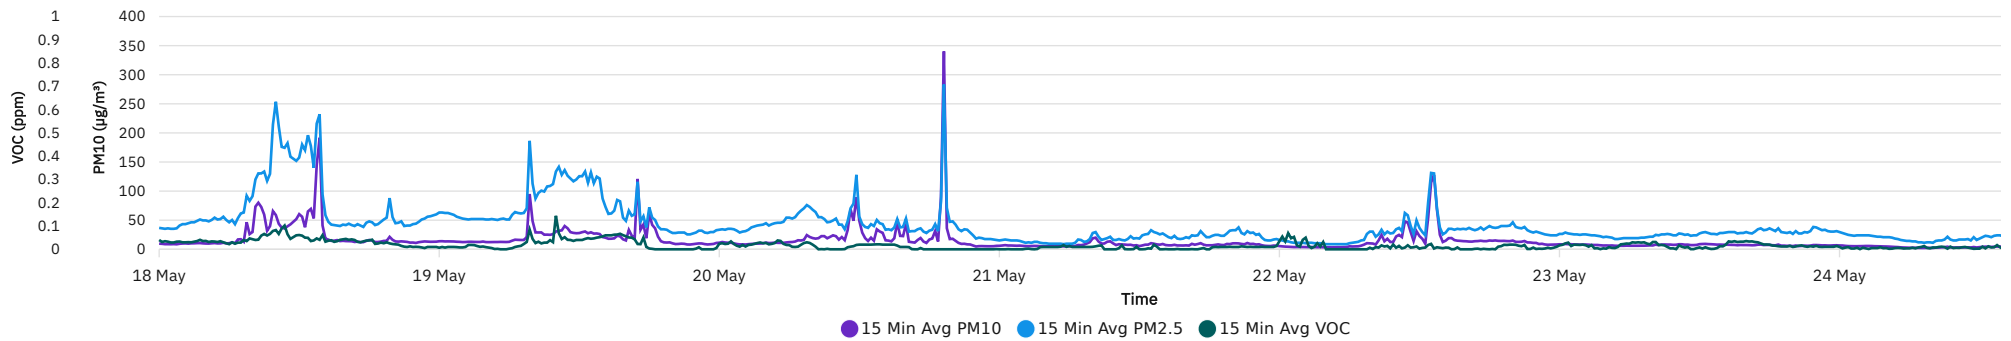


AM-17\_Reach 5\_3183

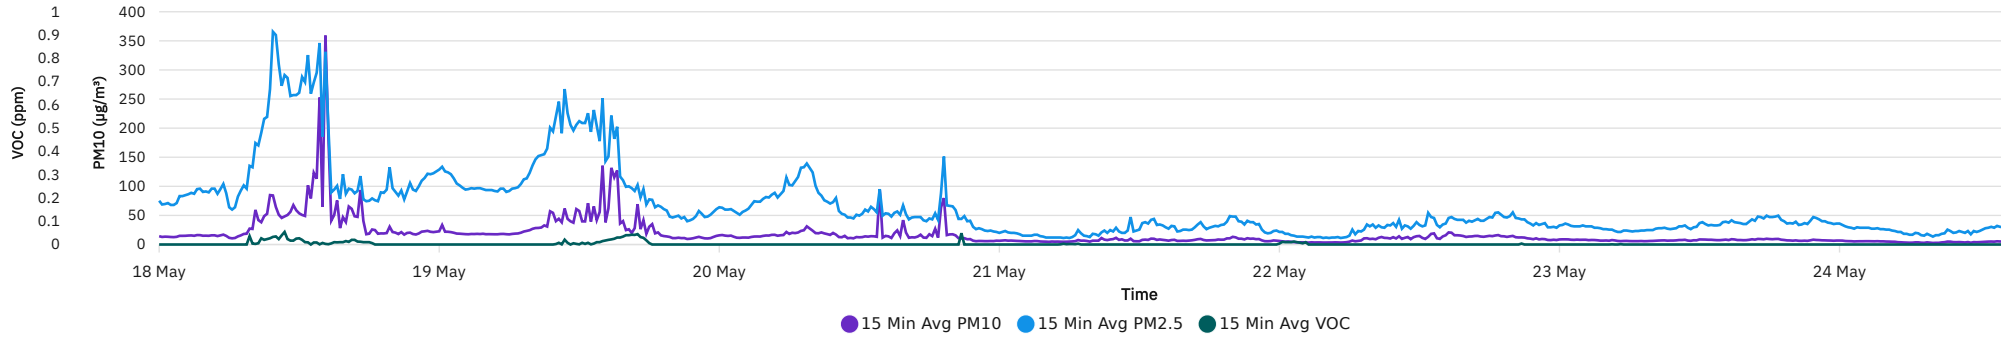


AM-18\_Reach 5\_3182\_WS

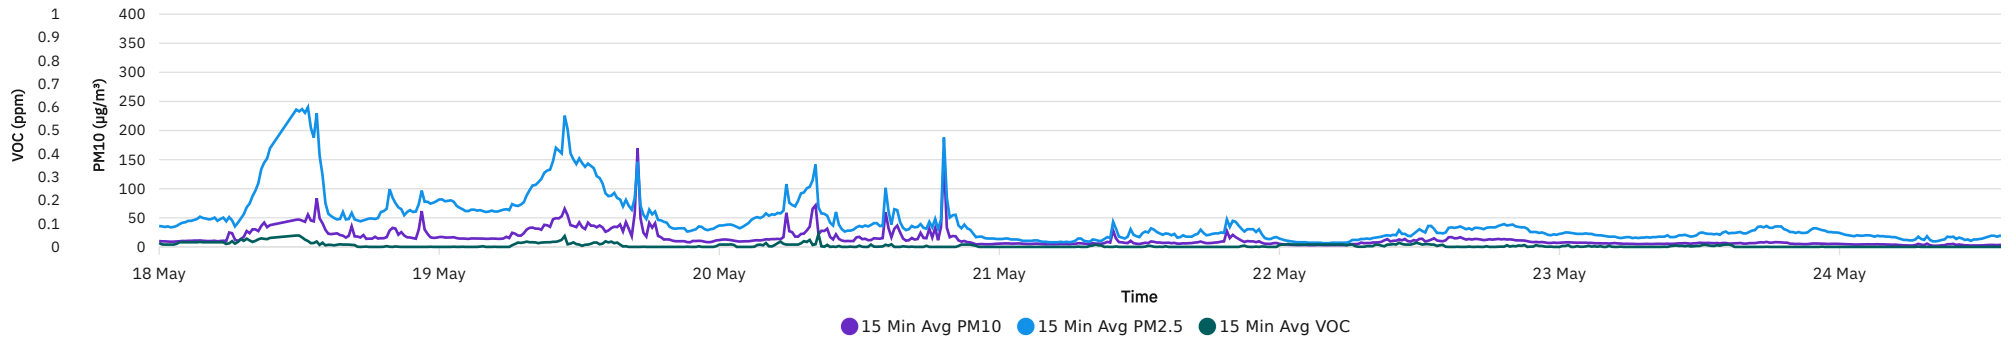

AM-19\_Reach 5\_3175

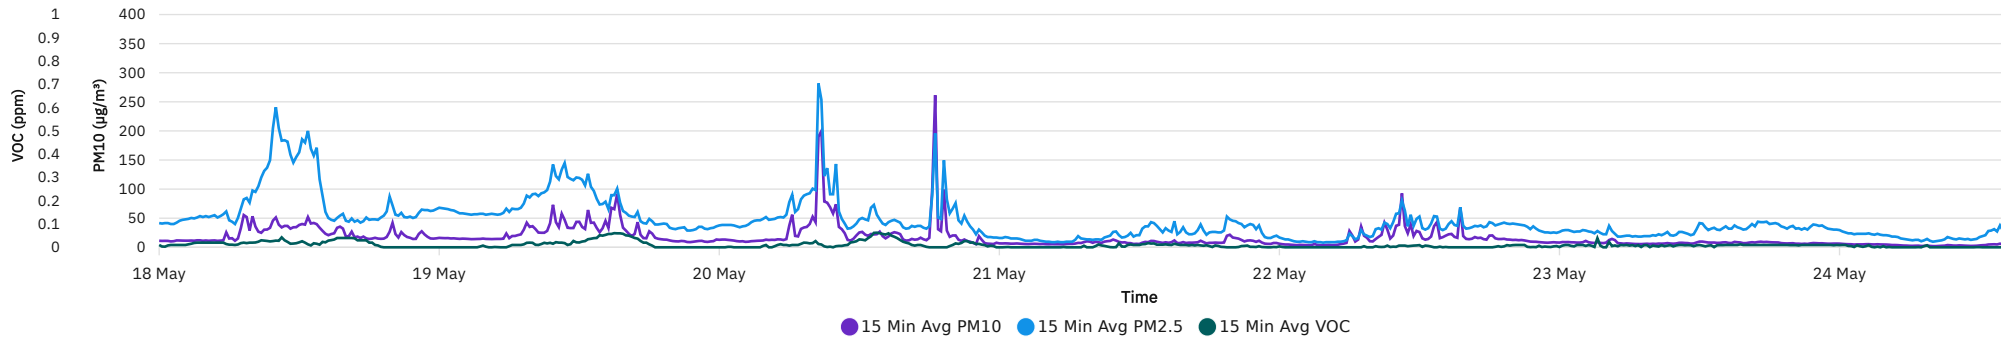

AM-20\_Reach 5\_3180\_WS

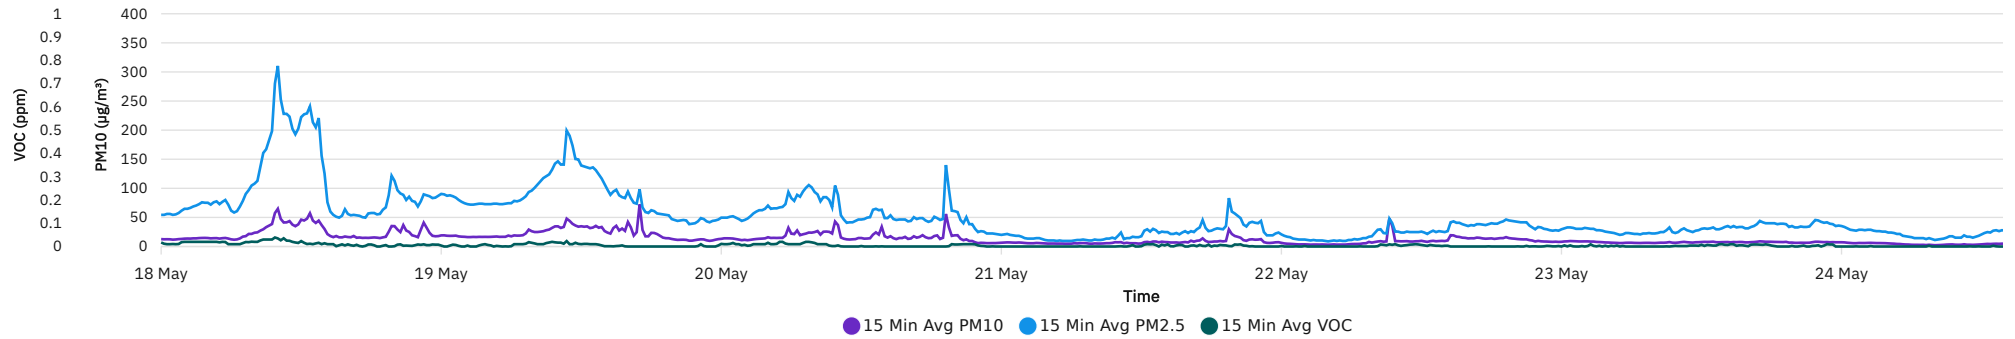

Exceedance Summary

Parameter	Action Level	Time Triggered	Cause	Mitigation
PM10	100.0 µg/m³	5/18/2026 13:22	Elevated readings were attributable to wind-blown dust across the site.	Contractor wetted the area to mitigate dust levels and fugitive dust.
PM10	150.0 µg/m³	5/18/2026 14:04	Elevated readings were attributable to wind-blown dust across the site.	Contractor wetted the area to mitigate dust levels and fugitive dust.
PM10	100.0 µg/m³	5/19/2026 13:54	Elevated readings were attributable to wind-blown dust across the site.	Contractor wetted the area to mitigate dust levels and fugitive dust.
PM10	150.0 µg/m³	5/19/2026 14:56	Elevated readings were attributable to wind-blown dust across the site.	Contractor wetted the area to mitigate dust levels and fugitive dust.
PM10	100.0 µg/m³	5/19/2026 16:50	Elevated readings were attributable to wind-blown dust across the site.	Contractor wetted the area to mitigate dust levels and fugitive dust.
PM10	150.0 µg/m³	5/20/2026 18:16	Elevated readings were attributable to wind-blown dust across the site.	Contractor wetted the area to mitigate dust levels and fugitive dust.
PM10	150.0 µg/m³	5/20/2026 19:01	Elevated readings were attributable to wind-blown dust across the site.	Contractor wetted the area to mitigate dust levels and fugitive dust.
PM2.5	25.0 µg/m³	5/18/2026 14:08	Elevated readings were attributable to wind-blown dust across the site.	Contractor wetted the area to mitigate dust levels and fugitive dust.



Reach 5\_EWP\_AQS Report


Battery Park\_AQS

Report Period

From:	05/25/2026 00:00
To:	05/31/2026 23:59
PM10 Action Level:	100 µg/m³
PM2.5 Action Level:	25 µg/m³
VOC Action Level:	5 ppm

Daily Environmental Summary	Temp (°F)	Relative Humidity (%)	Barometer (inHg)	Wind Speed (mph)	Prevailing Wind Direction
05/25/2026	54.5 - 70.0	0.0 - 0.0	27.6 - 32.6	0.2 - 5.5	S
05/26/2026	61.0 - 75.0	0.0 - 66.9	26.9 - 32.8	0.2 - 6.8	WSW
05/27/2026	67.3 - 79.3	0.0 - 65.5	28.1 - 32.5	0.2 - 7.9	SSE
05/28/2026	62.4 - 76.6	0.0 - 51.8	28.7 - 32.3	0.6 - 9.9	NE
05/29/2026	58.5 - 75.0	0.0 - 53.7	27.9 - 32.5	0.3 - 8.4	N
05/30/2026	52.3 - 68.7	0.0 - 50.4	27.9 - 32.1	0.3 - 14.7	NE
05/31/2026	51.6 - 74.3	0.0 - 55.5	28.0 - 32.6	0.2 - 7.7	N


Daily Monitoring Summary	PM2.5 (µg/m³)	Time	PM10 (µg/m³)	Time	VOC (ppm)	Time
Min Contribution (15 min avg.) - 5/25/2026	0.0	14:45	0.0	11:45	0.0000	00:00
Max Contribution (15 min avg.) - 5/25/2026	14.2	07:15	14.4	07:15	0.0093	10:15
Daily Avg. Contribution (15 min avg.) - 5/25/2026	2.6	-	2.7	-	0.0005	-
Min Contribution (15 min avg.) - 5/26/2026	0.0	07:30	0.0	07:30	0.0000	00:15
Max Contribution (15 min avg.) - 5/26/2026	3.1	20:15	18.1	14:30	0.1047	08:45
Daily Avg. Contribution (15 min avg.) - 5/26/2026	1.2	-	4.0	-	0.0121	-
Min Contribution (15 min avg.) - 5/27/2026	0.0	01:30	0.0	01:30	0.0000	00:00
Max Contribution (15 min avg.) - 5/27/2026	9.2	06:15	126.9	23:45	0.0213	14:30
Daily Avg. Contribution (15 min avg.) - 5/27/2026	2.2	-	5.7	-	0.0034	-
Min Contribution (15 min avg.) - 5/28/2026	0.0	08:45	0.0	03:30	0.0000	02:15
Max Contribution (15 min avg.) - 5/28/2026	42.8	15:15	517.5	15:15	0.0520	09:00
Daily Avg. Contribution (15 min avg.) - 5/28/2026	4.5	-	47.2	-	0.0063	-
Min Contribution (15 min avg.) - 5/29/2026	0.0	03:00	0.0	14:45	0.0000	00:00
Max Contribution (15 min avg.) - 5/29/2026	4.3	10:00	46.5	13:00	0.0200	21:30
Daily Avg. Contribution (15 min avg.) - 5/29/2026	1.0	-	6.0	-	0.0025	-
Min Contribution (15 min avg.) - 5/30/2026	0.3	02:30	0.0	02:30	0.0000	00:15
Max Contribution (15 min avg.) - 5/30/2026	23.2	04:30	255.6	04:30	0.0820	05:45
Daily Avg. Contribution (15 min avg.) - 5/30/2026	3.2	-	28.5	-	0.0055	-
Min Contribution (15 min avg.) - 5/31/2026	0.0	04:30	0.0	04:00	0.0000	00:00
Max Contribution (15 min avg.) - 5/31/2026	20.9	05:45	21.9	05:45	0.0740	13:30
Daily Avg. Contribution (15 min avg.) - 5/31/2026	0.9	-	1.0	-	0.0047	-





Stopped Initial Avg Rolling Avg


PM2.5 Average Contribution ( $\mu\text{g}/\text{m}^3$ )

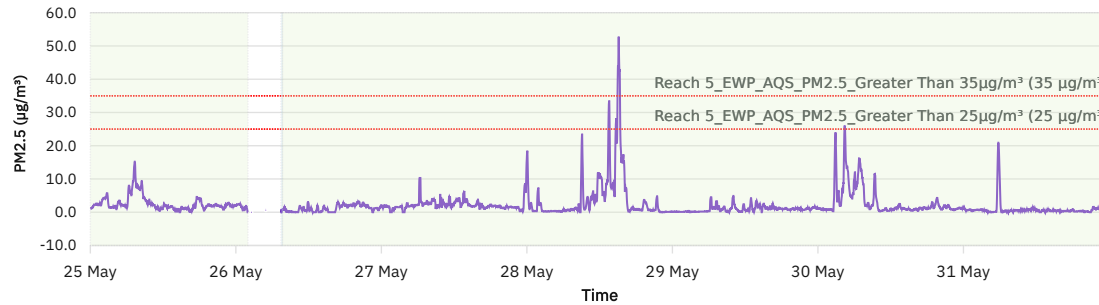

● 15 Min Rolling Avg PM2.5 Contribution

Stopped Initial Avg Rolling Avg


PM10 Average Contribution ( $\mu\text{g}/\text{m}^3$ )

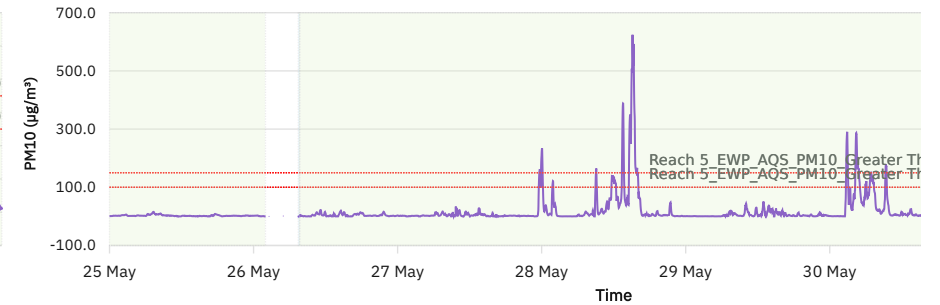

● 15 Min Rolling Avg PM10 Contribution


Stopped Initial Avg Rolling Avg

VOC Average Contribution (ppm)

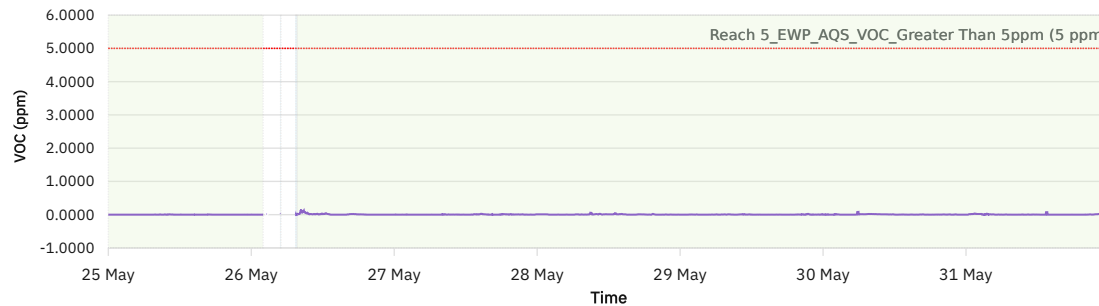


● 15 Min Rolling Avg VOC Contribution


Wind rose (mph)

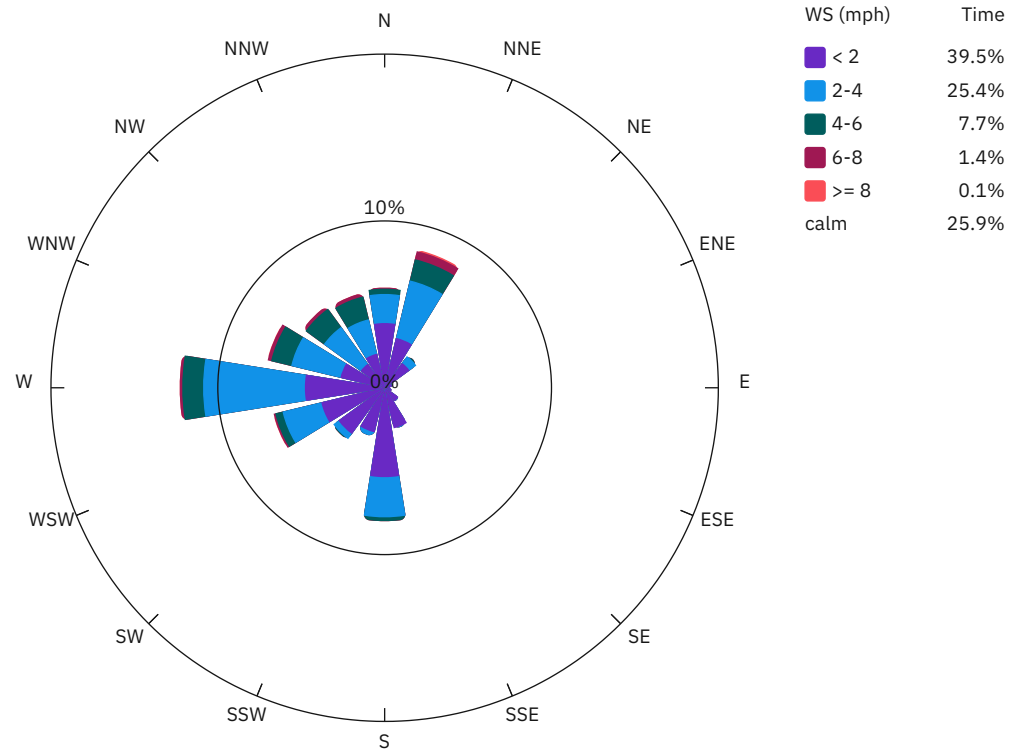


AM-16\_Reach 5\_3178\_WS

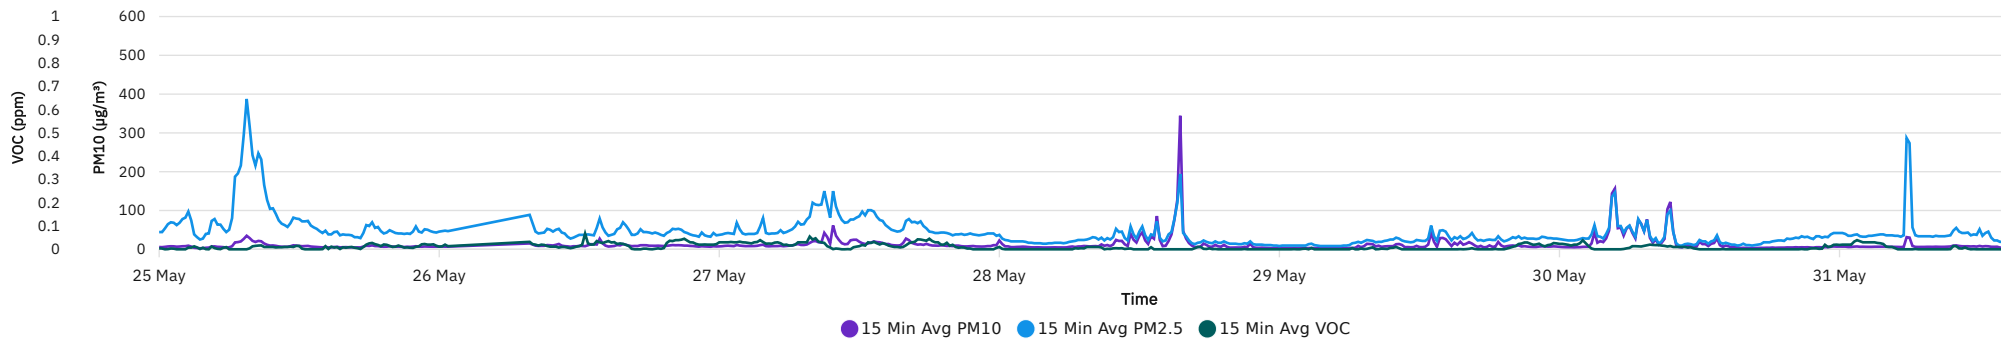


AM-17\_Reach 5\_3183

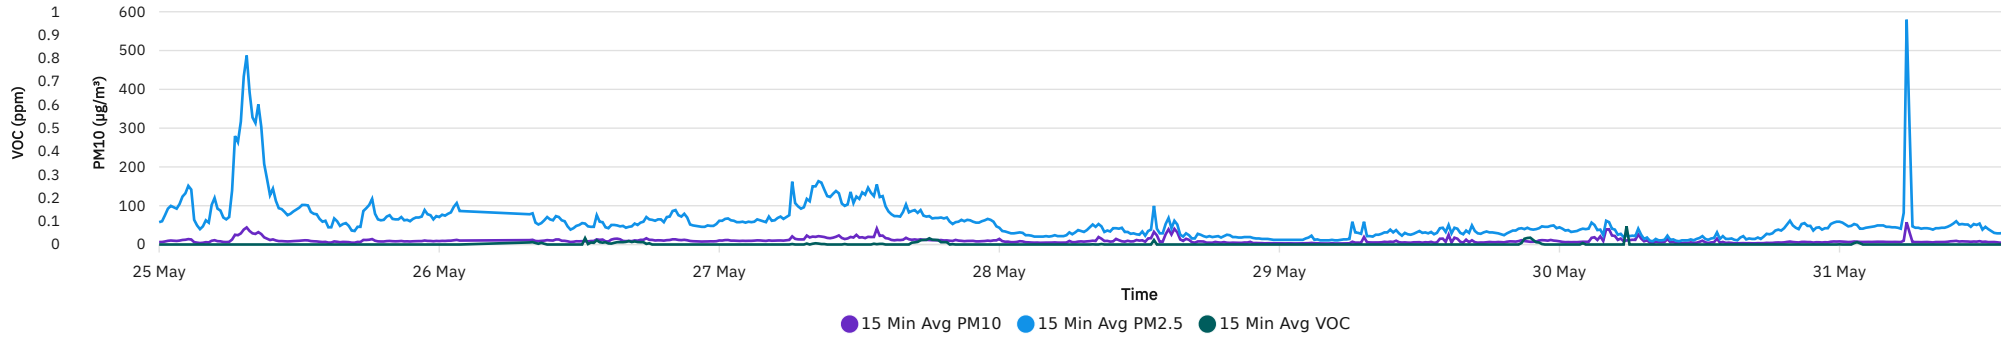


AM-18\_Reach 5\_3182\_WS

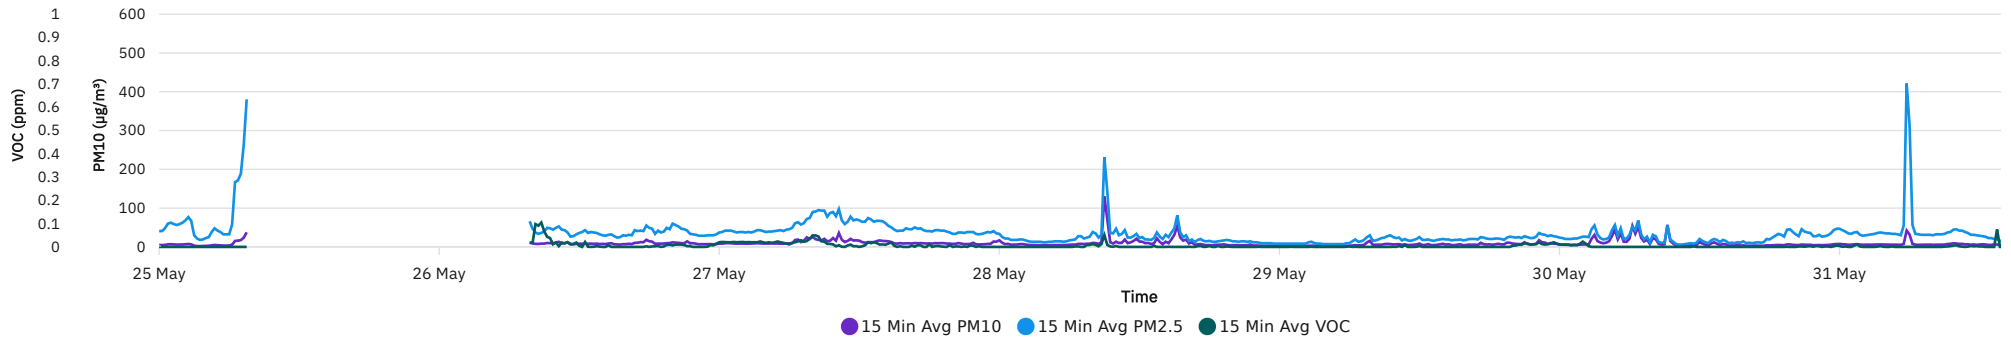

AM-19\_Reach 5\_3175

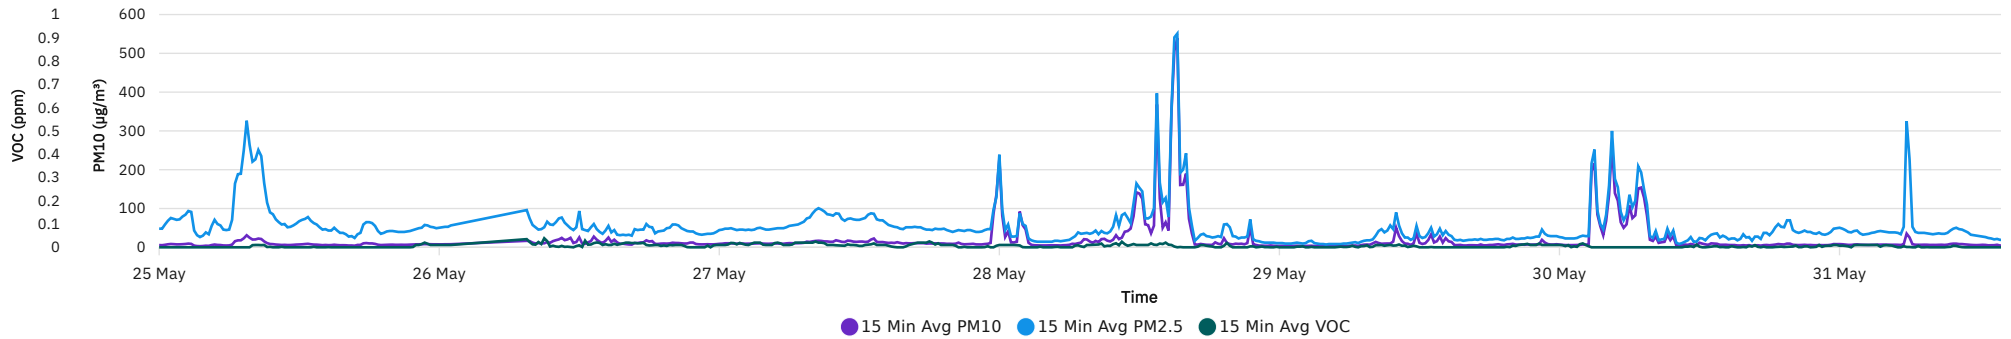

AM-20\_Reach 5\_3180\_WS

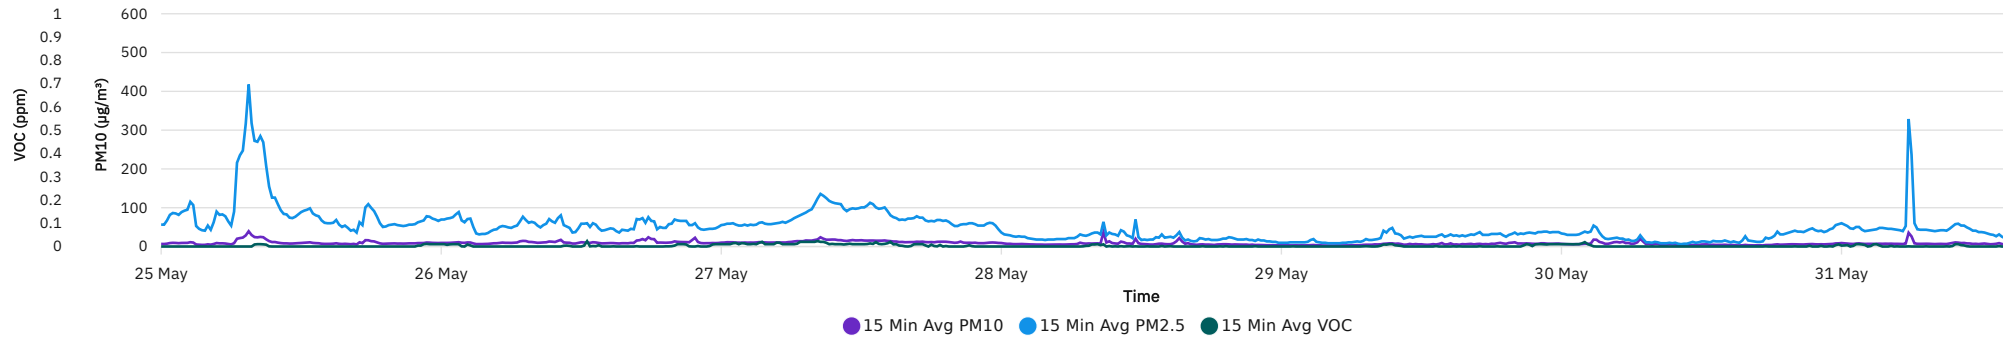

Exceedance Summary

Parameter	Action Level	Time Triggered	Cause	Mitigation
PM10	150.0 µg/m³	5/27/2026 23:32	Elevated readings were attributable to wind-blown dust across the site.	Contractor wetted the area to mitigate dust levels and fugitive dust.
PM10	150.0 µg/m³	5/27/2026 23:51	Elevated readings were attributable to wind-blown dust across the site.	Contractor wetted the area to mitigate dust levels and fugitive dust.
PM10	100.0 µg/m³	5/28/2026 01:47	Elevated readings were attributable to wind-blown dust across the site.	Contractor wetted the area to mitigate dust levels and fugitive dust.
PM10	150.0 µg/m³	5/28/2026 08:59	Elevated readings were due to Contractor's Work.	Contractor wetted the area to mitigate dust levels and fugitive dust.
PM10	150.0 µg/m³	5/28/2026 11:38	Elevated readings were due to Contractor's Work.	Contractor wetted the area to mitigate dust levels and fugitive dust.
PM10	100.0 µg/m³	5/28/2026 13:21	Elevated readings were due to Contractor's Work.	Contractor wetted the area to mitigate dust levels and fugitive dust.
PM10	150.0 µg/m³	5/28/2026 14:32	Elevated readings were due to Contractor's Work.	Contractor wetted the area to mitigate dust levels and fugitive dust.
PM10	100.0 µg/m³	5/30/2026 02:42	Elevated readings were attributable to wind-blown dust across the site.	Contractor wetted the area to mitigate dust levels and fugitive dust.
PM10	100.0 µg/m³	5/30/2026 04:14	Elevated readings were attributable to wind-blown dust across the site.	Contractor wetted the area to mitigate dust levels and fugitive dust.
PM10	100.0 µg/m³	5/30/2026 05:55	Elevated readings were attributable to wind-blown dust across the site.	Contractor wetted the area to mitigate dust levels and fugitive dust.
PM10	100.0 µg/m³	5/30/2026 06:39	Elevated readings were attributable to wind-blown dust across the site.	Contractor wetted the area to mitigate dust levels and fugitive dust.
PM10	100.0 µg/m³	5/30/2026 09:14	Elevated readings were due to bad generator operation.	The generator was removed from service.
PM2.5	25.0 µg/m³	5/28/2026 13:27	Elevated readings were due to Contractor's Work.	Contractor wetted the area to mitigate dust levels and fugitive dust.
PM2.5	25.0 µg/m³	5/28/2026 14:39	Elevated readings were due to Contractor's Work.	Contractor wetted the area to mitigate dust levels and fugitive dust.
PM2.5	25.0 µg/m³	5/28/2026 14:55	Elevated readings were due to Contractor's Work.	Contractor wetted the area to mitigate dust levels and fugitive dust.
PM2.5	25.0 µg/m³	5/30/2026 04:23	Elevated readings were attributable to wind-blown dust across the site.	Contractor wetted the area to mitigate dust levels and fugitive dust.



Reach 6 (Albany St)\_EWP\_AQS Report

Battery Park_AQS	
Report Period	
From:	05/01/2026 00:00
To:	05/03/2026 23:59
PM10 Action Level:	100 µg/m³
PM2.5 Action Level:	25 µg/m³
VOC Action Level:	5 ppm

Daily Environmental Summary	Temp (°F)	Relative Humidity (%)	Barometer (inHg)	Wind Speed (mph)	Prevailing Wind Direction
05/01/2026	46.4 - 74.3	0.0 - 0.0	29.4 - 31.1	0.3 - 5.2	ESE
05/02/2026	51.4 - 61.7	0.0 - 0.0	26.6 - 31.2	0.5 - 22.2	ESE
05/03/2026	43.9 - 61.0	0.0 - 0.0	29.4 - 31.1	0.6 - 7.0	SE

Daily Monitoring Summary	PM2.5 (µg/m³)	Time	PM10 (µg/m³)	Time	VOC (ppm)	Time
Min Contribution (15 min avg.) - 5/1/2026	0.0	00:30	0.0	03:30	0.0000	00:00
Max Contribution (15 min avg.) - 5/1/2026	1.2	20:30	2.1	08:15	0.0100	09:15
Daily Avg. Contribution (15 min avg.) - 5/1/2026	0.2	-	0.2	-	0.0006	-
Min Contribution (15 min avg.) - 5/2/2026	0.0	00:30	0.0	00:00	0.0000	00:00
Max Contribution (15 min avg.) - 5/2/2026	0.5	04:00	1.3	06:00	0.0053	05:15
Daily Avg. Contribution (15 min avg.) - 5/2/2026	0.0	-	0.2	-	0.0003	-
Min Contribution (15 min avg.) - 5/3/2026	0.0	00:00	0.0	01:30	0.0000	00:00
Max Contribution (15 min avg.) - 5/3/2026	0.4	16:30	5.5	17:15	0.0067	22:30
Daily Avg. Contribution (15 min avg.) - 5/3/2026	0.0	-	0.5	-	0.0005	-




Stopped Initial Avg Rolling Avg


PM2.5 Average Contribution (µg/m³)

Stopped Initial Avg Rolling Avg

PM10 Average Contribution (µg/m³)

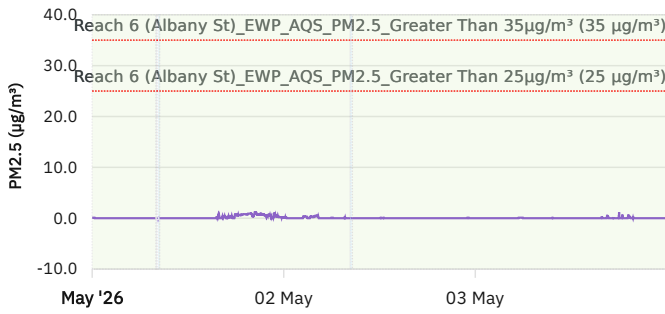


15 Min Rolling Avg PM2.5 Contribution

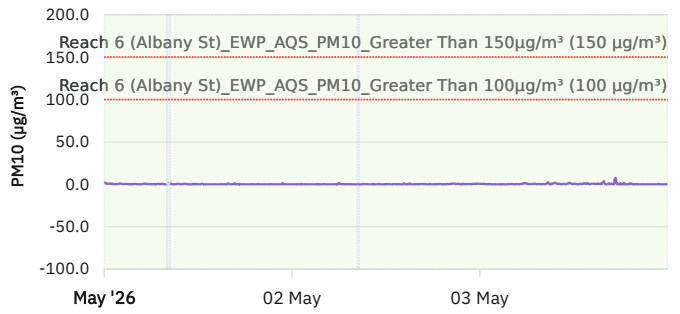


15 Min Rolling Avg PM10 Contribution

Stopped Initial Avg Rolling Avg


### VOC Average Contribution (ppm)

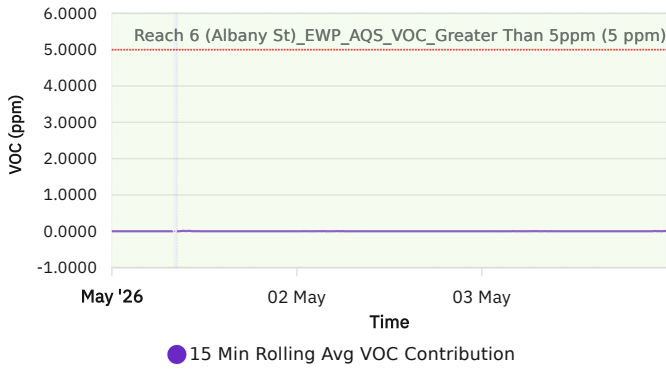


### Wind rose (mph)

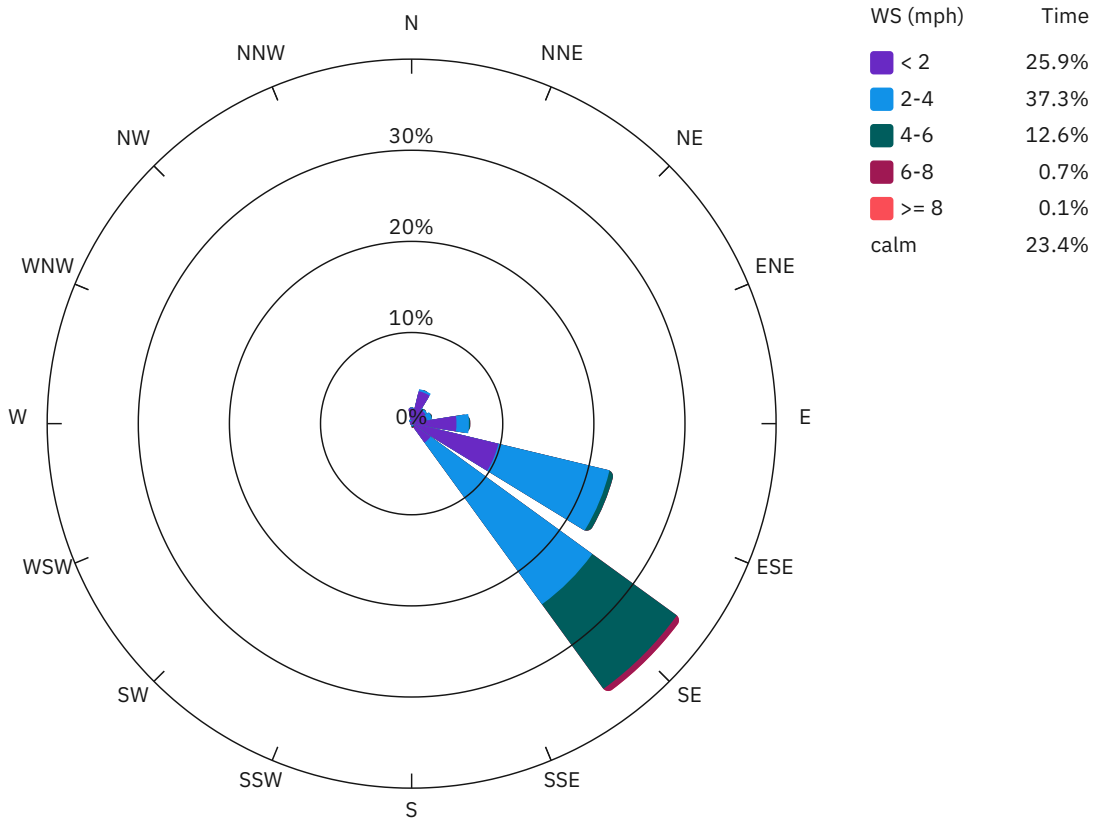

### AM-11\_Reach 6\_3185

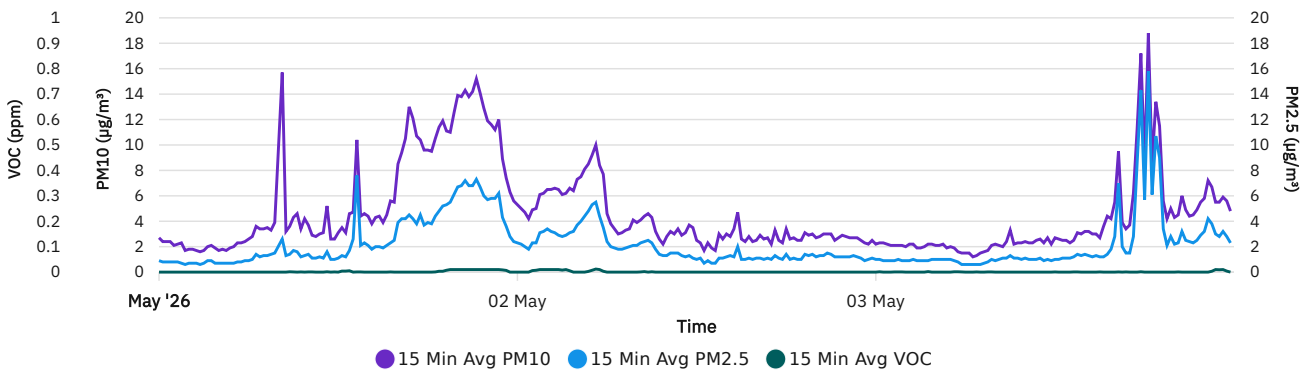

AM-12\_Reach 6\_3186\_WS

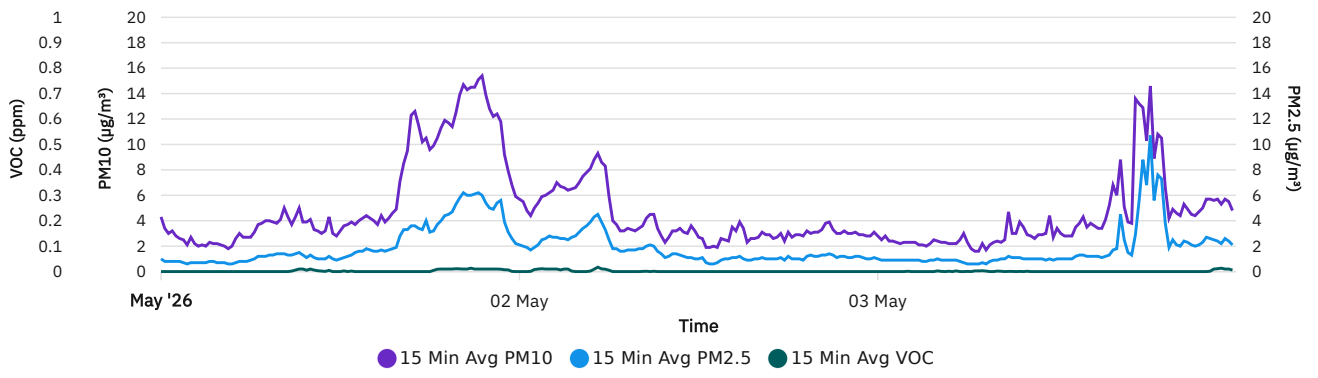



Reach 6 (Albany St)\_EWP\_AQS Report

Battery Park_AQS	
Report Period	
From:	05/04/2026 00:00
To:	05/10/2026 23:59
PM10 Action Level:	100 µg/m³
PM2.5 Action Level:	25 µg/m³
VOC Action Level:	5 ppm

Daily Environmental Summary	Temp (°F)	Relative Humidity (%)	Barometer (inHg)	Wind Speed (mph)	Prevailing Wind Direction
05/04/2026	50.4 - 75.0	0.0 - 0.0	29.4 - 31.1	0.4 - 4.6	E
05/05/2026	60.4 - 84.7	0.0 - 0.0	29.1 - 31.1	0.3 - 4.5	NNE
05/06/2026	55.0 - 69.3	0.0 - 0.0	29.2 - 30.9	0.3 - 6.0	ENE
05/07/2026	47.8 - 64.9	0.0 - 0.0	29.2 - 31.1	0.6 - 6.2	SE
05/08/2026	48.0 - 62.4	0.0 - 0.0	29.4 - 30.9	0.3 - 6.1	ESE
05/09/2026	55.0 - 64.9	0.0 - 0.0	29.5 - 32.2	0.2 - 2.7	ENE
05/10/2026	52.7 - 67.3	0.0 - 0.0	29.3 - 31.5	0.3 - 2.6	E


Daily Monitoring Summary	PM2.5 (µg/m³)	Time	PM10 (µg/m³)	Time	VOC (ppm)	Time
Min Contribution (15 min avg.) - 5/4/2026	0.0	00:00	0.0	00:00	0.0000	01:30
Max Contribution (15 min avg.) - 5/4/2026	0.8	23:15	1.0	11:15	0.0093	00:45
Daily Avg. Contribution (15 min avg.) - 5/4/2026	0.1	-	0.1	-	0.0016	-
Min Contribution (15 min avg.) - 5/5/2026	0.0	06:15	0.0	00:00	0.0000	00:00
Max Contribution (15 min avg.) - 5/5/2026	3.1	09:45	5.6	09:45	0.0213	12:00
Daily Avg. Contribution (15 min avg.) - 5/5/2026	0.5	-	0.2	-	0.0007	-
Min Contribution (15 min avg.) - 5/6/2026	0.0	10:00	0.0	00:00	0.0000	00:00
Max Contribution (15 min avg.) - 5/6/2026	2.2	15:00	7.9	14:15	0.0060	16:00
Daily Avg. Contribution (15 min avg.) - 5/6/2026	0.3	-	0.3	-	0.0005	-
Min Contribution (15 min avg.) - 5/7/2026	0.0	00:00	0.0	02:00	0.0000	00:00
Max Contribution (15 min avg.) - 5/7/2026	0.7	02:45	3.3	02:45	0.0033	23:45
Daily Avg. Contribution (15 min avg.) - 5/7/2026	0.0	-	0.4	-	0.0000	-
Min Contribution (15 min avg.) - 5/8/2026	0.0	00:00	0.0	00:00	0.0000	01:15
Max Contribution (15 min avg.) - 5/8/2026	1.2	01:30	4.5	16:15	0.0100	00:30
Daily Avg. Contribution (15 min avg.) - 5/8/2026	0.0	-	0.3	-	0.0011	-
Min Contribution (15 min avg.) - 5/9/2026	0.0	00:00	0.0	00:00	0.0000	01:30
Max Contribution (15 min avg.) - 5/9/2026	2.5	13:30	2.5	13:30	0.0100	03:00
Daily Avg. Contribution (15 min avg.) - 5/9/2026	0.2	-	0.1	-	0.0013	-
Min Contribution (15 min avg.) - 5/10/2026	0.0	00:00	0.0	00:00	0.0000	00:00
Max Contribution (15 min avg.) - 5/10/2026	0.7	18:30	0.7	18:30	0.0093	20:30
Daily Avg. Contribution (15 min avg.) - 5/10/2026	0.0	-	0.0	-	0.0014	-




Stopped 
  Initial Avg 
  Rolling Avg

Stopped 
  Initial Avg 
  Rolling Avg

PM2.5 Average Contribution ( $\mu\text{g}/\text{m}^3$ )

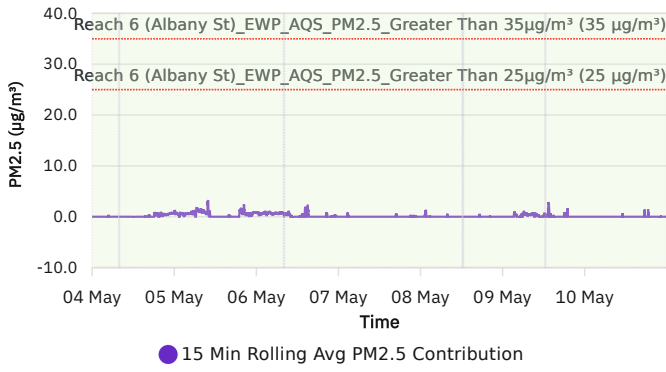


PM10 Average Contribution ( $\mu\text{g}/\text{m}^3$ )

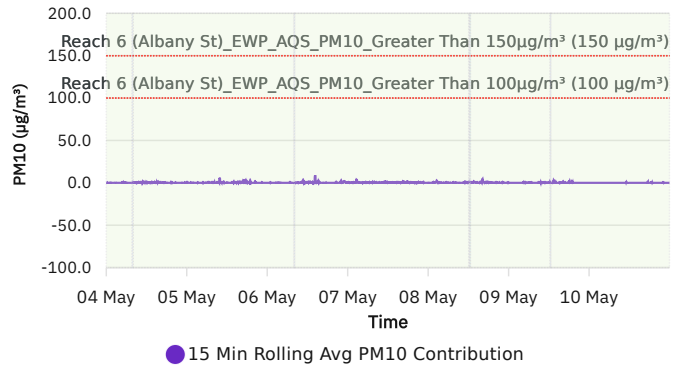


Stopped Initial Avg Rolling Avg


VOC Average Contribution (ppm)

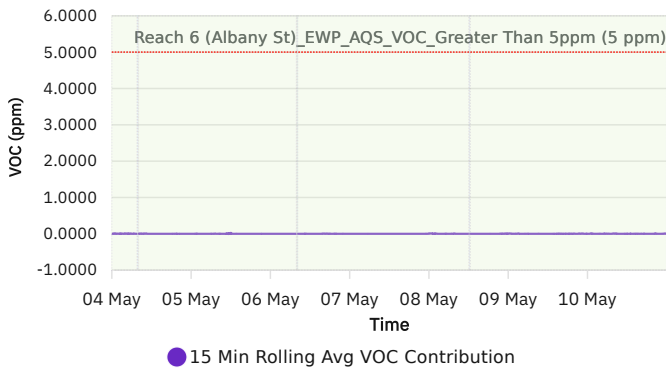


Wind rose (mph)

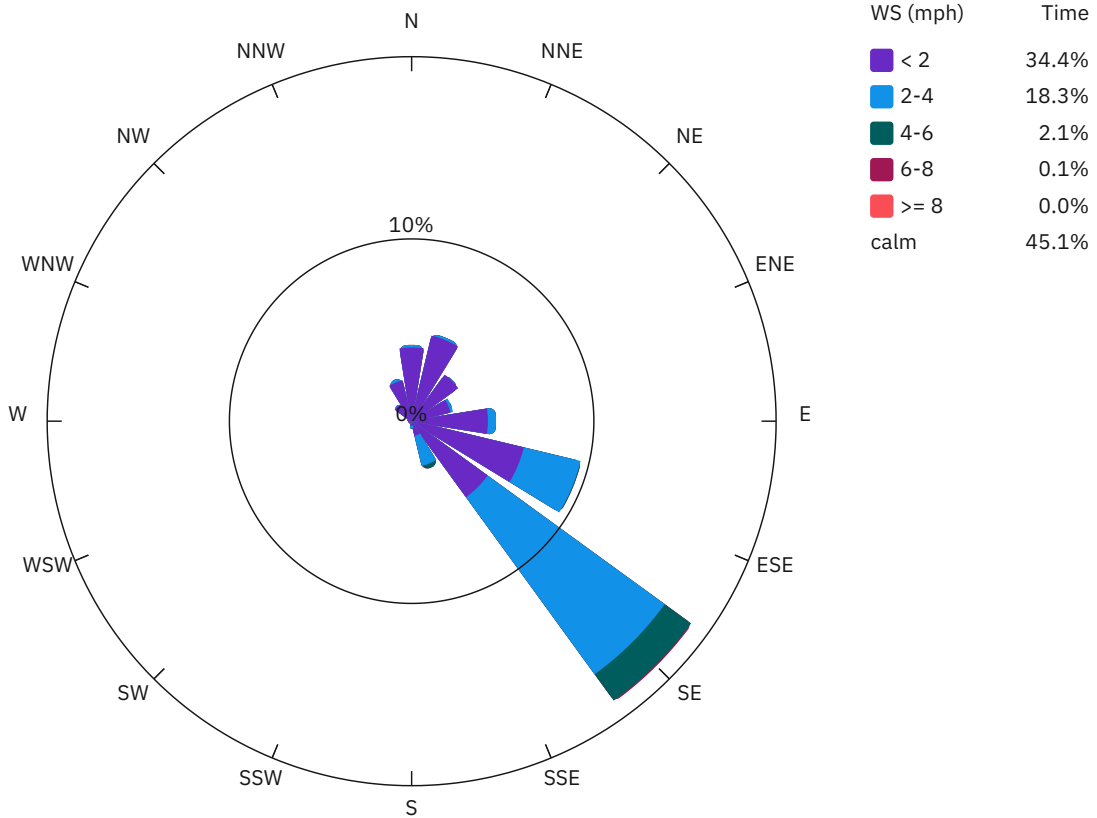

AM-11\_Reach 6\_3185

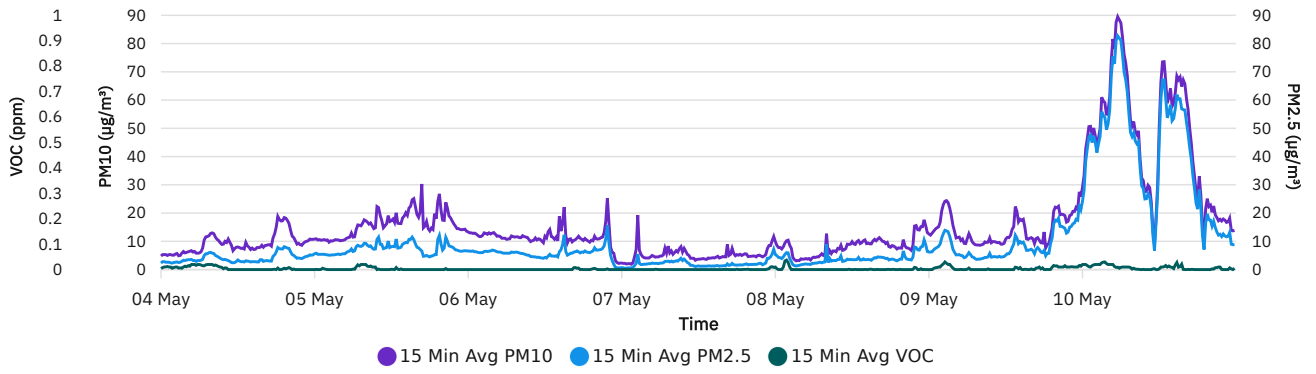

AM-12\_Reach 6\_3186\_WS

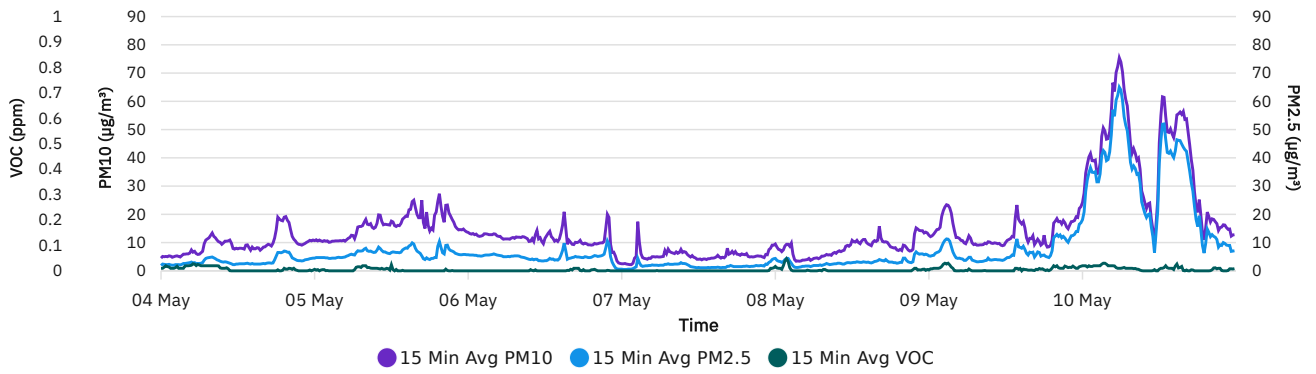



Reach 6 (Albany St)\_EWP\_AQS Report

Battery Park_AQS	
Report Period	
From:	05/11/2026 00:00
To:	05/17/2026 23:59
PM10 Action Level:	100 µg/m³
PM2.5 Action Level:	25 µg/m³
VOC Action Level:	5 ppm

Daily Environmental Summary	Temp (°F)	Relative Humidity (%)	Barometer (inHg)	Wind Speed (mph)	Prevailing Wind Direction
05/11/2026	53.8 - 65.3	0.0 - 0.0	29.4 - 46.6	0.3 - 85.0	E
05/12/2026	46.8 - 67.8	0.0 - 0.0	29.6 - 31.4	0.3 - 4.7	ESE
05/13/2026	54.1 - 72.9	0.0 - 0.0	29.3 - 31.9	0.3 - 1.8	NNE
05/14/2026	54.0 - 68.5	0.0 - 0.0	28.4 - 31.1	0.3 - 8.5	SE
05/15/2026	50.7 - 66.4	0.0 - 0.0	29.5 - 30.9	0.3 - 6.0	SE
05/16/2026	57.4 - 81.5	0.0 - 0.0	29.4 - 31.1	0.3 - 3.7	SE
05/17/2026	67.6 - 86.4	0.0 - 0.0	28.0 - 31.4	0.2 - 23.4	ESE


Daily Monitoring Summary	PM2.5 (µg/m³)	Time	PM10 (µg/m³)	Time	VOC (ppm)	Time
Min Contribution (15 min avg.) - 5/11/2026	0.0	00:00	0.0	00:00	0.0000	00:15
Max Contribution (15 min avg.) - 5/11/2026	0.7	17:45	2.2	07:15	0.0100	22:30
Daily Avg. Contribution (15 min avg.) - 5/11/2026	0.0	-	0.3	-	0.0006	-
Min Contribution (15 min avg.) - 5/12/2026	0.0	00:00	0.0	00:00	0.0000	00:15
Max Contribution (15 min avg.) - 5/12/2026	0.6	13:45	1.4	03:30	0.0100	01:30
Daily Avg. Contribution (15 min avg.) - 5/12/2026	0.0	-	0.3	-	0.0008	-
Min Contribution (15 min avg.) - 5/13/2026	0.0	01:45	0.0	00:00	0.0000	00:15
Max Contribution (15 min avg.) - 5/13/2026	2.6	13:45	5.8	13:45	0.0133	13:45
Daily Avg. Contribution (15 min avg.) - 5/13/2026	0.3	-	0.3	-	0.0004	-
Min Contribution (15 min avg.) - 5/14/2026	0.0	01:15	0.0	00:00	0.0000	00:00
Max Contribution (15 min avg.) - 5/14/2026	0.8	00:00	2.2	18:45	0.0047	04:15
Daily Avg. Contribution (15 min avg.) - 5/14/2026	0.0	-	0.2	-	0.0003	-
Min Contribution (15 min avg.) - 5/15/2026	0.0	00:00	0.0	02:30	0.0000	00:00
Max Contribution (15 min avg.) - 5/15/2026	1.9	14:45	28.6	14:45	0.0107	13:15
Daily Avg. Contribution (15 min avg.) - 5/15/2026	0.1	-	2.1	-	0.0002	-
Min Contribution (15 min avg.) - 5/16/2026	0.0	00:00	0.0	00:15	0.0000	00:00
Max Contribution (15 min avg.) - 5/16/2026	2.5	09:00	4.2	17:45	0.0133	08:15
Daily Avg. Contribution (15 min avg.) - 5/16/2026	0.1	-	0.3	-	0.0009	-
Min Contribution (15 min avg.) - 5/17/2026	0.0	00:00	0.0	00:00	0.0000	00:15
Max Contribution (15 min avg.) - 5/17/2026	0.4	08:00	1.2	08:00	0.0093	21:45
Daily Avg. Contribution (15 min avg.) - 5/17/2026	0.0	-	0.1	-	0.0011	-




Stopped 
  Initial Avg 
  Rolling Avg

Stopped 
  Initial Avg 
  Rolling Avg

PM2.5 Average Contribution ( $\mu\text{g}/\text{m}^3$ )

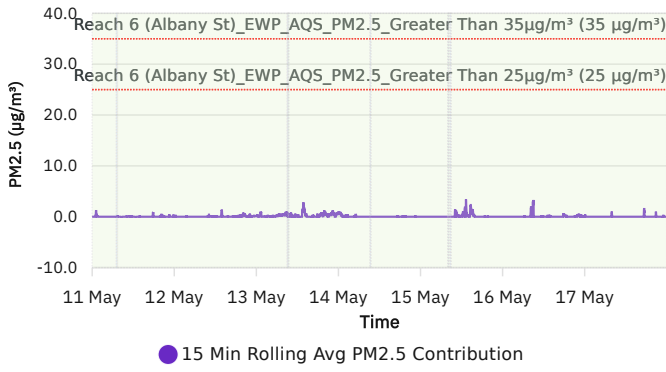


PM10 Average Contribution ( $\mu\text{g}/\text{m}^3$ )

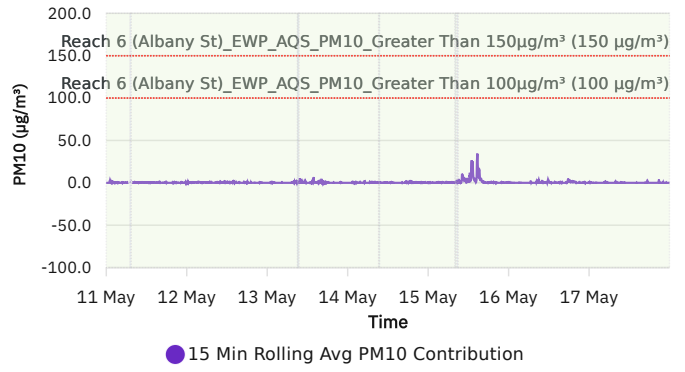


Stopped Initial Avg Rolling Avg


VOC Average Contribution (ppm)

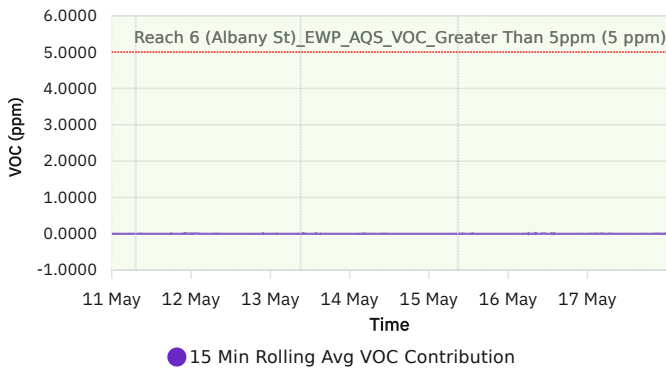


Wind rose (mph)

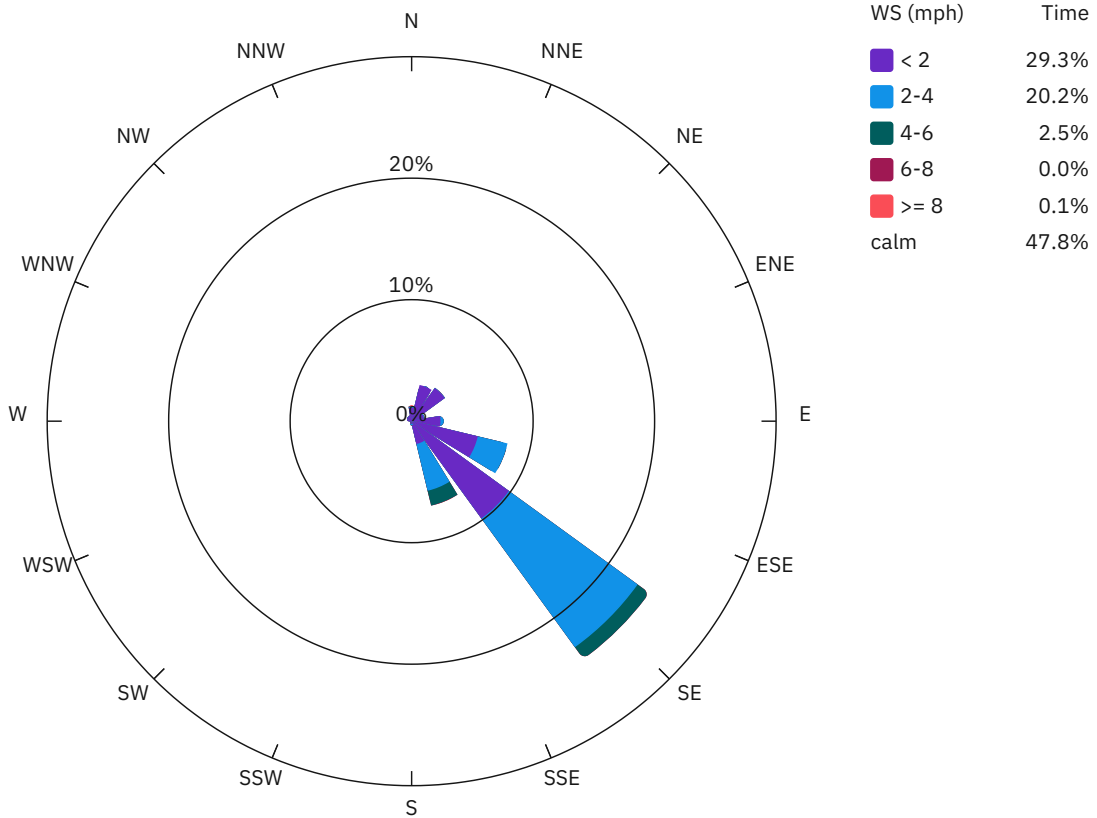

AM-11\_Reach 6\_3185

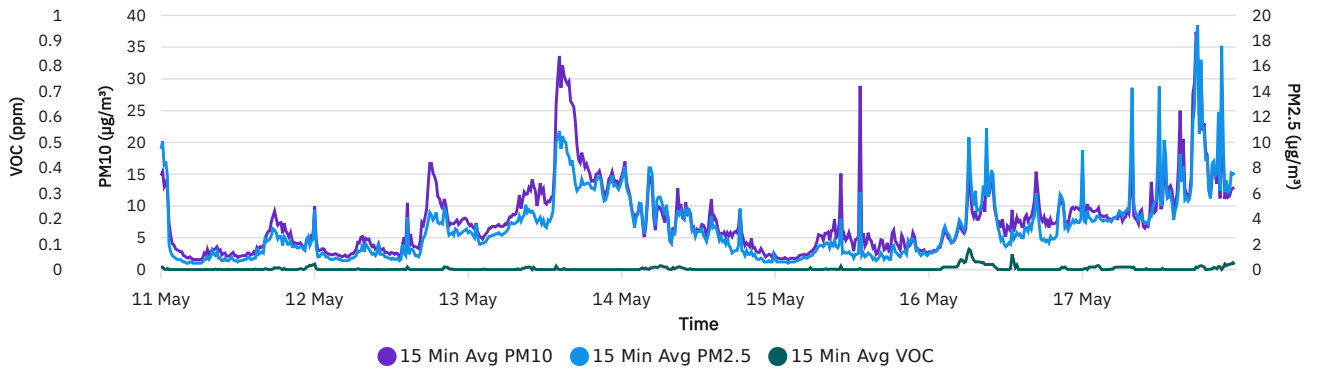

AM-12\_Reach 6\_3186\_WS

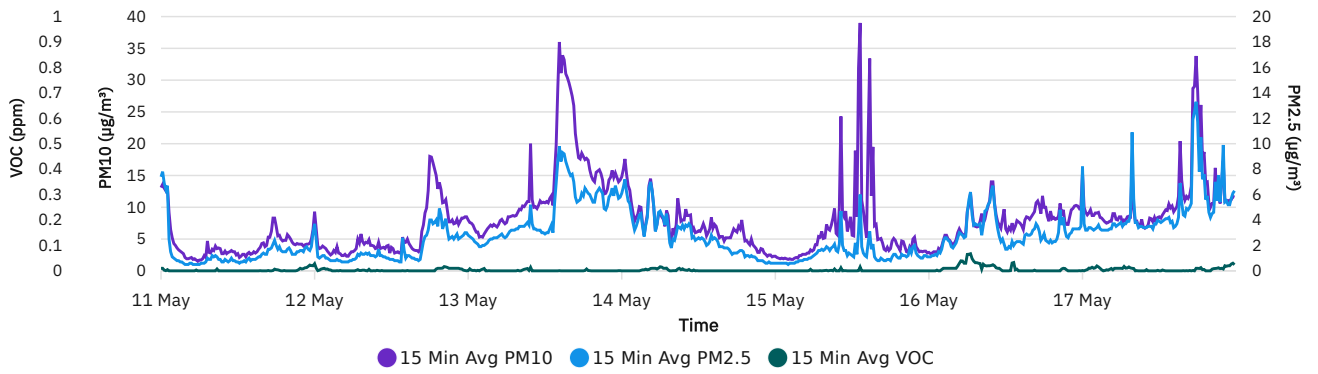



Reach 6 (Albany St)\_EWP\_AQS Report

Battery Park_AQS	
Report Period	
From:	05/18/2026 00:00
To:	05/24/2026 23:59
PM10 Action Level:	100 µg/m³
PM2.5 Action Level:	25 µg/m³
VOC Action Level:	5 ppm

Daily Environmental Summary	Temp (°F)	Relative Humidity (%)	Barometer (inHg)	Wind Speed (mph)	Prevailing Wind Direction
05/18/2026	69.8 - 87.6	0.0 - 0.0	28.0 - 31.4	0.3 - 2.1	ESE
05/19/2026	74.1 - 92.7	0.0 - 0.0	29.4 - 31.4	0.4 - 4.0	E
05/20/2026	66.7 - 90.9	0.0 - 0.0	29.4 - 31.1	0.3 - 6.0	SE
05/21/2026	55.0 - 66.9	0.0 - 0.0	29.7 - 31.4	0.3 - 5.4	SE
05/22/2026	56.5 - 69.1	0.0 - 0.0	29.9 - 31.6	0.3 - 4.7	SE
05/23/2026	49.5 - 60.1	0.0 - 0.0	30.0 - 31.7	0.4 - 2.5	E
05/24/2026	51.1 - 56.3	0.0 - 0.0	29.6 - 32.1	0.4 - 2.3	ENE


Daily Monitoring Summary	PM2.5 (µg/m³)	Time	PM10 (µg/m³)	Time	VOC (ppm)	Time
Min Contribution (15 min avg.) - 5/18/2026	0.0	00:00	0.0	00:00	0.0000	01:15
Max Contribution (15 min avg.) - 5/18/2026	3.3	17:45	32.8	13:45	0.0233	09:00
Daily Avg. Contribution (15 min avg.) - 5/18/2026	0.1	-	1.4	-	0.0024	-
Min Contribution (15 min avg.) - 5/19/2026	0.0	00:00	0.0	00:00	0.0000	00:00
Max Contribution (15 min avg.) - 5/19/2026	1.9	17:00	40.6	17:00	0.0073	11:00
Daily Avg. Contribution (15 min avg.) - 5/19/2026	0.0	-	0.8	-	0.0005	-
Min Contribution (15 min avg.) - 5/20/2026	0.0	00:00	0.0	00:00	0.0000	00:30
Max Contribution (15 min avg.) - 5/20/2026	5.8	18:30	86.9	18:30	0.0107	11:00
Daily Avg. Contribution (15 min avg.) - 5/20/2026	0.3	-	7.1	-	0.0009	-
Min Contribution (15 min avg.) - 5/21/2026	0.0	00:00	0.0	00:30	0.0000	00:00
Max Contribution (15 min avg.) - 5/21/2026	3.4	14:30	15.4	14:30	0.0273	14:15
Daily Avg. Contribution (15 min avg.) - 5/21/2026	0.1	-	0.8	-	0.0012	-
Min Contribution (15 min avg.) - 5/22/2026	0.0	00:00	0.0	05:30	0.0000	00:00
Max Contribution (15 min avg.) - 5/22/2026	2.5	13:45	32.2	13:45	0.0013	20:45
Daily Avg. Contribution (15 min avg.) - 5/22/2026	0.1	-	1.8	-	0.0000	-
Min Contribution (15 min avg.) - 5/23/2026	0.0	00:00	0.0	00:00	0.0000	00:00
Max Contribution (15 min avg.) - 5/23/2026	0.4	23:15	1.1	04:30	0.0067	08:15
Daily Avg. Contribution (15 min avg.) - 5/23/2026	0.0	-	0.1	-	0.0010	-
Min Contribution (15 min avg.) - 5/24/2026	0.0	00:15	0.0	00:15	0.0000	00:15
Max Contribution (15 min avg.) - 5/24/2026	0.6	09:30	0.7	09:30	0.0007	00:00
Daily Avg. Contribution (15 min avg.) - 5/24/2026	0.1	-	0.1	-	0.0000	-




Stopped 
  Initial Avg 
  Rolling Avg

Stopped 
  Initial Avg 
  Rolling Avg

PM2.5 Average Contribution ( $\mu\text{g}/\text{m}^3$ )

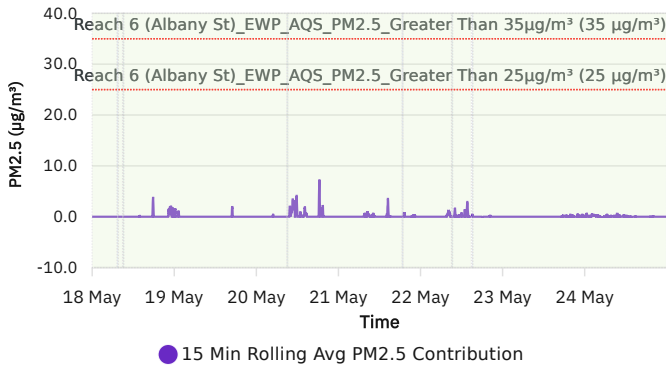


PM10 Average Contribution ( $\mu\text{g}/\text{m}^3$ )

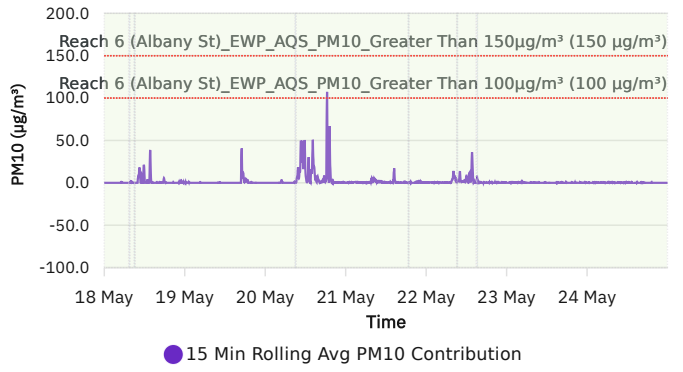


Stopped Initial Avg Rolling Avg


VOC Average Contribution (ppm)

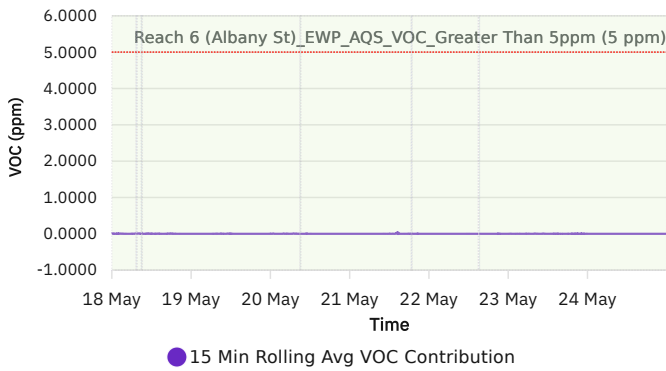


Wind rose (mph)

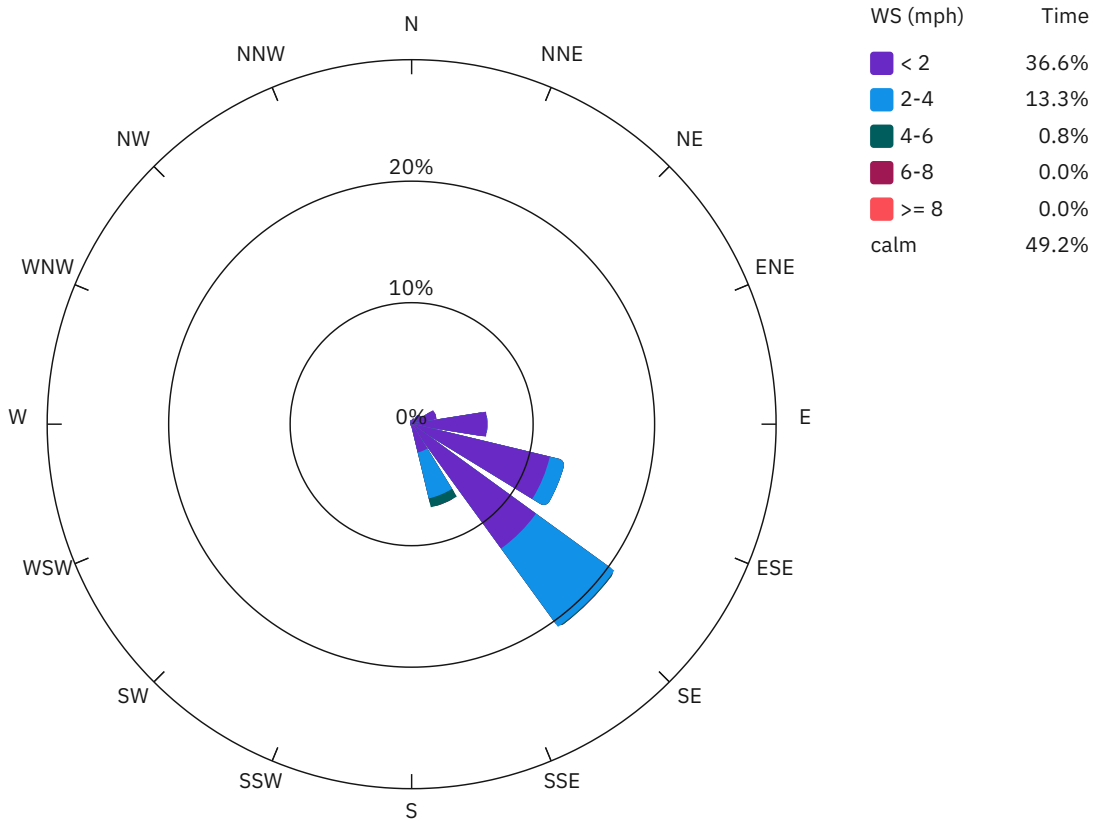

AM-11\_Reach 6\_3185

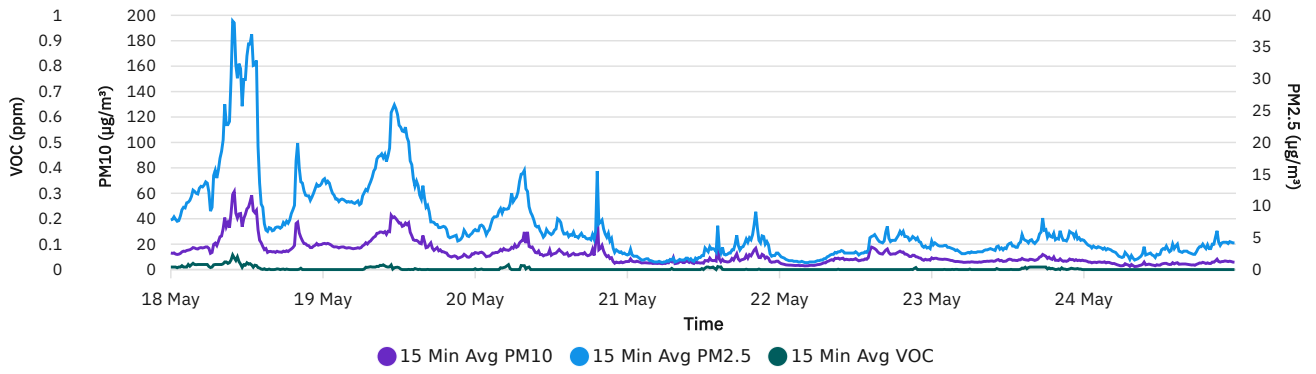

AM-12\_Reach 6\_3186\_WS

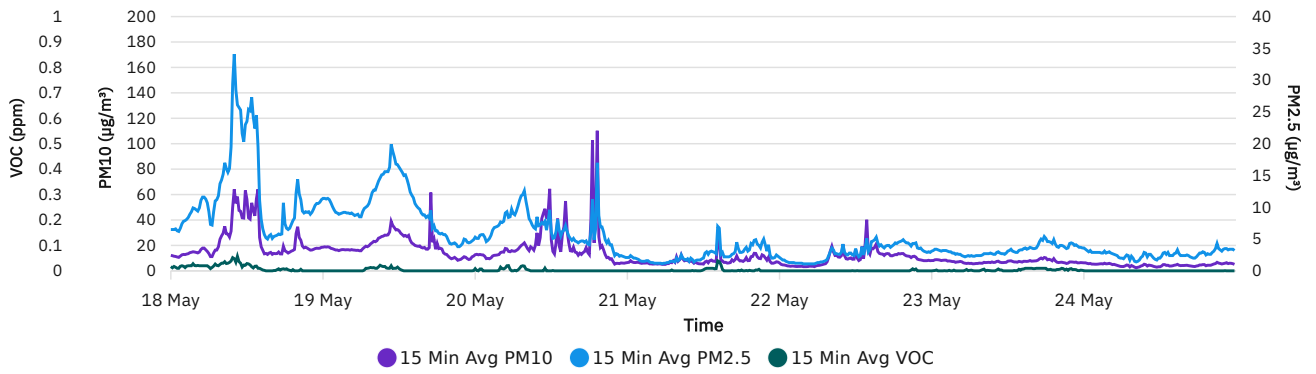

Exceedance Summary

Parameter	Action Level	Time Triggered	Cause	Mitigation
PM10	100.0 µg/m <sup>3</sup>	5/20/2026 18:25	Elevated readings were attributable to wind-blown dust across the site.	Contractor wetted the area to mitigate dust levels and fugitive dust.



Reach 6 (Albany St)\_EWP\_AQS Report

Battery Park\_AQS

Report Period

From:	05/25/2026 00:00
To:	05/31/2026 23:59
PM10 Action Level:	100 µg/m³
PM2.5 Action Level:	25 µg/m³
VOC Action Level:	5 ppm

Daily Environmental Summary	Temp (°F)	Relative Humidity (%)	Barometer (inHg)	Wind Speed (mph)	Prevailing Wind Direction
05/25/2026	56.1 - 58.5	0.0 - 0.0	29.8 - 31.0	0.3 - 2.3	E
05/26/2026	59.5 - 79.5	0.0 - 0.0	29.6 - 31.4	0.2 - 3.1	SE
05/27/2026	68.4 - 82.9	0.0 - 0.0	29.4 - 31.3	0.3 - 5.1	ESE
05/28/2026	63.0 - 76.3	0.0 - 0.0	29.4 - 31.1	0.4 - 7.0	SSE
05/29/2026	58.8 - 76.6	0.0 - 0.0	29.2 - 31.2	0.3 - 4.5	SE
05/30/2026	53.1 - 70.0	0.0 - 0.0	29.6 - 31.3	0.4 - 7.2	SE
05/31/2026	52.5 - 75.7	0.0 - 0.0	29.3 - 31.4	0.2 - 4.2	SE


Daily Monitoring Summary	PM2.5 (µg/m³)	Time	PM10 (µg/m³)	Time	VOC (ppm)	Time
Min Contribution (15 min avg.) - 5/25/2026	0.0	00:00	0.0	00:00	0.0000	00:00
Max Contribution (15 min avg.) - 5/25/2026	0.0	00:00	0.0	00:00	0.0047	09:00
Daily Avg. Contribution (15 min avg.) - 5/25/2026	0.0	-	0.0	-	0.0002	-
Min Contribution (15 min avg.) - 5/26/2026	0.0	07:45	0.0	10:00	0.0000	08:15
Max Contribution (15 min avg.) - 5/26/2026	3.4	07:15	5.8	07:15	0.0160	10:15
Daily Avg. Contribution (15 min avg.) - 5/26/2026	0.1	-	0.4	-	0.0009	-
Min Contribution (15 min avg.) - 5/27/2026	0.0	00:00	0.0	00:00	0.0000	01:00
Max Contribution (15 min avg.) - 5/27/2026	0.1	06:30	5.2	11:45	0.0287	10:00
Daily Avg. Contribution (15 min avg.) - 5/27/2026	0.0	-	0.3	-	0.0014	-
Min Contribution (15 min avg.) - 5/28/2026	0.0	00:15	0.0	06:45	0.0000	00:00
Max Contribution (15 min avg.) - 5/28/2026	1.3	15:15	17.1	15:15	0.0007	10:15
Daily Avg. Contribution (15 min avg.) - 5/28/2026	0.1	-	1.8	-	0.0000	-
Min Contribution (15 min avg.) - 5/29/2026	0.0	00:00	0.0	05:30	0.0000	00:00
Max Contribution (15 min avg.) - 5/29/2026	0.7	10:45	3.2	11:00	0.0100	11:00
Daily Avg. Contribution (15 min avg.) - 5/29/2026	0.0	-	0.7	-	0.0004	-
Min Contribution (15 min avg.) - 5/30/2026	0.0	00:00	0.0	01:00	0.0000	00:30
Max Contribution (15 min avg.) - 5/30/2026	9.3	04:15	117.4	04:15	0.0060	23:45
Daily Avg. Contribution (15 min avg.) - 5/30/2026	0.4	-	5.5	-	0.0003	-
Min Contribution (15 min avg.) - 5/31/2026	0.0	00:00	0.0	00:00	0.0000	00:45
Max Contribution (15 min avg.) - 5/31/2026	3.7	06:00	6.8	06:00	0.0067	01:45
Daily Avg. Contribution (15 min avg.) - 5/31/2026	0.1	-	0.3	-	0.0004	-




Stopped Initial Avg Rolling Avg

Stopped Initial Avg Rolling Avg

PM2.5 Average Contribution ( $\mu\text{g}/\text{m}^3$ )

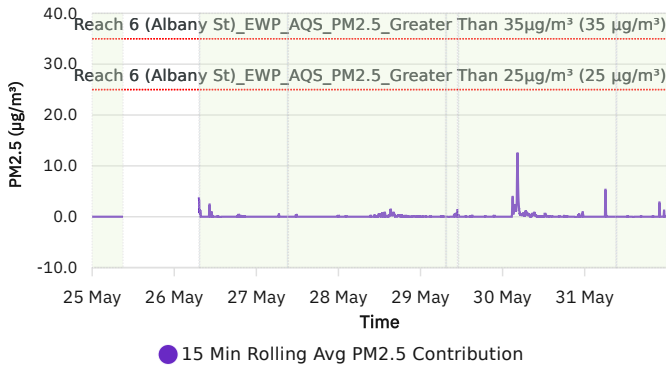


PM10 Average Contribution ( $\mu\text{g}/\text{m}^3$ )

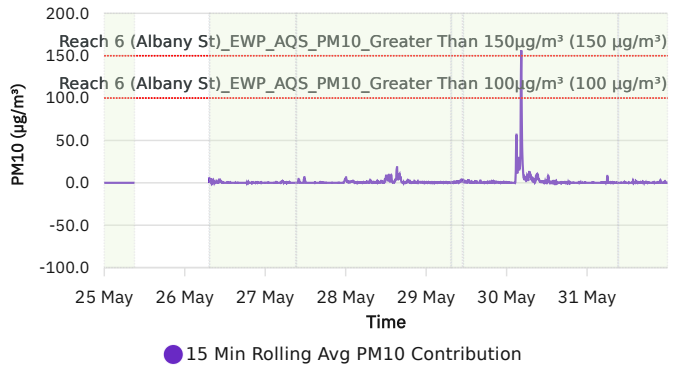


Stopped Initial Avg Rolling Avg


VOC Average Contribution (ppm)

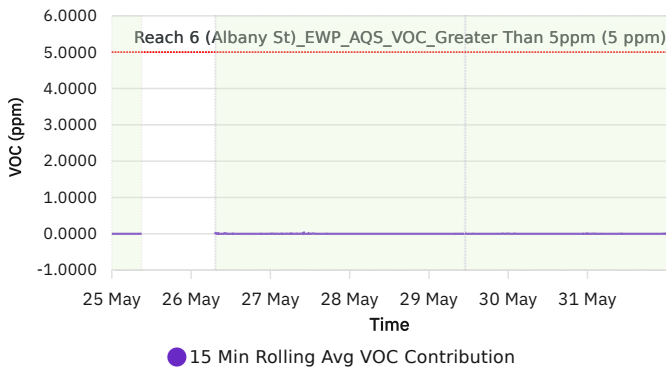


Wind rose (mph)

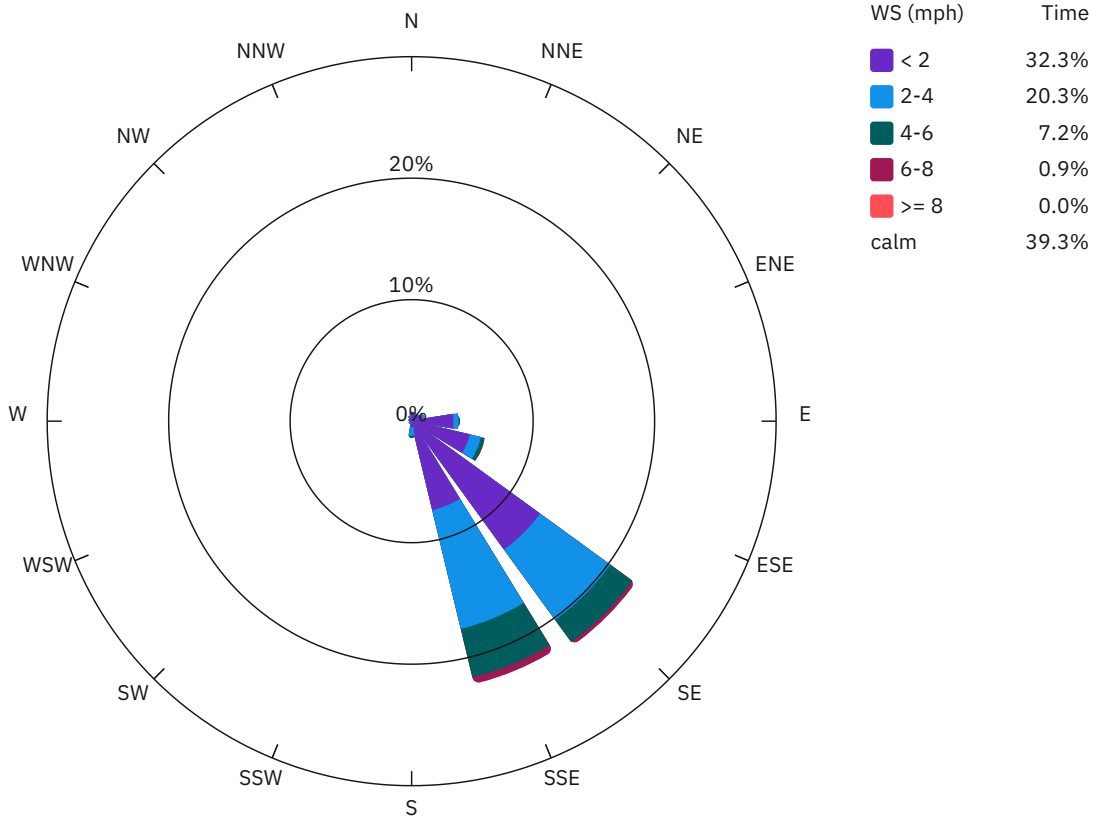

AM-11\_Reach 6\_3185

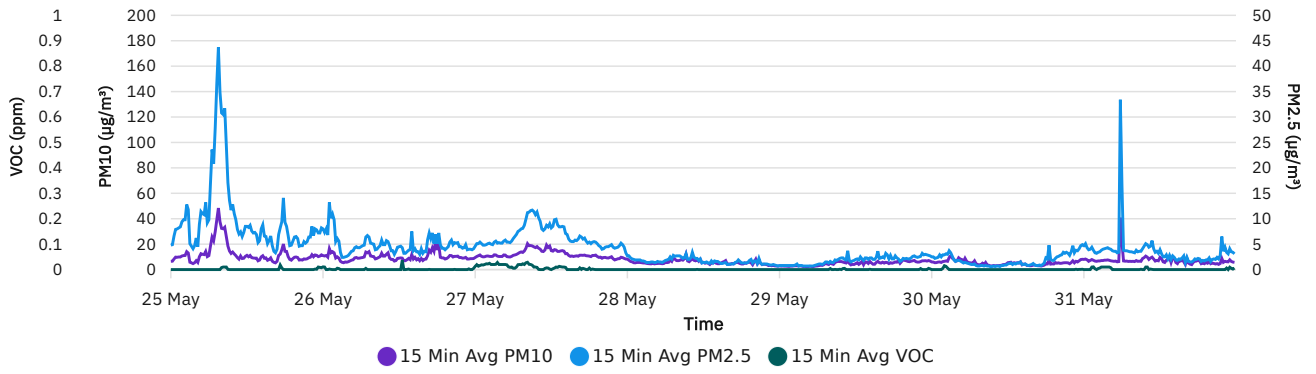

AM-12\_Reach 6\_3186\_WS

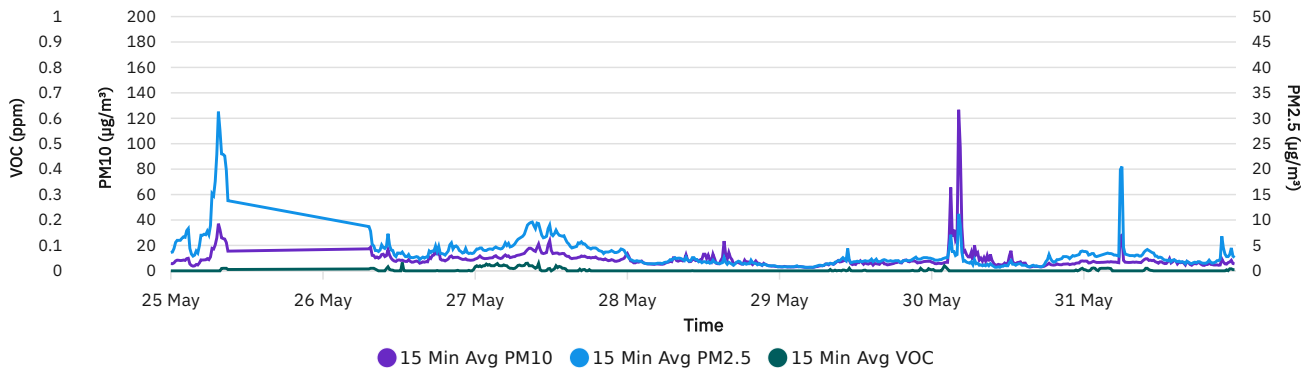

Exceedance Summary

Parameter	Action Level	Time Triggered	Cause	Mitigation
PM10	100.0 µg/m³	5/30/2026 04:14	Elevated readings were attributable to wind-blown dust across the site.	Contractor wetted the area to mitigate dust levels and fugitive dust.



Reach 6 (Rector St)\_EWP\_AQS Report

Battery Park\_AQS

Report Period

From: 05/01/2026 00:00

To: 05/03/2026 23:59


PM10 Action Level: 100 µg/m³

PM2.5 Action Level: 25 µg/m³


VOC Action Level: 5 ppm

Daily Environmental Summary	Temp (°F)	Relative Humidity (%)	Barometer (inHg)	Wind Speed (mph)	Prevailing Wind Direction
05/01/2026	-	-	-	-	-
05/02/2026	-	-	-	-	-
05/03/2026	-	-	-	-	-


Daily Monitoring Summary	PM2.5 (µg/m³)	Time	PM10 (µg/m³)	Time	VOC (ppm)	Time
Min Contribution (15 min avg.) - 5/1/2026	-	-	-	-	-	-
Max Contribution (15 min avg.) - 5/1/2026	-	-	-	-	-	-
Daily Avg. Contribution (15 min avg.) - 5/1/2026	-	-	-	-	-	-
Min Contribution (15 min avg.) - 5/2/2026	-	-	-	-	-	-
Max Contribution (15 min avg.) - 5/2/2026	-	-	-	-	-	-
Daily Avg. Contribution (15 min avg.) - 5/2/2026	-	-	-	-	-	-
Min Contribution (15 min avg.) - 5/3/2026	-	-	-	-	-	-
Max Contribution (15 min avg.) - 5/3/2026	-	-	-	-	-	-
Daily Avg. Contribution (15 min avg.) - 5/3/2026	-	-	-	-	-	-

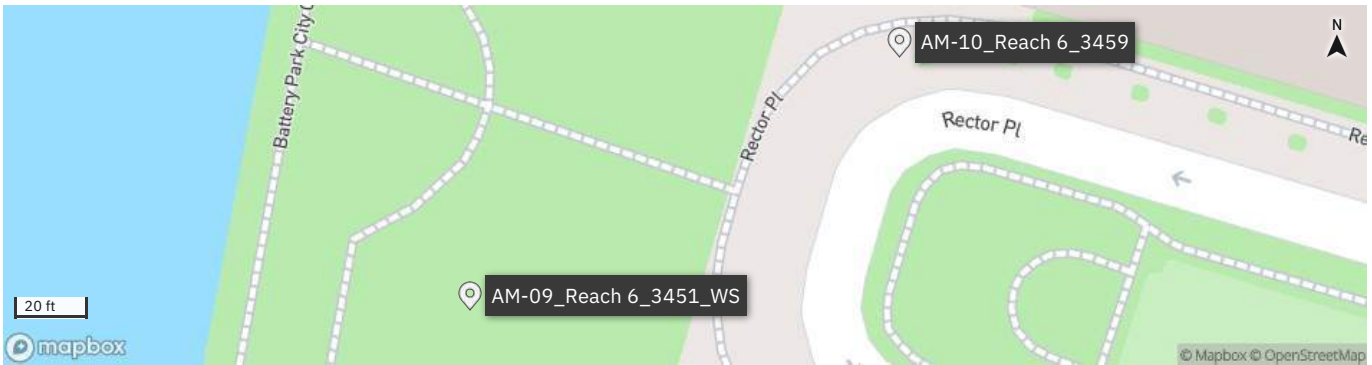


PM2.5 Average Contribution (µg/m³)

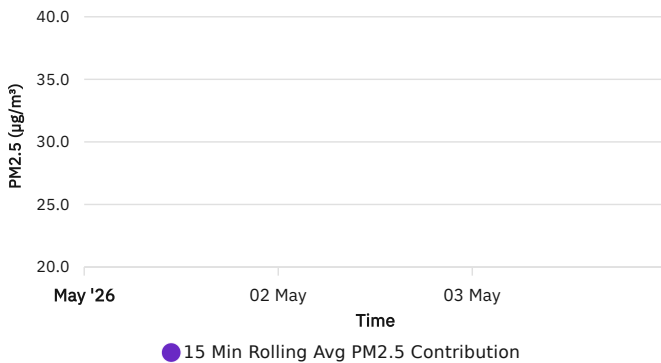


PM10 Average Contribution (µg/m³)




### VOC Average Contribution (ppm)



### AM-09\_Reach 6\_3451\_WS



### AM-10\_Reach 6\_3459



No data was found for the selected reporting range.



Reach 6 (Rector St)\_EWP\_AQS Report


Battery Park\_AQS

Report Period


From:	05/04/2026 00:00
To:	05/10/2026 23:59
PM10 Action Level:	100 µg/m³
PM2.5 Action Level:	25 µg/m³
VOC Action Level:	5 ppm

Daily Environmental Summary	Temp (°F)	Relative Humidity (%)	Barometer (inHg)	Wind Speed (mph)	Prevailing Wind Direction
05/04/2026	-	-	-	-	-
05/05/2026	-	-	-	-	-
05/06/2026	69.6 - 73.2	48.1 - 57.7	29.8 - 29.9	0.3 - 0.5	E
05/07/2026	71.4 - 72.3	41.0 - 48.1	29.9 - 30.0	0.2 - 0.5	E
05/08/2026	54.5 - 62.1	32.8 - 52.0	29.7 - 30.8	0.3 - 19.3	SW
05/09/2026	52.9 - 65.7	49.1 - 84.6	29.7 - 33.3	0.3 - 9.9	E
05/10/2026	51.1 - 67.5	60.9 - 88.4	29.7 - 31.1	0.4 - 6.9	SSW


Daily Monitoring Summary	PM2.5 (µg/m³)	Time	PM10 (µg/m³)	Time	VOC (ppm)	Time
Min Contribution (15 min avg.) - 5/4/2026	-	-	-	-	-	-
Max Contribution (15 min avg.) - 5/4/2026	-	-	-	-	-	-
Daily Avg. Contribution (15 min avg.) - 5/4/2026	-	-	-	-	-	-
Min Contribution (15 min avg.) - 5/5/2026	-	-	-	-	-	-
Max Contribution (15 min avg.) - 5/5/2026	-	-	-	-	-	-
Daily Avg. Contribution (15 min avg.) - 5/5/2026	-	-	-	-	-	-
Min Contribution (15 min avg.) - 5/6/2026	0.0	15:30	0.0	15:30	0.0000	17:45
Max Contribution (15 min avg.) - 5/6/2026	0.0	15:30	0.0	15:30	0.0100	15:30
Daily Avg. Contribution (15 min avg.) - 5/6/2026	0.0	-	0.0	-	0.0008	-
Min Contribution (15 min avg.) - 5/7/2026	0.0	00:00	0.0	00:00	0.0000	00:00
Max Contribution (15 min avg.) - 5/7/2026	0.0	00:00	0.0	00:00	0.0040	00:30
Daily Avg. Contribution (15 min avg.) - 5/7/2026	0.0	-	0.0	-	0.0002	-
Min Contribution (15 min avg.) - 5/8/2026	0.0	23:30	0.0	12:00	0.0000	10:00
Max Contribution (15 min avg.) - 5/8/2026	2.7	22:15	7.3	16:15	0.0027	21:30
Daily Avg. Contribution (15 min avg.) - 5/8/2026	1.5	-	1.5	-	0.0001	-
Min Contribution (15 min avg.) - 5/9/2026	0.0	00:30	0.0	00:30	0.0000	00:00
Max Contribution (15 min avg.) - 5/9/2026	4.9	23:00	5.7	01:45	0.0047	23:00
Daily Avg. Contribution (15 min avg.) - 5/9/2026	0.8	-	0.9	-	0.0002	-
Min Contribution (15 min avg.) - 5/10/2026	0.0	00:00	0.0	00:00	0.0000	00:00
Max Contribution (15 min avg.) - 5/10/2026	13.6	12:00	14.6	12:00	0.0073	12:00
Daily Avg. Contribution (15 min avg.) - 5/10/2026	3.2	-	3.6	-	0.0009	-

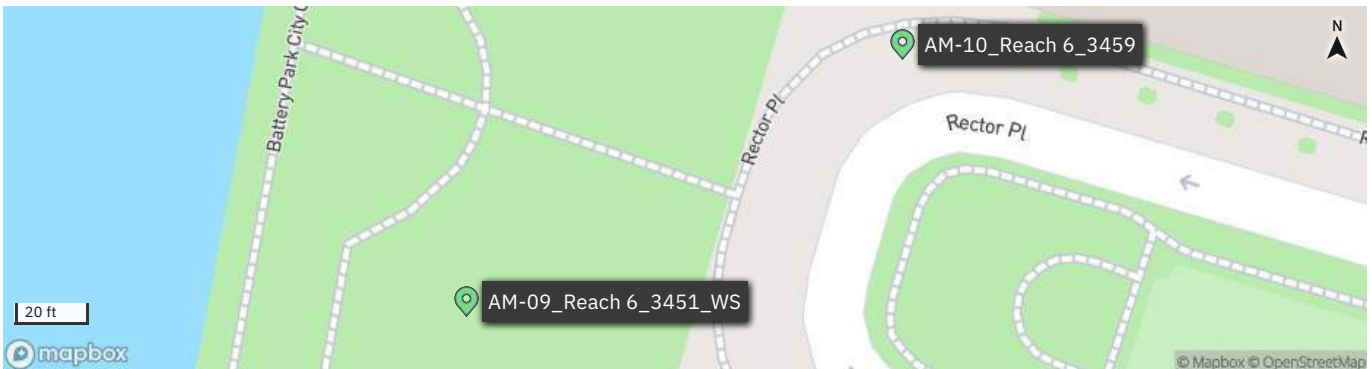

PM2.5 Average Contribution ( $\mu\text{g}/\text{m}^3$ )

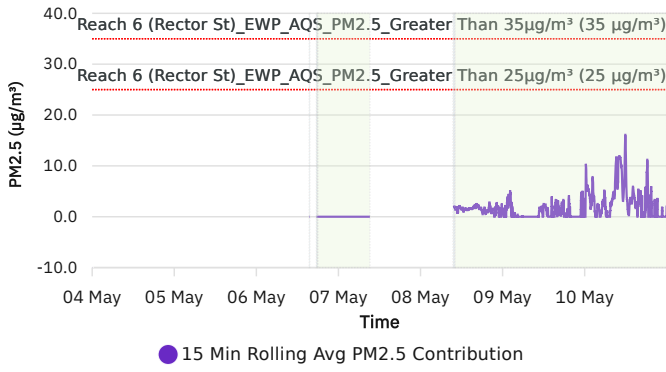


PM10 Average Contribution ( $\mu\text{g}/\text{m}^3$ )

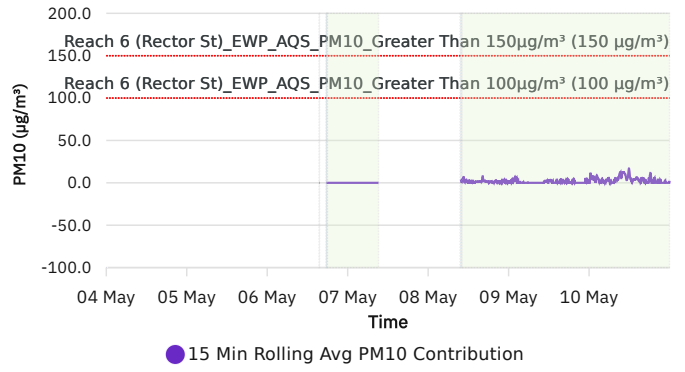


Stopped Initial Avg Rolling Avg


VOC Average Contribution (ppm)

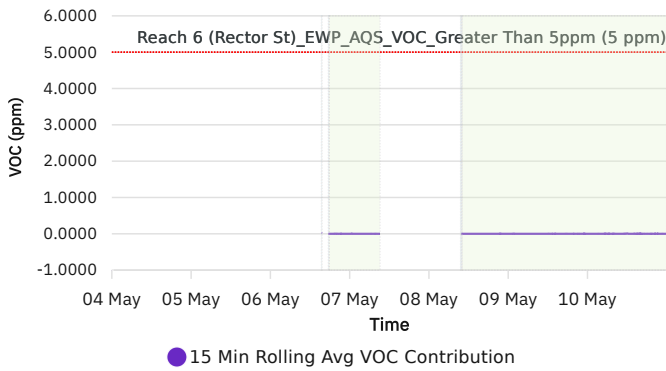


Wind rose (mph)

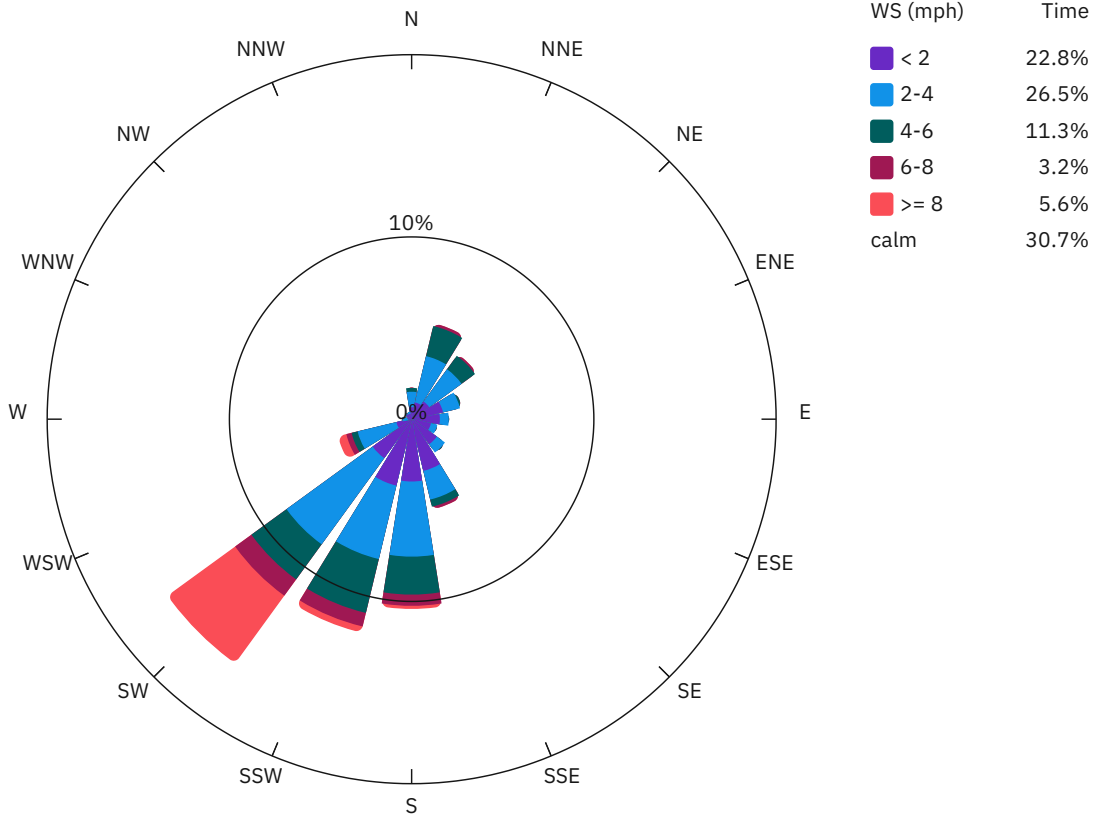

AM-09\_Reach 6\_3451\_WS

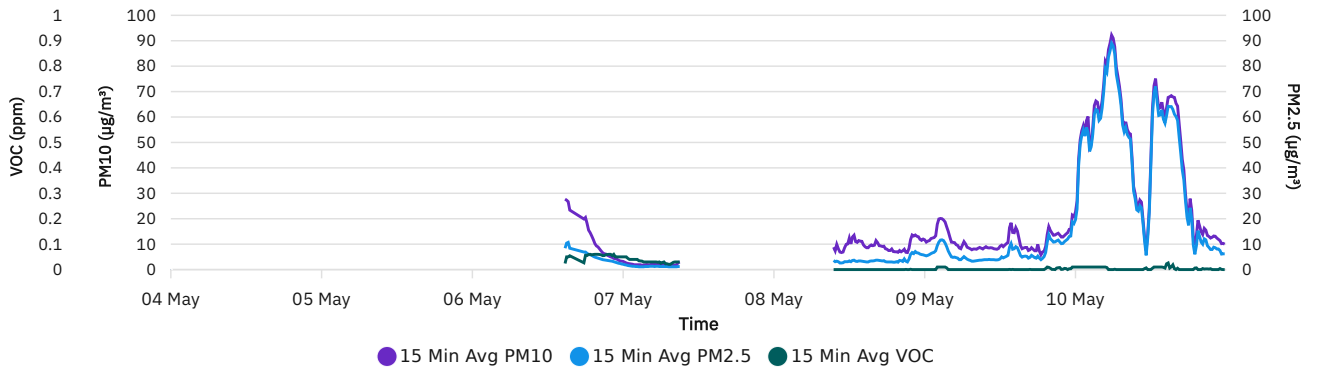

AM-10\_Reach 6\_3459

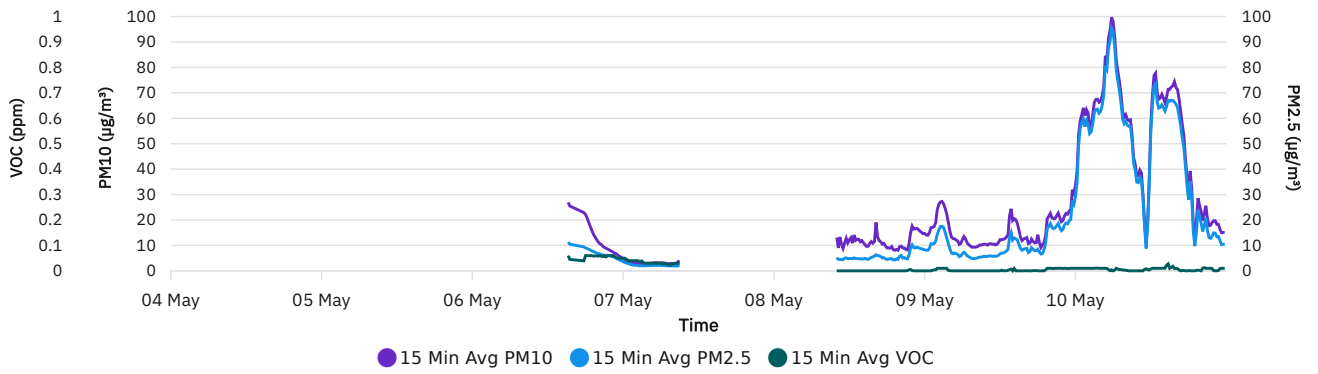




Reach 6 (Rector St)\_EWP\_AQS Report


Battery Park_AQS	
Report Period	
From:	05/11/2026 00:00
To:	05/17/2026 23:59
PM10 Action Level:	100 µg/m³
PM2.5 Action Level:	25 µg/m³
VOC Action Level:	5 ppm

Daily Environmental Summary	Temp (°F)	Relative Humidity (%)	Barometer (inHg)	Wind Speed (mph)	Prevailing Wind Direction
05/11/2026	52.2 - 62.4	27.3 - 71.7	30.0 - 31.2	0.5 - 11.6	S
05/12/2026	45.3 - 69.8	24.4 - 64.8	30.0 - 31.3	0.9 - 10.8	S
05/13/2026	51.8 - 73.9	34.8 - 66.3	29.8 - 32.9	0.5 - 11.9	NNE
05/14/2026	52.5 - 69.4	38.5 - 79.5	29.6 - 31.1	0.3 - 16.1	SSW
05/15/2026	50.0 - 66.2	44.8 - 68.2	29.7 - 31.9	0.6 - 12.8	S
05/16/2026	53.1 - 81.0	29.6 - 76.8	29.8 - 48.4	0.3 - 7.5	ESE
05/17/2026	65.8 - 84.9	38.5 - 56.1	29.8 - 31.2	0.5 - 5.6	E


Daily Monitoring Summary	PM2.5 (µg/m³)	Time	PM10 (µg/m³)	Time	VOC (ppm)	Time
Min Contribution (15 min avg.) - 5/11/2026	0.0	02:15	0.0	01:15	0.0000	00:00
Max Contribution (15 min avg.) - 5/11/2026	13.9	10:45	89.9	11:30	0.0473	13:30
Daily Avg. Contribution (15 min avg.) - 5/11/2026	1.0	-	3.7	-	0.0013	-
Min Contribution (15 min avg.) - 5/12/2026	0.0	00:45	0.0	00:45	0.0000	00:00
Max Contribution (15 min avg.) - 5/12/2026	7.4	10:00	39.6	10:00	0.0173	07:45
Daily Avg. Contribution (15 min avg.) - 5/12/2026	0.7	-	2.5	-	0.0007	-
Min Contribution (15 min avg.) - 5/13/2026	0.0	00:00	0.0	00:00	0.0000	00:00
Max Contribution (15 min avg.) - 5/13/2026	2.2	17:00	41.6	17:00	0.0100	11:00
Daily Avg. Contribution (15 min avg.) - 5/13/2026	0.1	-	4.1	-	0.0002	-
Min Contribution (15 min avg.) - 5/14/2026	0.0	00:00	0.0	00:00	0.0000	00:00
Max Contribution (15 min avg.) - 5/14/2026	9.9	08:45	22.4	18:45	0.0187	08:45
Daily Avg. Contribution (15 min avg.) - 5/14/2026	0.9	-	1.8	-	0.0006	-
Min Contribution (15 min avg.) - 5/15/2026	0.0	02:15	0.0	02:15	0.0000	00:00
Max Contribution (15 min avg.) - 5/15/2026	1.7	21:30	8.0	11:15	0.0020	08:45
Daily Avg. Contribution (15 min avg.) - 5/15/2026	0.6	-	1.1	-	0.0001	-
Min Contribution (15 min avg.) - 5/16/2026	0.0	00:00	0.0	00:00	0.0000	00:00
Max Contribution (15 min avg.) - 5/16/2026	3.5	09:30	3.2	09:30	0.0060	09:15
Daily Avg. Contribution (15 min avg.) - 5/16/2026	0.3	-	0.4	-	0.0004	-
Min Contribution (15 min avg.) - 5/17/2026	0.0	00:00	0.0	00:00	0.0000	00:00
Max Contribution (15 min avg.) - 5/17/2026	2.3	05:00	2.4	05:00	0.0000	00:00
Daily Avg. Contribution (15 min avg.) - 5/17/2026	0.3	-	0.3	-	0.0000	-

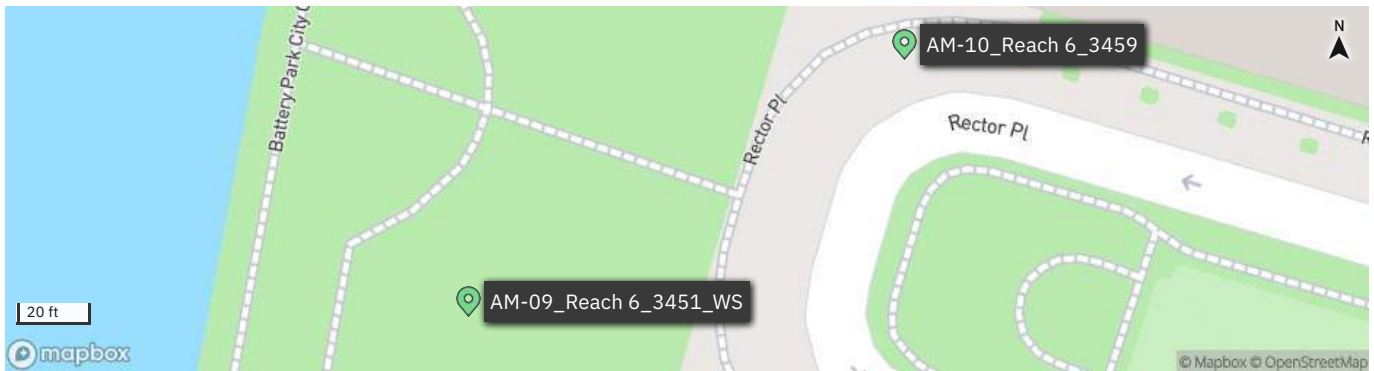

PM2.5 Average Contribution ( $\mu\text{g}/\text{m}^3$ )

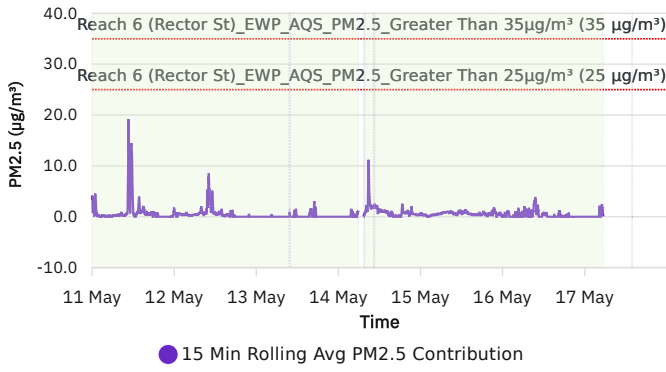


PM10 Average Contribution ( $\mu\text{g}/\text{m}^3$ )

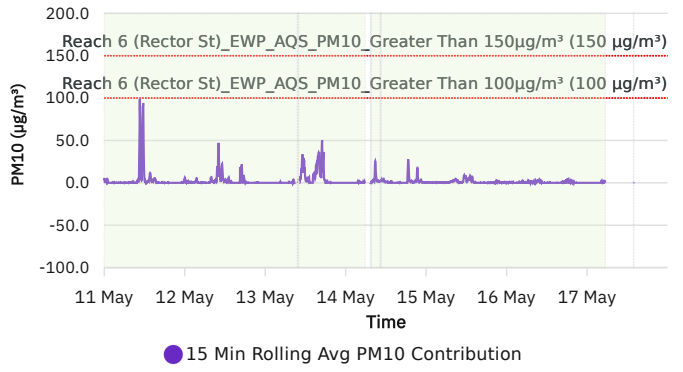


Stopped Initial Avg Rolling Avg


VOC Average Contribution (ppm)

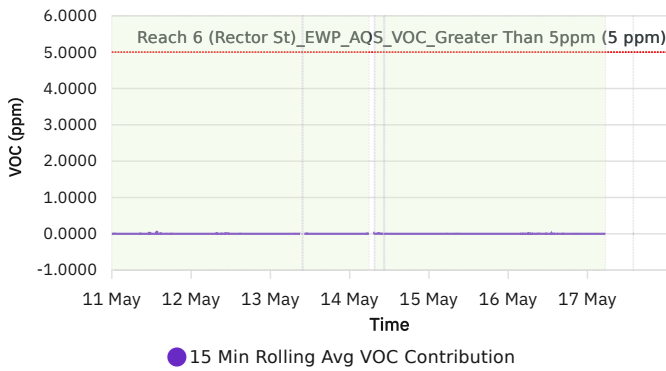


Wind rose (mph)

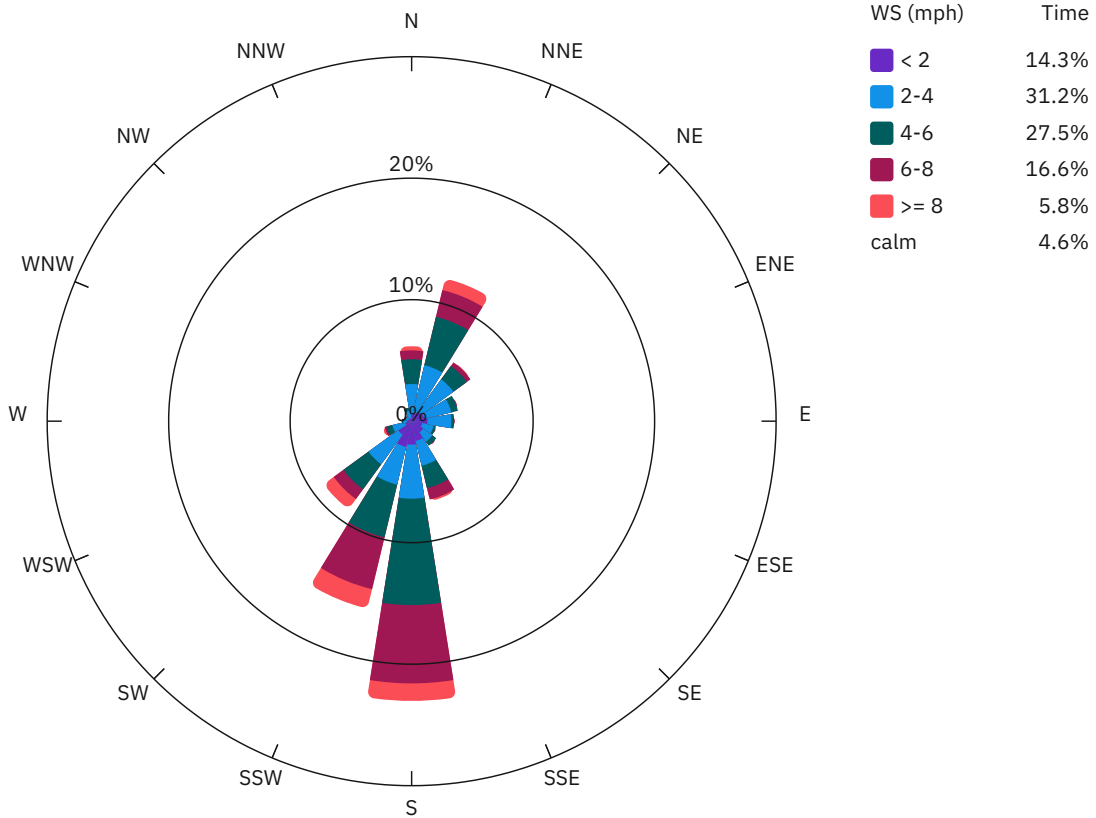

AM-09\_Reach 6\_3451\_WS

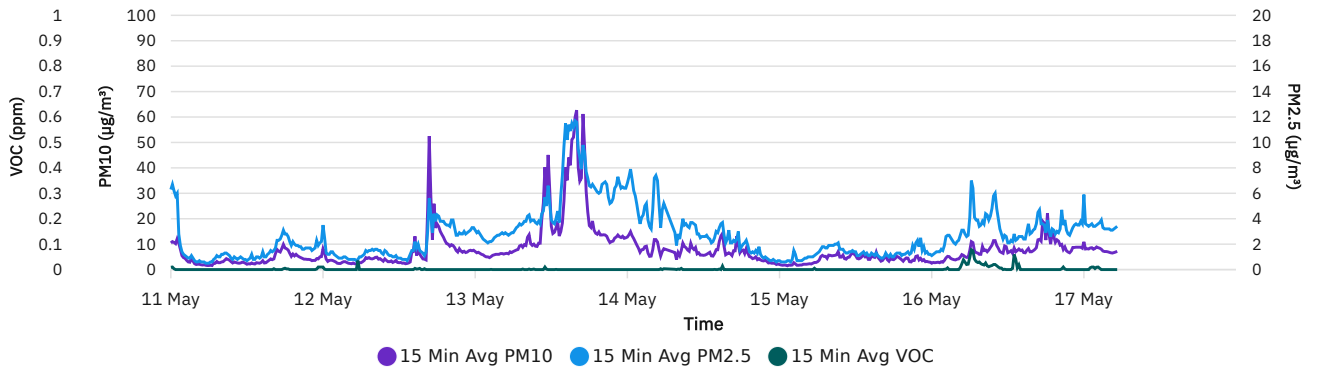

AM-10\_Reach 6\_3459

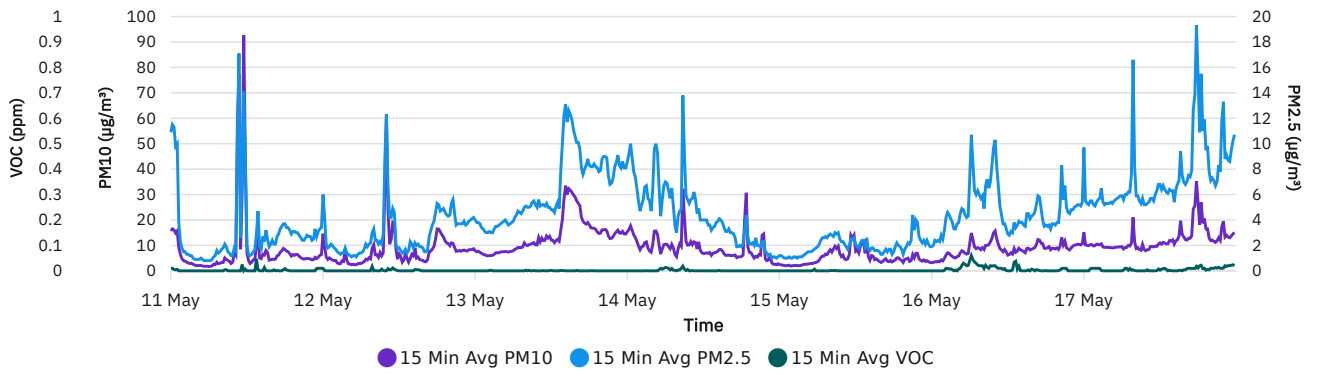




Reach 6 (Rector St)\_EWP\_AQS Report

Battery Park_AQS	
Report Period	
From:	05/18/2026 00:00
To:	05/24/2026 23:59
PM10 Action Level:	100 µg/m³
PM2.5 Action Level:	25 µg/m³
VOC Action Level:	5 ppm

Daily Environmental Summary	Temp (°F)	Relative Humidity (%)	Barometer (inHg)	Wind Speed (mph)	Prevailing Wind Direction
05/18/2026	63.9 - 87.8	39.7 - 71.9	29.8 - 30.7	0.8 - 9.2	NNW
05/19/2026	72.0 - 94.8	33.7 - 71.4	29.6 - 36.2	0.5 - 7.5	E
05/20/2026	65.7 - 93.6	37.5 - 90.5	29.9 - 30.9	0.3 - 22.0	S
05/21/2026	52.7 - 65.8	47.6 - 84.5	30.1 - 31.1	0.4 - 10.3	SSW
05/22/2026	55.6 - 68.2	37.5 - 54.0	30.2 - 31.1	0.7 - 12.4	SSW
05/23/2026	48.2 - 58.1	41.6 - 88.3	30.3 - 31.1	0.6 - 6.2	S
05/24/2026	48.7 - 54.7	85.4 - 90.9	30.2 - 31.0	0.5 - 6.2	SSE


Daily Monitoring Summary	PM2.5 (µg/m³)	Time	PM10 (µg/m³)	Time	VOC (ppm)	Time
Min Contribution (15 min avg.) - 5/18/2026	0.0	08:45	0.0	08:45	0.0000	09:15
Max Contribution (15 min avg.) - 5/18/2026	25.5	10:45	106.7	10:45	0.0200	08:45
Daily Avg. Contribution (15 min avg.) - 5/18/2026	3.3	-	6.0	-	0.0009	-
Min Contribution (15 min avg.) - 5/19/2026	0.0	00:00	0.0	00:00	0.0000	00:00
Max Contribution (15 min avg.) - 5/19/2026	9.5	12:00	39.1	13:15	0.0320	08:30
Daily Avg. Contribution (15 min avg.) - 5/19/2026	1.2	-	2.7	-	0.0013	-
Min Contribution (15 min avg.) - 5/20/2026	0.0	00:00	0.0	00:00	0.0000	00:00
Max Contribution (15 min avg.) - 5/20/2026	17.8	18:30	159.8	18:30	0.0073	12:30
Daily Avg. Contribution (15 min avg.) - 5/20/2026	1.8	-	3.9	-	0.0005	-
Min Contribution (15 min avg.) - 5/21/2026	0.0	20:00	0.0	03:45	0.0000	00:00
Max Contribution (15 min avg.) - 5/21/2026	2.2	19:45	2.4	20:45	0.0187	11:00
Daily Avg. Contribution (15 min avg.) - 5/21/2026	0.8	-	0.5	-	0.0006	-
Min Contribution (15 min avg.) - 5/22/2026	0.0	16:30	0.0	06:45	0.0000	00:00
Max Contribution (15 min avg.) - 5/22/2026	3.0	09:30	9.4	10:45	0.0007	00:45
Daily Avg. Contribution (15 min avg.) - 5/22/2026	1.0	-	1.5	-	0.0000	-
Min Contribution (15 min avg.) - 5/23/2026	0.3	05:00	0.3	05:00	0.0000	00:00
Max Contribution (15 min avg.) - 5/23/2026	1.7	12:30	1.7	01:15	0.0013	05:45
Daily Avg. Contribution (15 min avg.) - 5/23/2026	1.0	-	0.9	-	0.0000	-
Min Contribution (15 min avg.) - 5/24/2026	-	-	-	-	-	-
Max Contribution (15 min avg.) - 5/24/2026	-	-	-	-	-	-
Daily Avg. Contribution (15 min avg.) - 5/24/2026	-	-	-	-	-	-

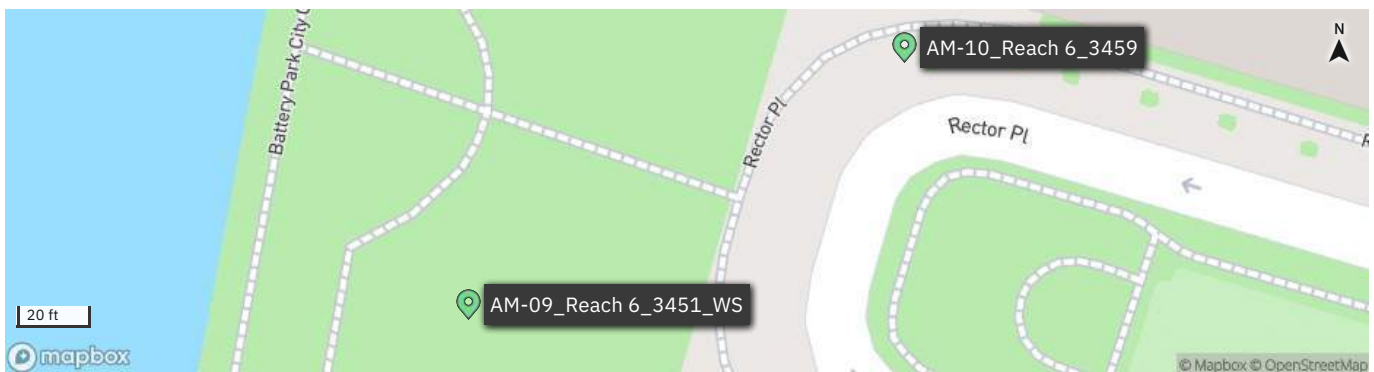


Stopped 
  Initial Avg 
  Rolling Avg

Stopped 
  Initial Avg 
  Rolling Avg

PM2.5 Average Contribution ( $\mu\text{g}/\text{m}^3$ )

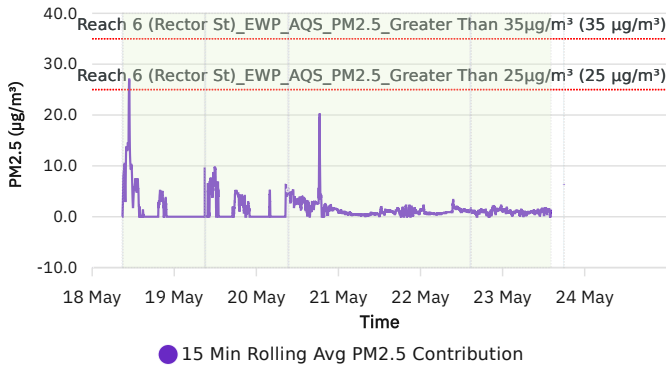


PM10 Average Contribution ( $\mu\text{g}/\text{m}^3$ )

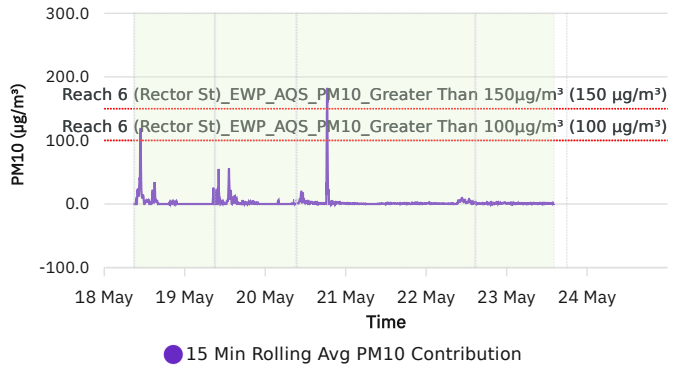


Stopped Initial Avg Rolling Avg


VOC Average Contribution (ppm)

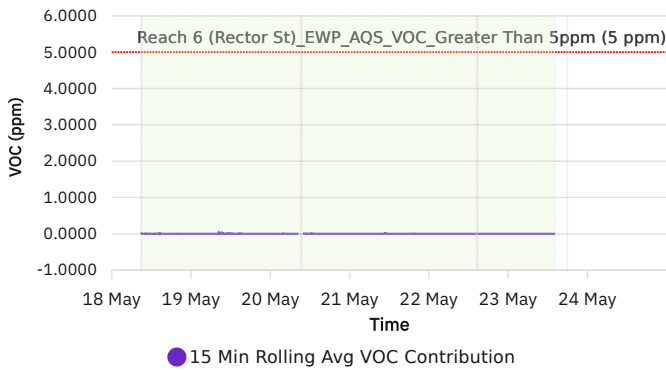


Wind rose (mph)

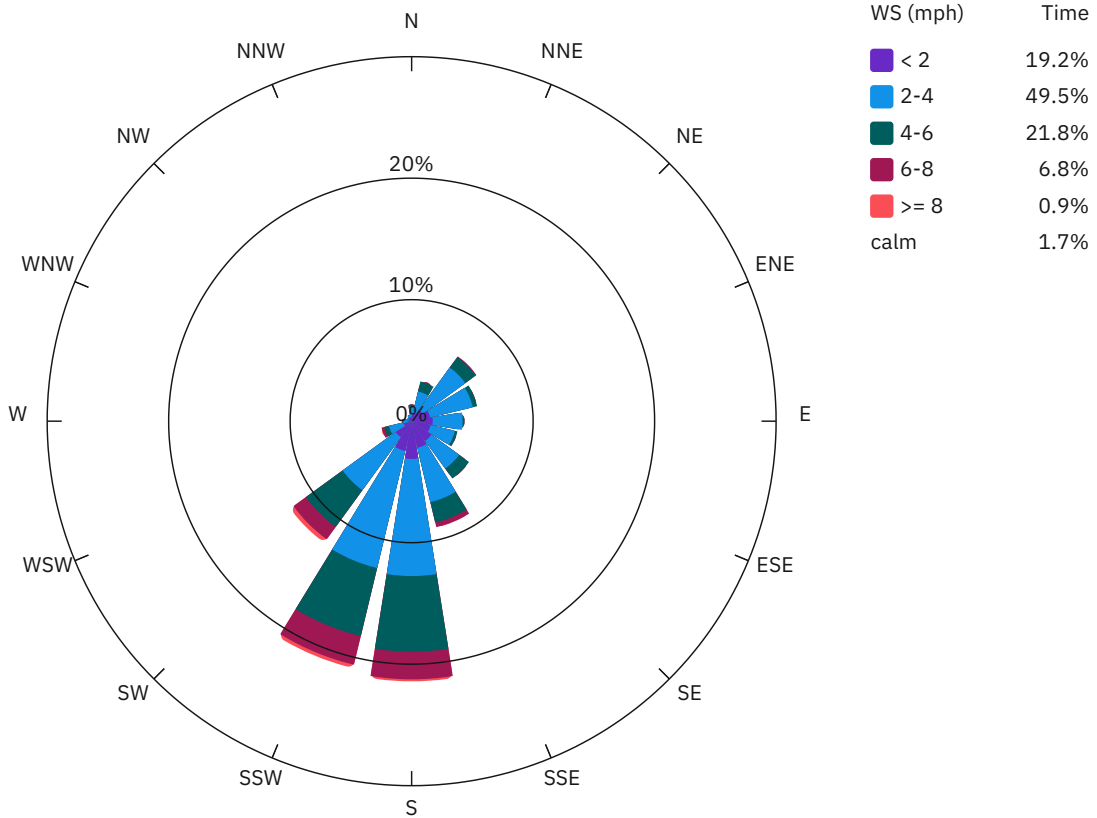

AM-09\_Reach 6\_3451\_WS

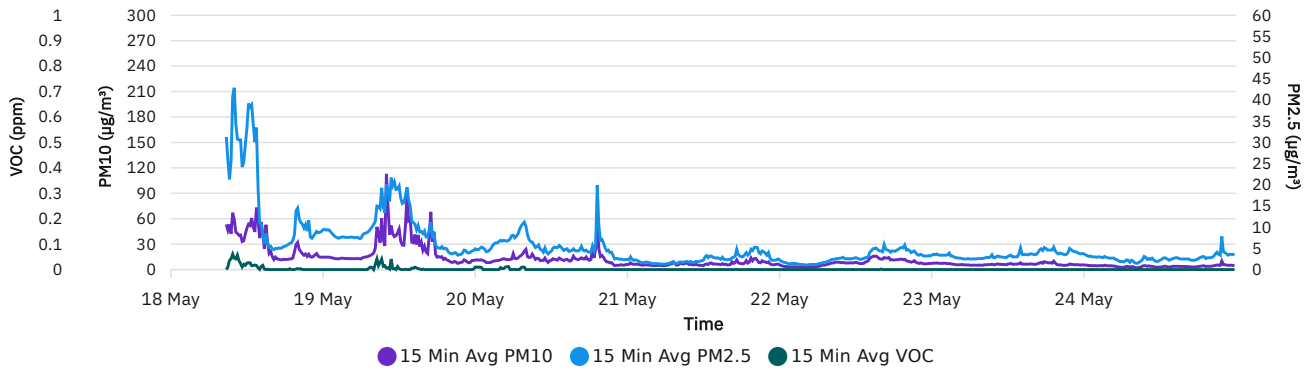

AM-10\_Reach 6\_3459

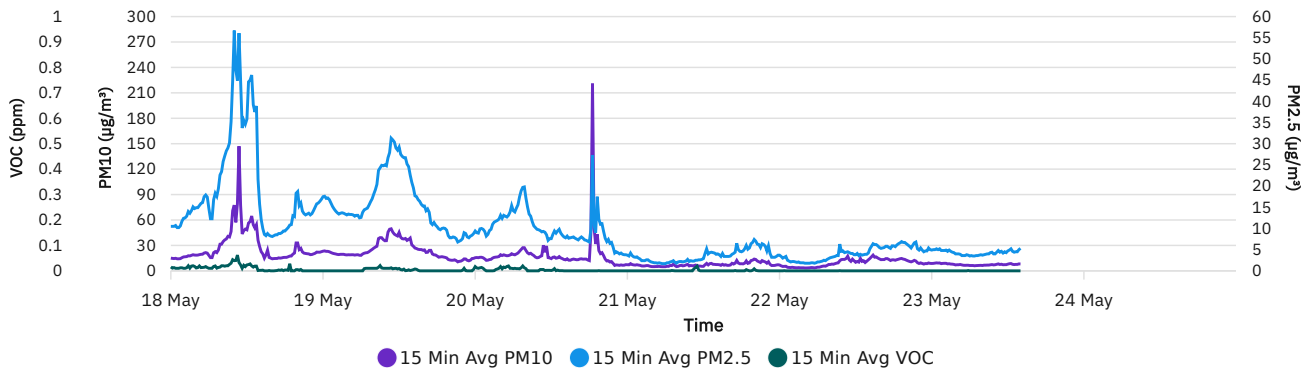

Exceedance Summary

Parameter	Action Level	Time Triggered	Cause	Mitigation
PM10	100.0 µg/m <sup>3</sup>	5/18/2026 10:44	Elevated readings were attributable to wind-blown dust across the site.	Contractor wetted the area to mitigate dust levels and fugitive dust.
PM10	100.0 µg/m <sup>3</sup>	5/20/2026 18:21	Elevated readings were attributable to wind-blown dust across the site.	Contractor wetted the area to mitigate dust levels and fugitive dust.
PM2.5	25.0 µg/m <sup>3</sup>	5/18/2026 10:45	Elevated readings were attributable to wind-blown dust across the site.	Contractor wetted the area to mitigate dust levels and fugitive dust.



Reach 6 (Rector St)\_EWP\_AQS Report


Battery Park_AQS	
Report Period	
From:	05/25/2026 00:00
To:	05/31/2026 23:59
PM10 Action Level:	100 µg/m³
PM2.5 Action Level:	25 µg/m³
VOC Action Level:	5 ppm

Daily Environmental Summary	Temp (°F)	Relative Humidity (%)	Barometer (inHg)	Wind Speed (mph)	Prevailing Wind Direction
05/25/2026	54.3 - 74.3	62.5 - 92.7	30.0 - 31.1	0.3 - 7.9	ESE
05/26/2026	59.9 - 80.8	37.3 - 86.6	30.0 - 31.1	0.3 - 5.6	S
05/27/2026	66.2 - 85.1	40.5 - 68.7	29.7 - 30.9	0.3 - 8.6	ESE
05/28/2026	61.3 - 75.6	36.0 - 56.1	29.8 - 31.0	1.4 - 14.5	S
05/29/2026	57.2 - 78.8	30.9 - 61.3	29.7 - 30.9	0.9 - 10.8	SW
05/30/2026	52.2 - 67.6	42.0 - 59.1	29.2 - 31.1	0.5 - 16.4	SW
05/31/2026	50.7 - 76.5	29.0 - 70.8	29.7 - 31.0	0.1 - 13.5	WSW


Daily Monitoring Summary	PM2.5 (µg/m³)	Time	PM10 (µg/m³)	Time	VOC (ppm)	Time
Min Contribution (15 min avg.) - 5/25/2026	-	-	-	-	-	-
Max Contribution (15 min avg.) - 5/25/2026	-	-	-	-	-	-
Daily Avg. Contribution (15 min avg.) - 5/25/2026	-	-	-	-	-	-
Min Contribution (15 min avg.) - 5/26/2026	0.0	13:30	0.0	13:30	0.0000	09:30
Max Contribution (15 min avg.) - 5/26/2026	3.3	10:00	3.5	09:45	0.0127	12:30
Daily Avg. Contribution (15 min avg.) - 5/26/2026	0.8	-	0.7	-	0.0013	-
Min Contribution (15 min avg.) - 5/27/2026	0.0	00:00	0.0	00:00	0.0000	00:00
Max Contribution (15 min avg.) - 5/27/2026	4.6	11:30	5.1	11:30	0.0013	10:15
Daily Avg. Contribution (15 min avg.) - 5/27/2026	0.5	-	0.6	-	0.0000	-
Min Contribution (15 min avg.) - 5/28/2026	0.0	16:30	0.0	07:30	0.0000	00:00
Max Contribution (15 min avg.) - 5/28/2026	2.2	15:15	20.1	15:15	0.0027	10:15
Daily Avg. Contribution (15 min avg.) - 5/28/2026	0.7	-	1.1	-	0.0001	-
Min Contribution (15 min avg.) - 5/29/2026	0.0	00:00	0.0	00:00	0.0000	00:00
Max Contribution (15 min avg.) - 5/29/2026	6.8	12:30	61.8	12:30	0.0100	23:30
Daily Avg. Contribution (15 min avg.) - 5/29/2026	1.5	-	5.4	-	0.0005	-
Min Contribution (15 min avg.) - 5/30/2026	0.0	01:00	0.0	01:00	0.0000	00:30
Max Contribution (15 min avg.) - 5/30/2026	38.7	04:15	366.5	04:15	0.0007	00:00
Daily Avg. Contribution (15 min avg.) - 5/30/2026	3.0	-	26.1	-	0.0000	-
Min Contribution (15 min avg.) - 5/31/2026	0.0	06:45	0.0	06:45	0.0000	00:00
Max Contribution (15 min avg.) - 5/31/2026	6.3	06:00	7.6	06:00	0.0087	01:30
Daily Avg. Contribution (15 min avg.) - 5/31/2026	1.5	-	2.1	-	0.0004	-



PM2.5 Average Contribution ( $\mu\text{g}/\text{m}^3$ )

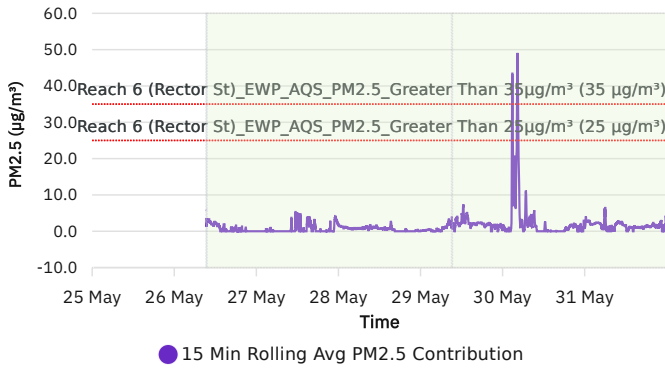


PM10 Average Contribution ( $\mu\text{g}/\text{m}^3$ )

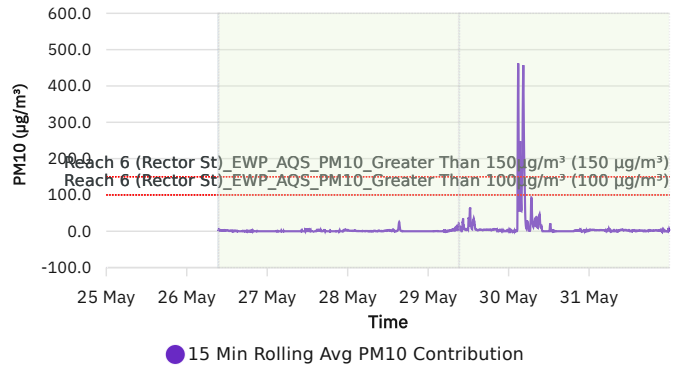


Stopped Initial Avg Rolling Avg


VOC Average Contribution (ppm)

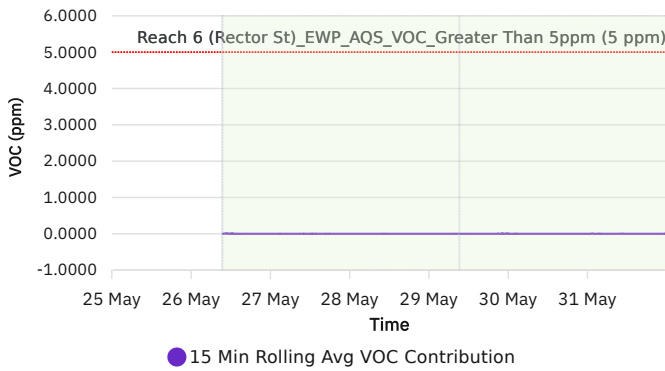


Wind rose (mph)

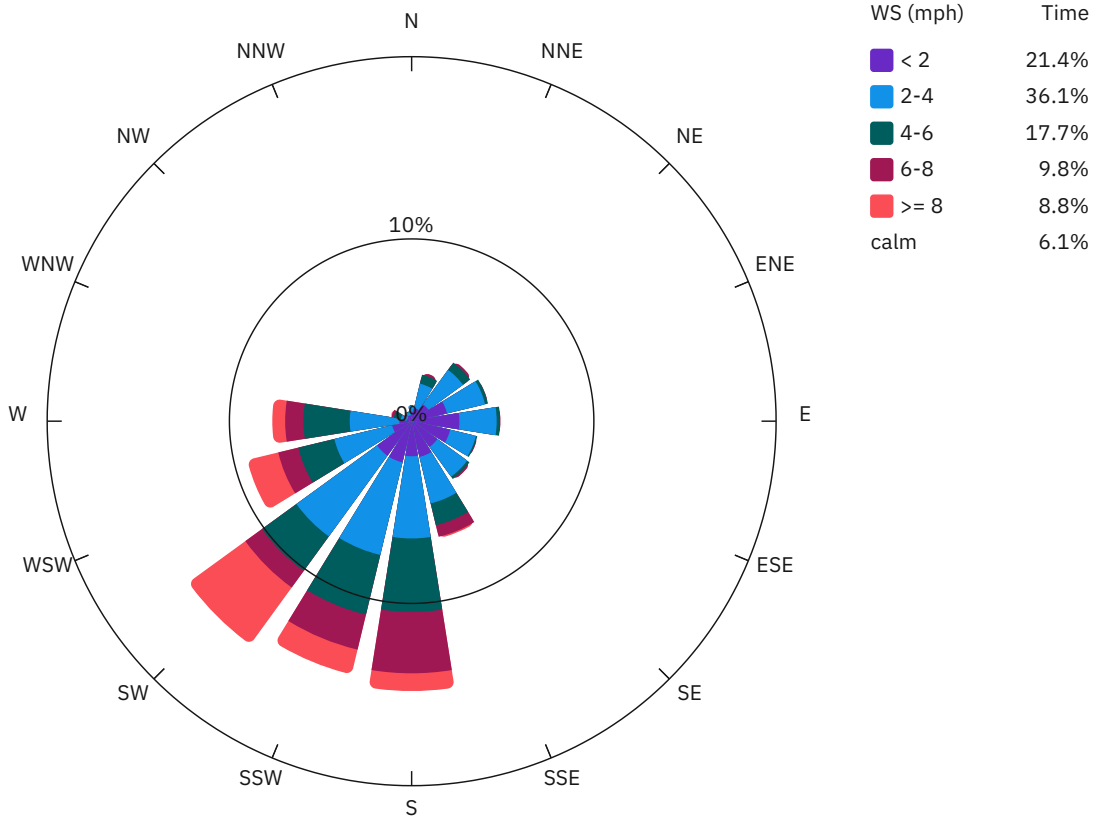

AM-09\_Reach 6\_3451\_WS

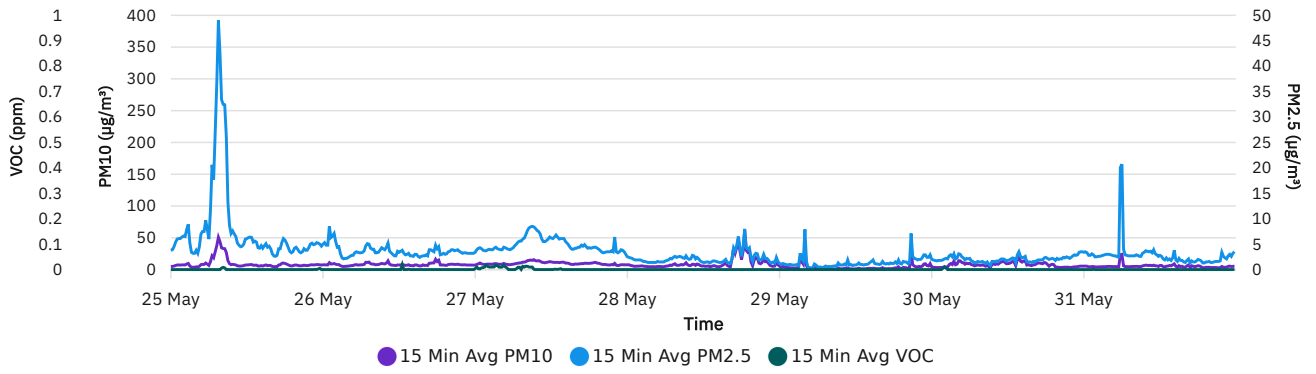

AM-10\_Reach 6\_3459

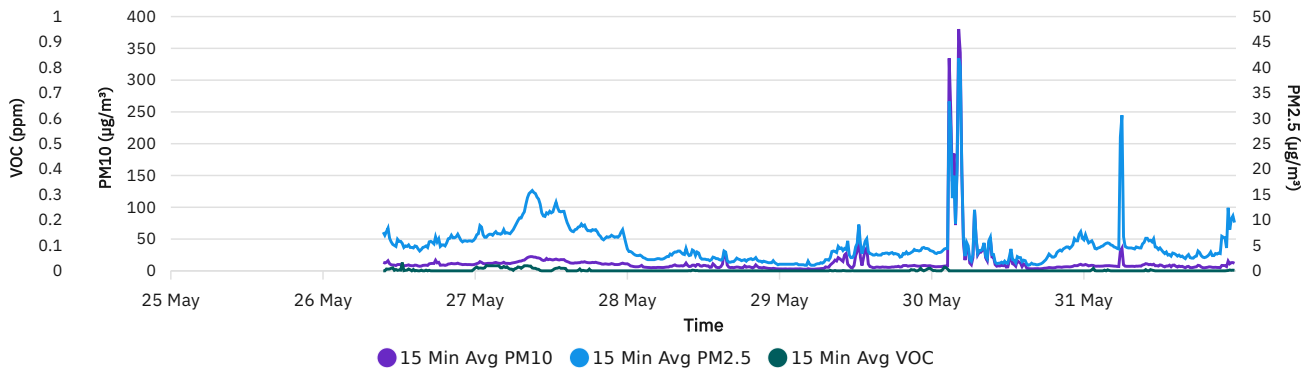

Exceedance Summary

Parameter	Action Level	Time Triggered	Cause	Mitigation
PM10	100.0 µg/m³	5/30/2026 02:40	Elevated readings were attributable to wind-blown dust across the site.	Contractor wetted the area to mitigate dust levels and fugitive dust.
PM10	100.0 µg/m³	5/30/2026 03:14	Elevated readings were attributable to wind-blown dust across the site.	Contractor wetted the area to mitigate dust levels and fugitive dust.
PM10	100.0 µg/m³	5/30/2026 03:54	Elevated readings were attributable to wind-blown dust across the site.	Contractor wetted the area to mitigate dust levels and fugitive dust.
PM2.5	25.0 µg/m³	5/30/2026 02:44	Elevated readings were attributable to wind-blown dust across the site.	Contractor wetted the area to mitigate dust levels and fugitive dust.
PM2.5	25.0 µg/m³	5/30/2026 04:10	Elevated readings were attributable to wind-blown dust across the site.	Contractor wetted the area to mitigate dust levels and fugitive dust.



Reach 7\_Stage\_7ABC Report


Battery Park\_AQS

Report Period

From:	05/01/2026 00:00
To:	05/03/2026 23:59
PM10 Action Level:	100 µg/m³
PM2.5 Action Level:	25 µg/m³
VOC Action Level:	5 ppm

Daily Environmental Summary	Temp (°F)	Relative Humidity (%)	Barometer (inHg)	Wind Speed (mph)	Prevailing Wind Direction
05/01/2026	46.4 - 65.1	29.6 - 62.1	29.9 - 30.6	0.3 - 6.8	SE
05/02/2026	49.8 - 69.1	24.5 - 71.2	29.8 - 30.1	0.2 - 4.8	E
05/03/2026	44.1 - 63.5	20.0 - 53.3	29.9 - 30.4	0.4 - 8.3	ENE


Daily Monitoring Summary	PM2.5 (µg/m³)	Time	PM10 (µg/m³)	Time	VOC (ppm)	Time
Min Contribution (15 min avg.) - 5/1/2026	0.0	00:00	0.0	00:15	0.0000	00:00
Max Contribution (15 min avg.) - 5/1/2026	1.6	08:30	7.7	08:30	0.1160	08:00
Daily Avg. Contribution (15 min avg.) - 5/1/2026	0.1	-	0.5	-	0.0345	-
Min Contribution (15 min avg.) - 5/2/2026	0.1	00:00	0.0	05:30	0.0400	08:15
Max Contribution (15 min avg.) - 5/2/2026	6.0	15:45	9.4	15:15	0.0600	15:15
Daily Avg. Contribution (15 min avg.) - 5/2/2026	0.6	-	0.8	-	0.0528	-
Min Contribution (15 min avg.) - 5/3/2026	0.1	15:30	0.0	15:30	0.0300	08:15
Max Contribution (15 min avg.) - 5/3/2026	3.5	17:45	3.8	17:45	0.0600	20:15
Daily Avg. Contribution (15 min avg.) - 5/3/2026	0.5	-	0.8	-	0.0452	-

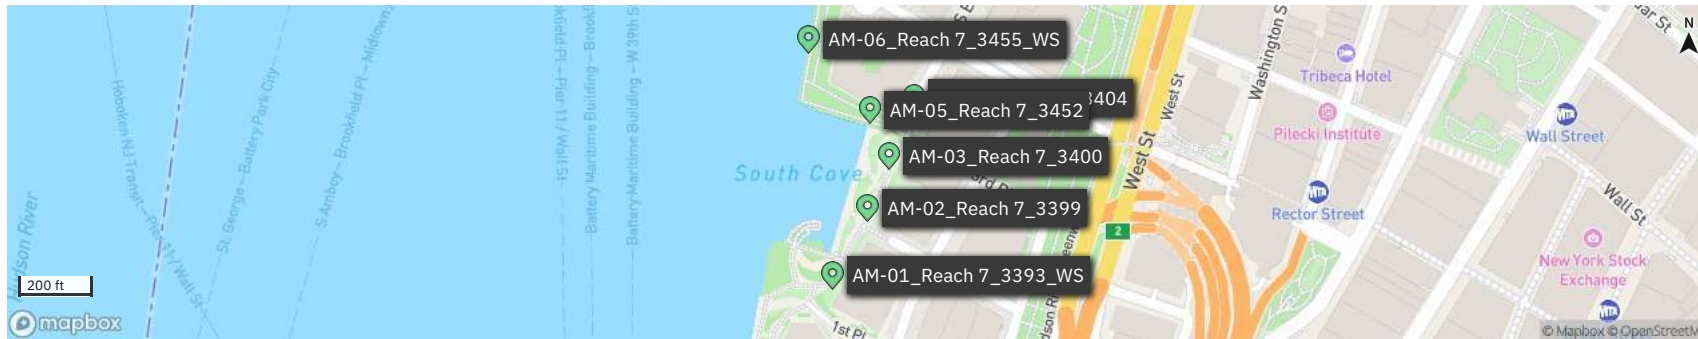


Stopped  Rolling Avg

Stopped  Rolling Avg

PM2.5 Average Contribution ( $\mu\text{g}/\text{m}^3$ )

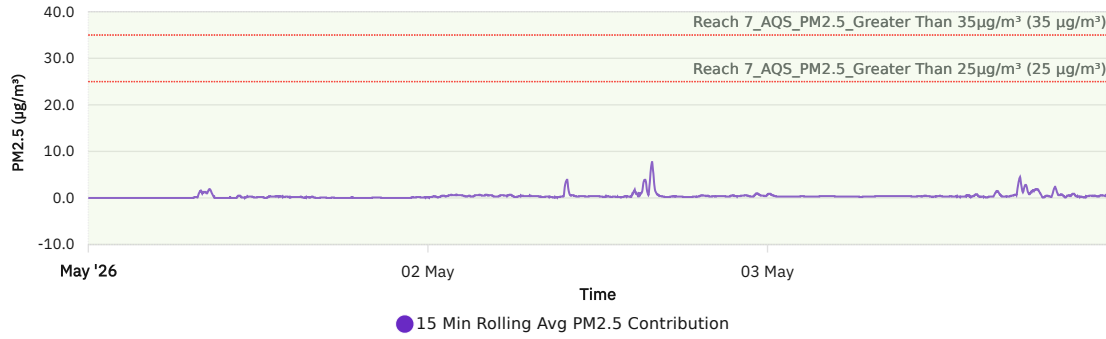


PM10 Average Contribution ( $\mu\text{g}/\text{m}^3$ )

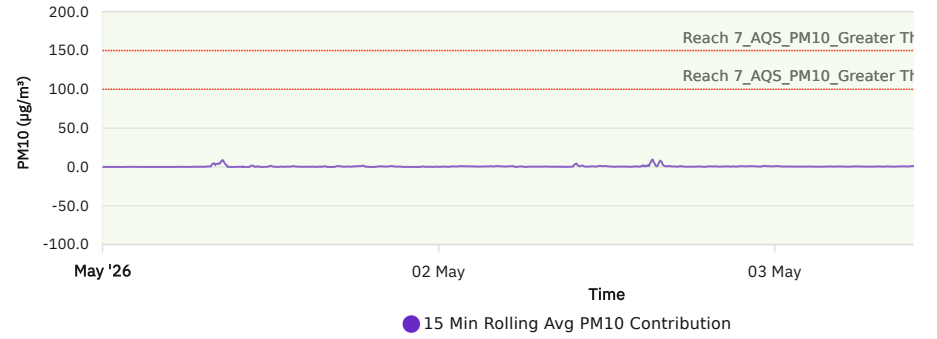


Stopped Rolling Avg


VOC Average Contribution (ppm)

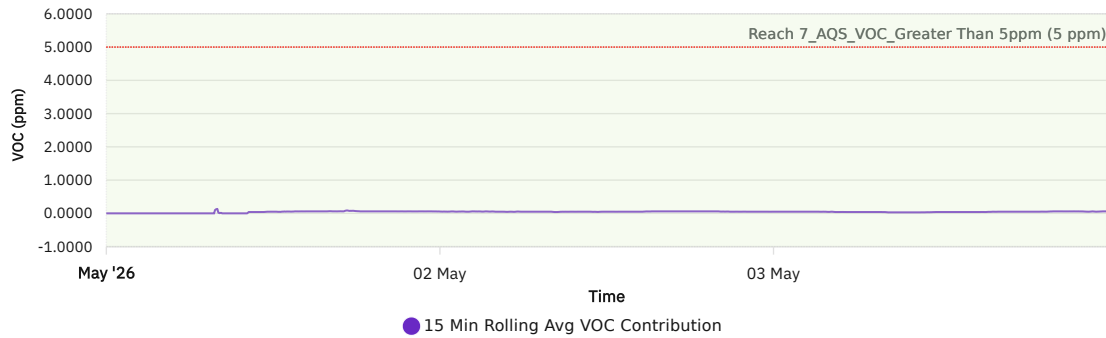


Wind rose (mph)

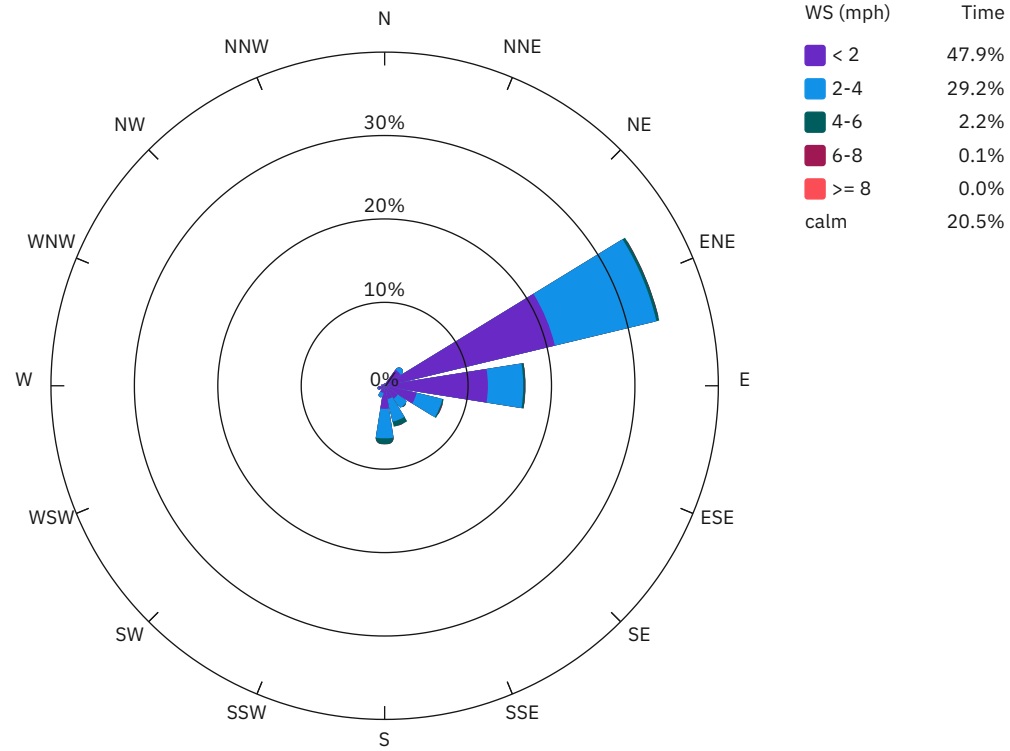


AM-01\_Reach 7\_3393\_WS

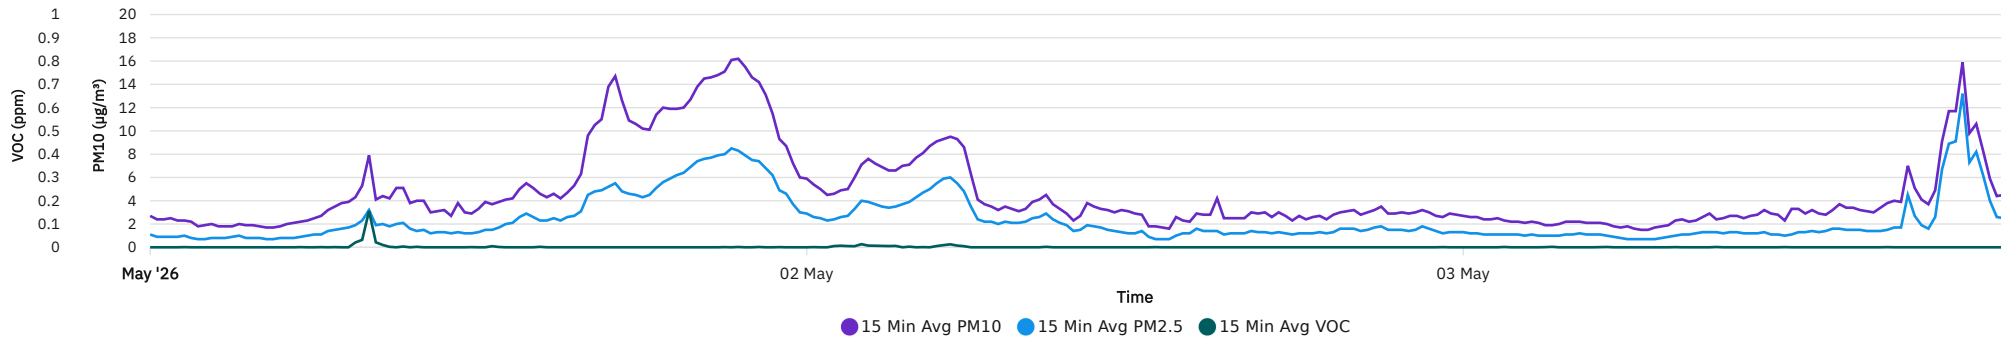


AM-02\_Reach 7\_3399

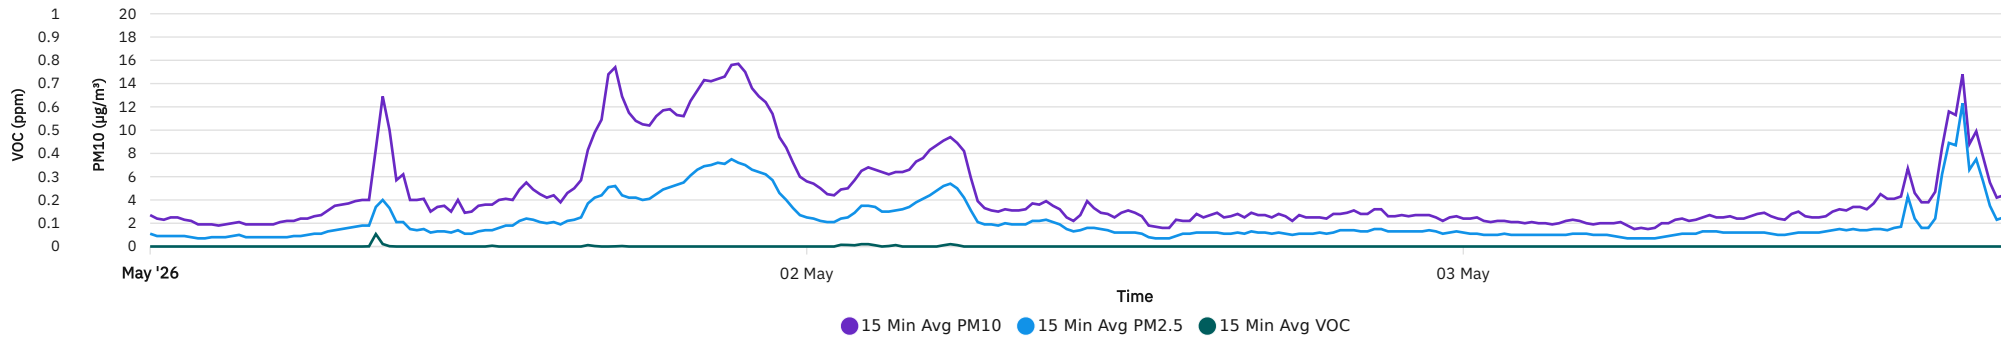


AM-03\_Reach 7\_3400

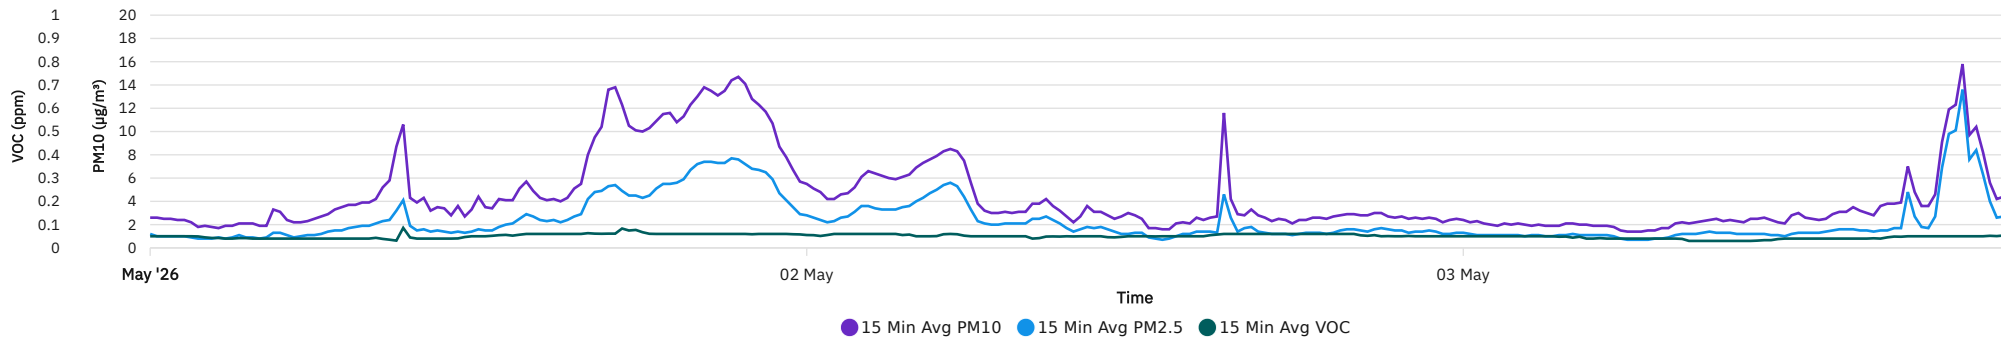


AM-04\_Reach 7\_3404

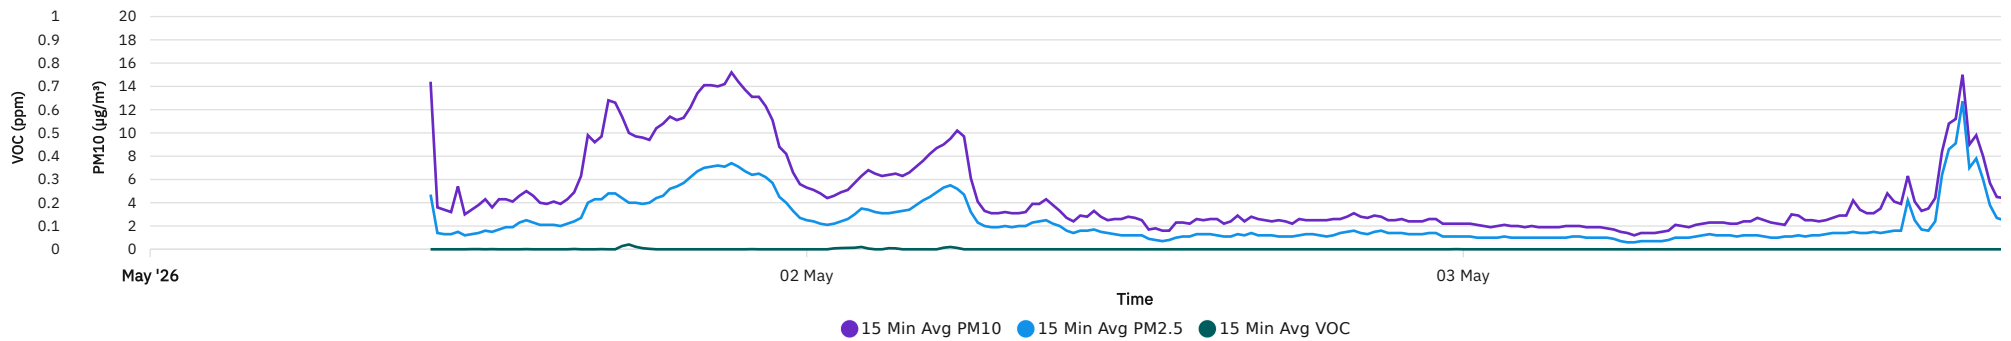

AM-05\_Reach 7\_3452

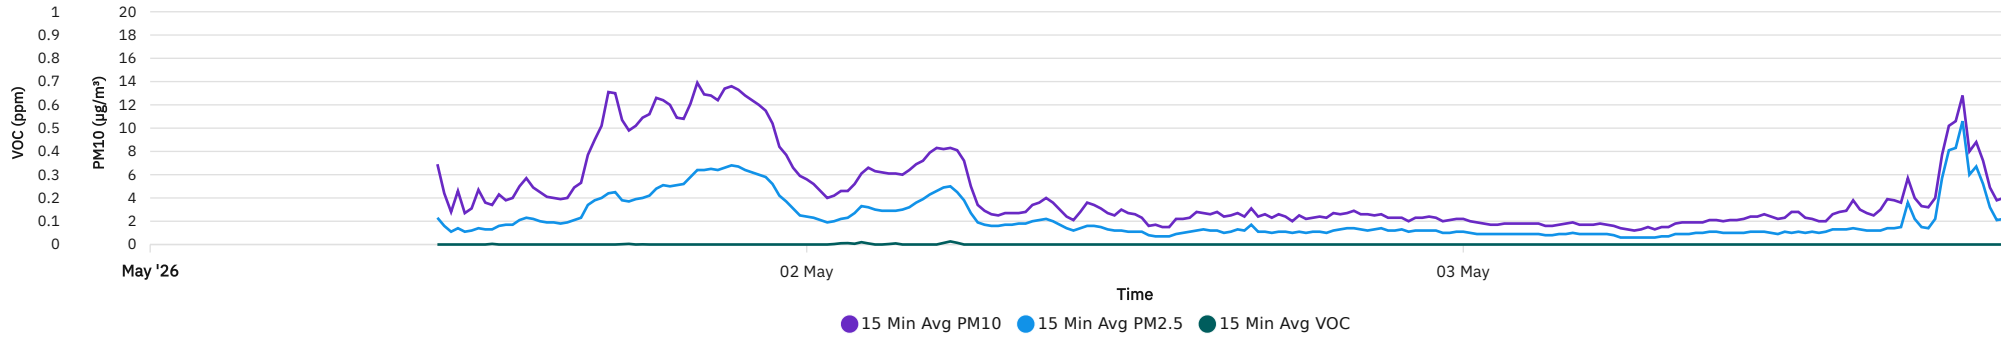

AM-06\_Reach 7\_3455\_WS

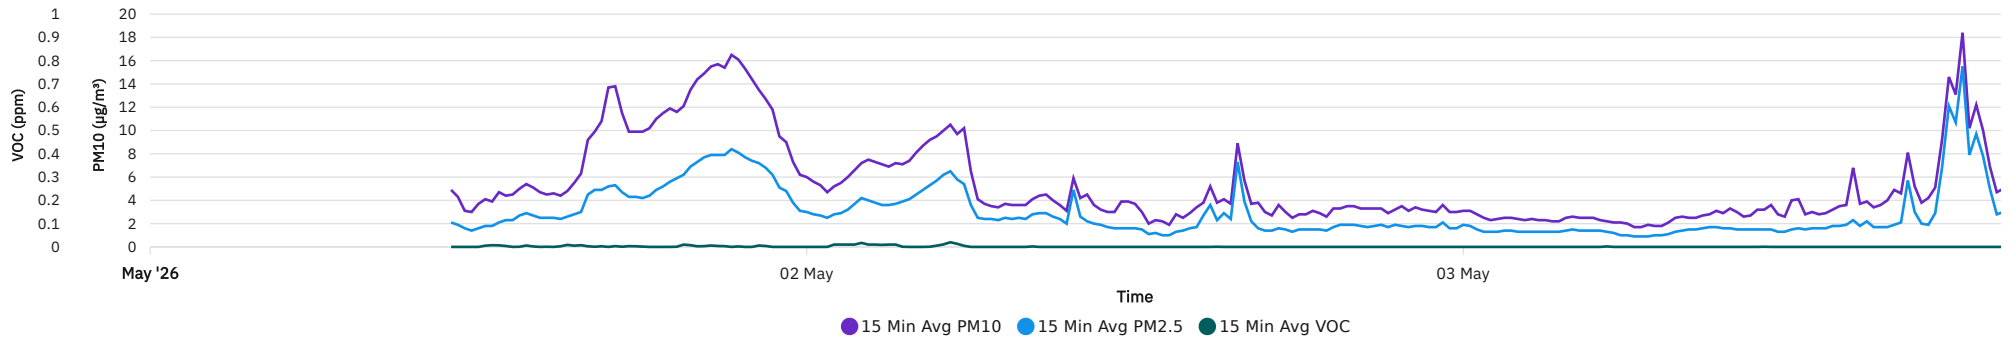



Reach 7\_Stage\_7ABC Report


Battery Park\_AQS


Report Period

From:	05/04/2026 00:00
To:	05/10/2026 23:59
PM10 Action Level:	100 µg/m³
PM2.5 Action Level:	25 µg/m³
VOC Action Level:	5 ppm

Daily Environmental Summary	Temp (°F)	Relative Humidity (%)	Barometer (inHg)	Wind Speed (mph)	Prevailing Wind Direction
05/04/2026	48.4 - 72.7	27.8 - 57.8	29.8 - 30.2	0.5 - 7.3	SSE
05/05/2026	57.6 - 85.5	28.6 - 63.2	29.8 - 30.1	0.3 - 8.8	SSE
05/06/2026	53.2 - 66.9	56.1 - 88.2	29.8 - 30.0	0.2 - 7.7	SSE
05/07/2026	47.7 - 72.0	22.6 - 83.8	29.8 - 30.0	0.3 - 5.3	ENE
05/08/2026	46.9 - 66.2	28.5 - 69.8	29.8 - 30.0	0.3 - 3.8	E
05/09/2026	52.0 - 67.6	49.9 - 87.2	29.9 - 30.0	-	-
05/10/2026	50.4 - 70.0	56.3 - 90.7	29.9 - 30.0	-	-


Daily Monitoring Summary	PM2.5 (µg/m³)	Time	PM10 (µg/m³)	Time	VOC (ppm)	Time
Min Contribution (15 min avg.) - 5/4/2026	0.0	06:30	0.0	05:45	0.0000	10:15
Max Contribution (15 min avg.) - 5/4/2026	1.7	04:45	5.6	11:30	0.1073	15:15
Daily Avg. Contribution (15 min avg.) - 5/4/2026	0.2	-	1.0	-	0.0621	-
Min Contribution (15 min avg.) - 5/5/2026	0.0	00:00	0.0	00:00	0.0000	09:15
Max Contribution (15 min avg.) - 5/5/2026	56.8	11:15	229.0	11:15	0.1300	19:00
Daily Avg. Contribution (15 min avg.) - 5/5/2026	1.9	-	7.1	-	0.0797	-
Min Contribution (15 min avg.) - 5/6/2026	0.0	00:00	0.0	00:00	0.0547	09:15
Max Contribution (15 min avg.) - 5/6/2026	4.8	09:15	65.0	09:15	0.1427	13:45
Daily Avg. Contribution (15 min avg.) - 5/6/2026	0.6	-	3.8	-	0.0904	-
Min Contribution (15 min avg.) - 5/7/2026	0.0	08:15	0.0	08:30	0.0407	08:15
Max Contribution (15 min avg.) - 5/7/2026	18.2	11:15	78.3	11:15	0.1327	11:00
Daily Avg. Contribution (15 min avg.) - 5/7/2026	1.3	-	5.3	-	0.0658	-
Min Contribution (15 min avg.) - 5/8/2026	0.3	00:15	0.3	00:15	0.0587	01:15
Max Contribution (15 min avg.) - 5/8/2026	1.2	02:30	6.0	02:30	0.0787	00:00
Daily Avg. Contribution (15 min avg.) - 5/8/2026	0.5	-	1.1	-	0.0664	-
Min Contribution (15 min avg.) - 5/9/2026	-	-	-	-	-	-
Max Contribution (15 min avg.) - 5/9/2026	-	-	-	-	-	-
Daily Avg. Contribution (15 min avg.) - 5/9/2026	-	-	-	-	-	-
Min Contribution (15 min avg.) - 5/10/2026	-	-	-	-	-	-
Max Contribution (15 min avg.) - 5/10/2026	-	-	-	-	-	-
Daily Avg. Contribution (15 min avg.) - 5/10/2026	-	-	-	-	-	-



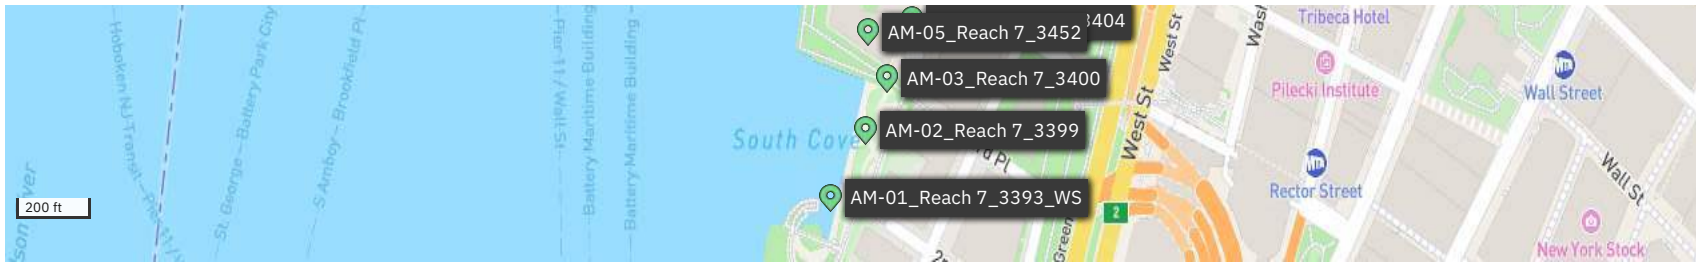

Stopped 
  Initial Avg 
  Rolling Avg


PM2.5 Average Contribution ( $\mu\text{g}/\text{m}^3$ )

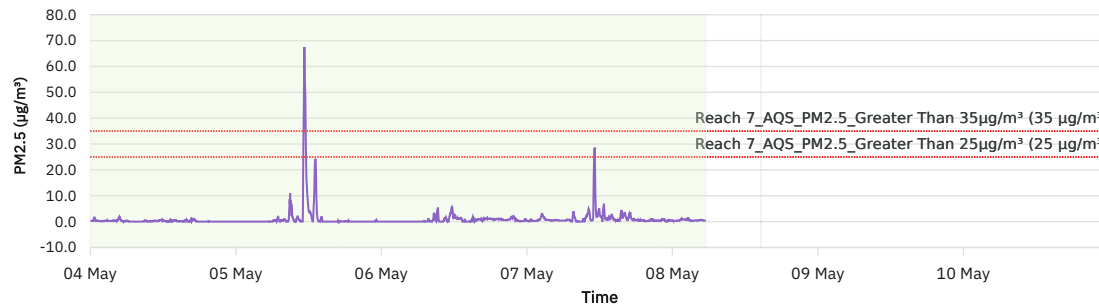

● 15 Min Rolling Avg PM2.5 Contribution

Stopped 
  Initial Avg 
  Rolling Avg


PM10 Average Contribution ( $\mu\text{g}/\text{m}^3$ )

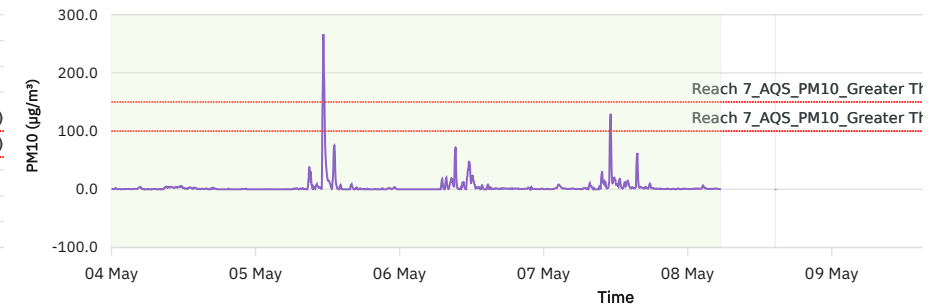

● 15 Min Rolling Avg PM10 Contribution


Stopped 
  Initial Avg 
  Rolling Avg

VOC Average Contribution (ppm)

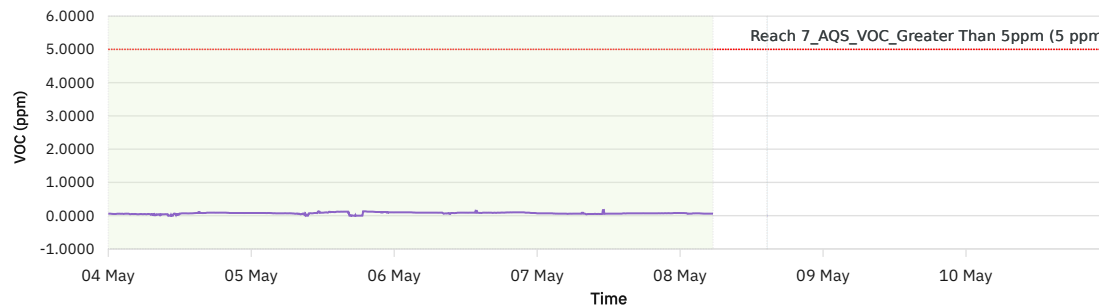


● 15 Min Rolling Avg VOC Contribution


Wind rose (mph)

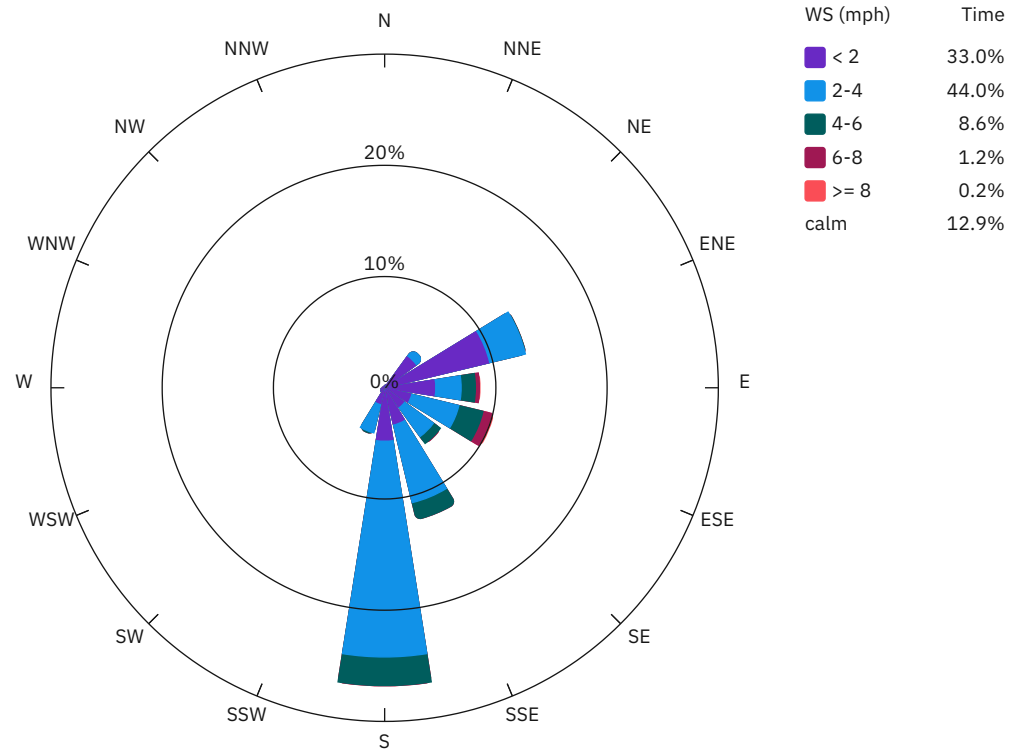


AM-01\_Reach 7\_3393\_WS

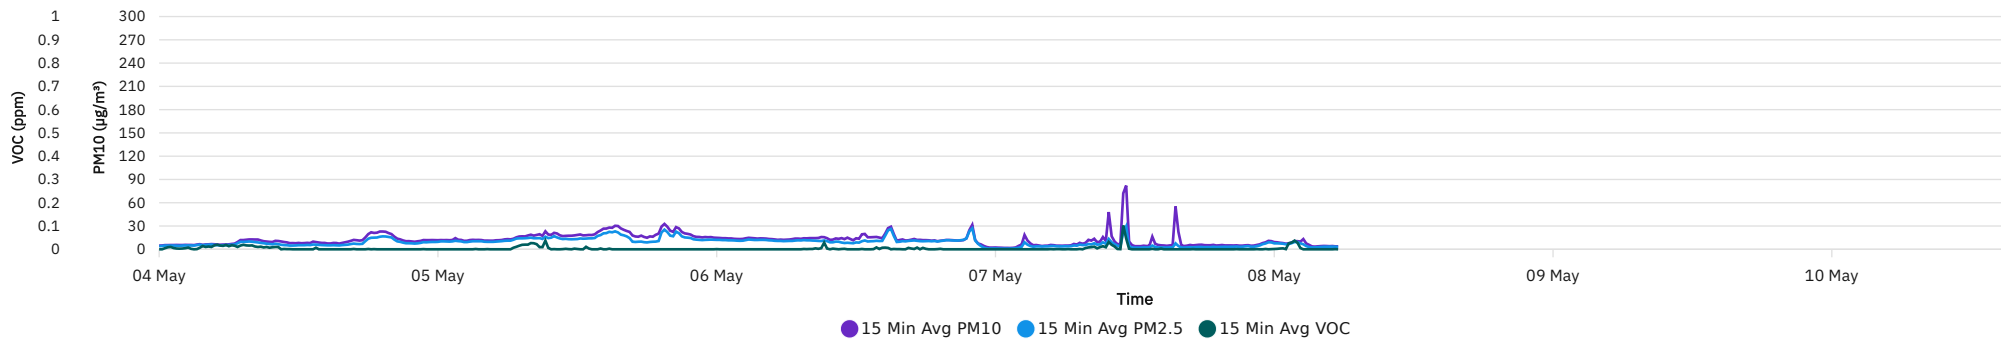


AM-02\_Reach 7\_3399

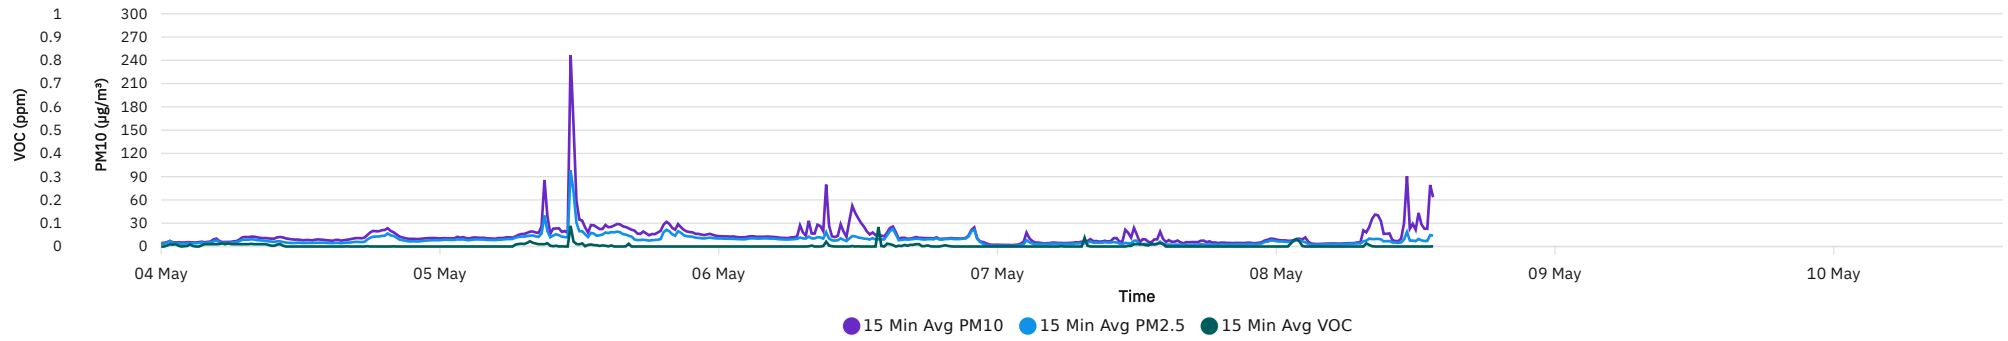


AM-03\_Reach 7\_3400

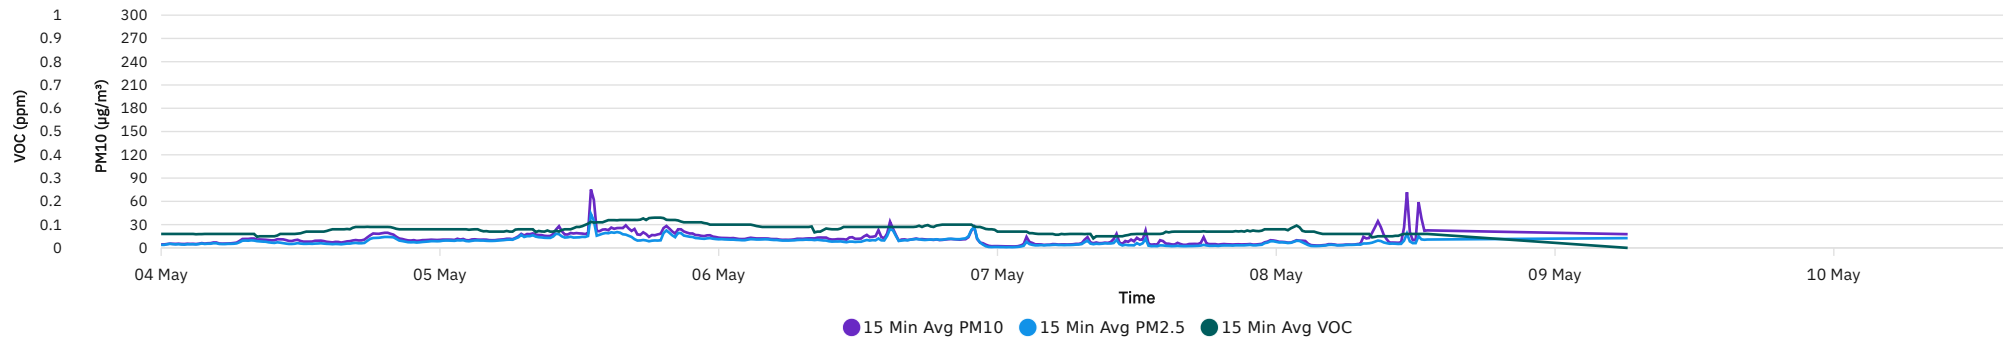


AM-04\_Reach 7\_3404

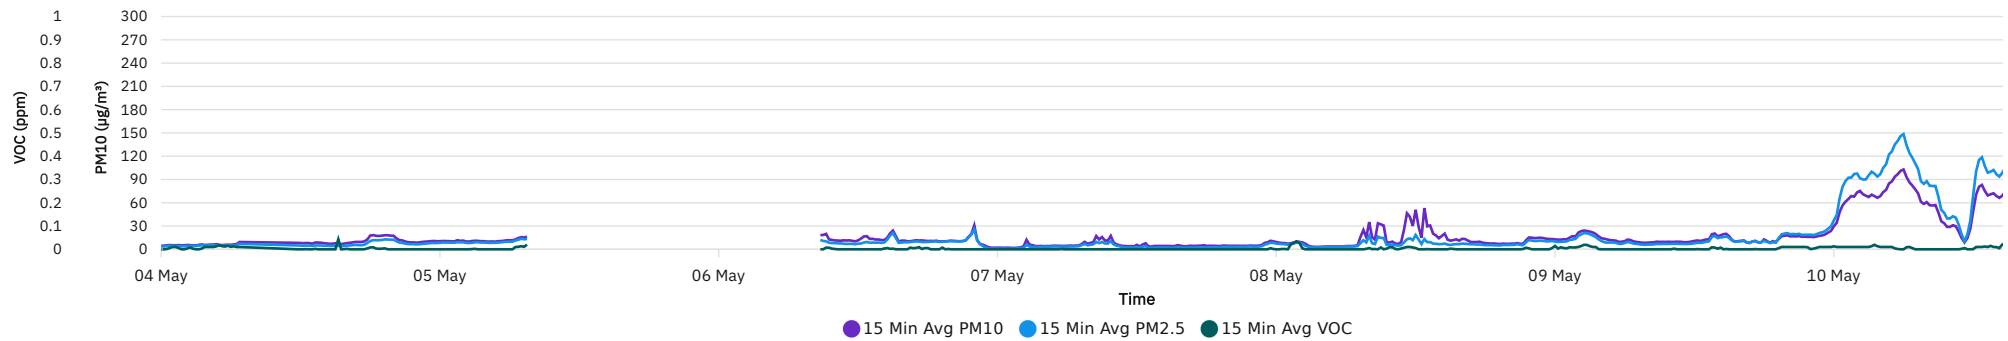

AM-05\_Reach 7\_3452

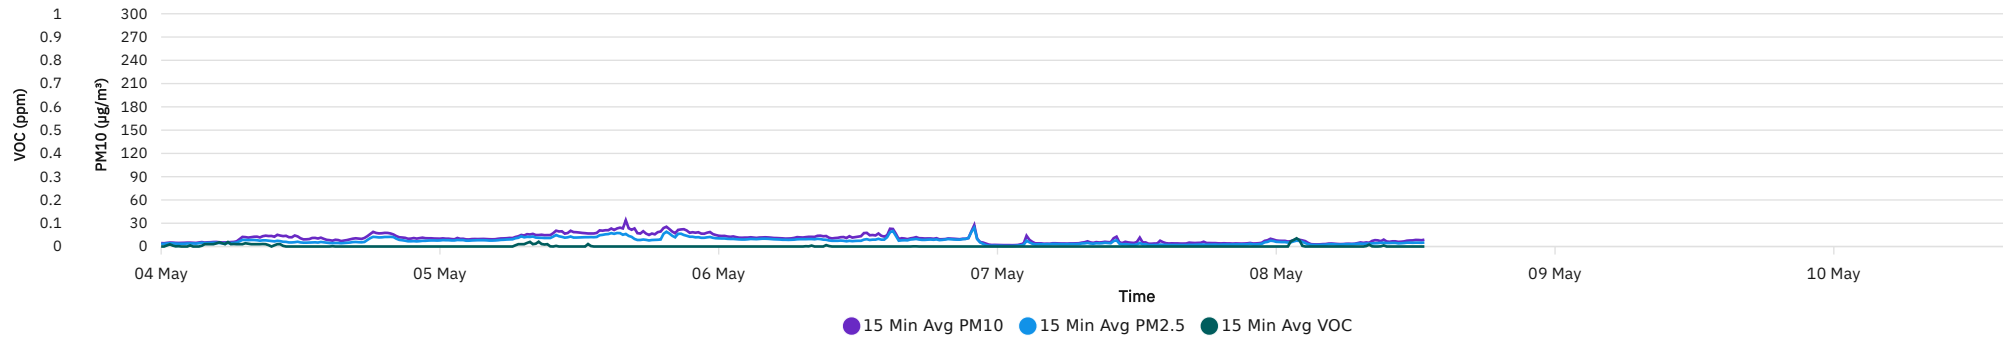

AM-06\_Reach 7\_3455\_WS

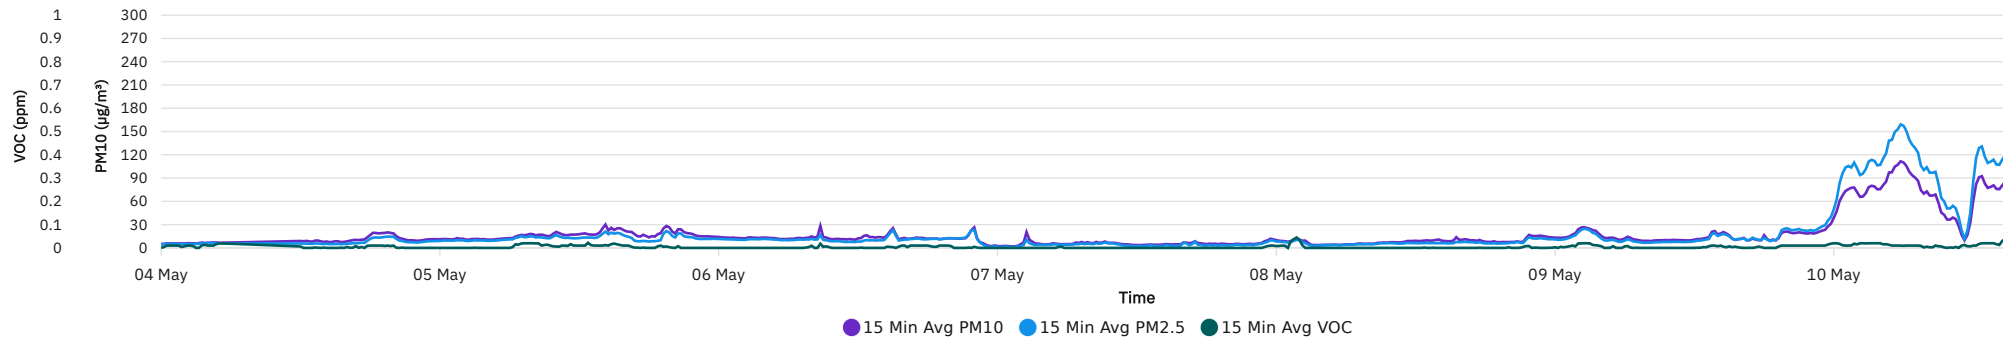

Exceedance Summary

Parameter	Action Level	Time Triggered	Cause	Mitigation
PM10	100.0 µg/m <sup>3</sup>	5/5/2026 11:07	Elevated readings were attributable to construction activities within the project area.	Contractor implemented dust control measures to mitigate fugitive dust.
PM10	100.0 µg/m <sup>3</sup>	5/7/2026 11:03	Elevated readings were attributable to construction activities within the project area.	Contractor implemented dust control measures to mitigate fugitive dust.
PM2.5	25.0 µg/m <sup>3</sup>	5/5/2026 11:08	Elevated readings were attributable to construction activities within the project area.	Contractor implemented dust control measures to mitigate fugitive dust.
PM2.5	25.0 µg/m <sup>3</sup>	5/7/2026 11:06	Elevated readings were attributable to construction activities within the project area.	Contractor implemented dust control measures to mitigate fugitive dust.

Reach 7_Stage_7ABC Report	Battery Park_AQS	
	Report Period	
	From:	05/11/2026 00:00
	To:	05/17/2026 23:59
	PM10 Action Level:	100 µg/m³
	PM2.5 Action Level:	25 µg/m³
VOC Action Level:	5 ppm	

Daily Environmental Summary	Temp (°F)	Relative Humidity (%)	Barometer (inHg)	Wind Speed (mph)	Prevailing Wind Direction
05/11/2026	52.7 - 63.1	25.1 - 73.1	30.0 - 30.2	0.3 - 4.4	SSE
05/12/2026	45.3 - 71.6	19.9 - 67.1	30.1 - 30.4	0.3 - 5.5	SE
05/13/2026	51.6 - 77.2	34.1 - 67.4	29.8 - 30.1	0.4 - 7.6	S
05/14/2026	52.7 - 72.9	36.7 - 80.5	29.7 - 29.9	0.2 - 4.3	SE
05/15/2026	50.2 - 72.9	36.6 - 67.2	29.8 - 30.1	0.3 - 6.6	E
05/16/2026	53.1 - 83.3	30.4 - 78.1	29.9 - 30.2	0.3 - 8.2	SE
05/17/2026	64.8 - 91.2	30.8 - 64.5	30.0 - 30.1	0.2 - 3.0	SE

Daily Monitoring Summary	PM2.5 (µg/m³)	Time	PM10 (µg/m³)	Time	VOC (ppm)	Time
Min Contribution (15 min avg.) - 5/11/2026	0.0	15:00	0.0	20:00	0.0357	14:15
Max Contribution (15 min avg.) - 5/11/2026	4.2	15:30	4.8	14:15	0.1027	18:30
Daily Avg. Contribution (15 min avg.) - 5/11/2026	0.4	-	1.3	-	0.0928	-
Min Contribution (15 min avg.) - 5/12/2026	0.0	00:15	0.0	00:15	0.0480	08:45
Max Contribution (15 min avg.) - 5/12/2026	62.1	09:45	294.3	13:15	0.0900	00:30
Daily Avg. Contribution (15 min avg.) - 5/12/2026	3.3	-	20.1	-	0.0743	-
Min Contribution (15 min avg.) - 5/13/2026	0.0	00:00	0.0	00:00	0.0047	07:45
Max Contribution (15 min avg.) - 5/13/2026	108.1	11:00	546.6	11:00	0.1100	17:00
Daily Avg. Contribution (15 min avg.) - 5/13/2026	7.7	-	42.1	-	0.0849	-
Min Contribution (15 min avg.) - 5/14/2026	0.0	00:00	0.0	00:00	0.0253	12:00
Max Contribution (15 min avg.) - 5/14/2026	5.0	12:45	20.7	13:45	0.2640	11:45
Daily Avg. Contribution (15 min avg.) - 5/14/2026	0.5	-	1.9	-	0.0899	-
Min Contribution (15 min avg.) - 5/15/2026	0.0	07:45	0.0	02:15	0.0573	10:30
Max Contribution (15 min avg.) - 5/15/2026	12.5	15:15	33.6	09:30	0.0980	21:30
Daily Avg. Contribution (15 min avg.) - 5/15/2026	0.6	-	1.8	-	0.0772	-
Min Contribution (15 min avg.) - 5/16/2026	0.0	01:00	0.0	01:00	0.0553	06:30
Max Contribution (15 min avg.) - 5/16/2026	2.0	06:15	4.4	19:45	0.1500	20:00
Daily Avg. Contribution (15 min avg.) - 5/16/2026	0.3	-	0.8	-	0.1078	-
Min Contribution (15 min avg.) - 5/17/2026	0.0	00:15	0.0	00:15	0.1340	06:00
Max Contribution (15 min avg.) - 5/17/2026	0.8	00:00	1.4	04:45	0.1473	01:00
Daily Avg. Contribution (15 min avg.) - 5/17/2026	0.3	-	0.5	-	0.1399	-

AM-06\_Reach 7\_3455\_WS



AM-05\_Reach 7\_3452 1404

AM-03\_Reach 7\_3400


AM-02\_Reach 7\_3399

AM-01\_Reach 7\_3393\_WS

200 ft

Stopped Initial Avg Rolling Avg


PM2.5 Average Contribution ( $\mu\text{g}/\text{m}^3$ )

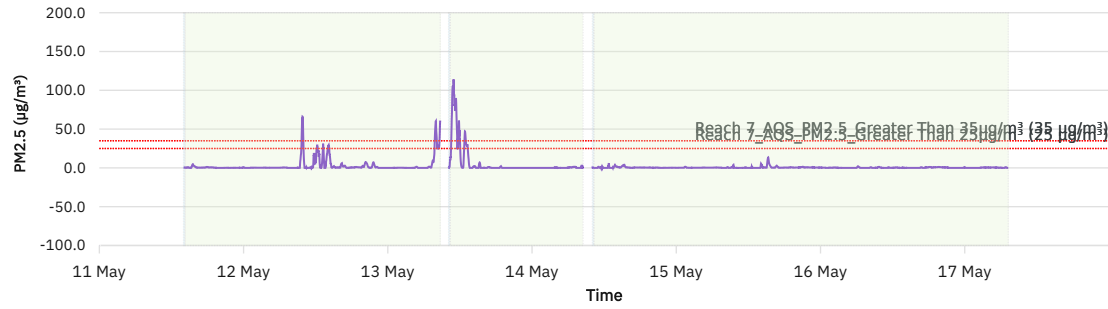

15 Min Rolling Avg PM2.5 Contribution

Stopped Initial Avg Rolling Avg


PM10 Average Contribution ( $\mu\text{g}/\text{m}^3$ )

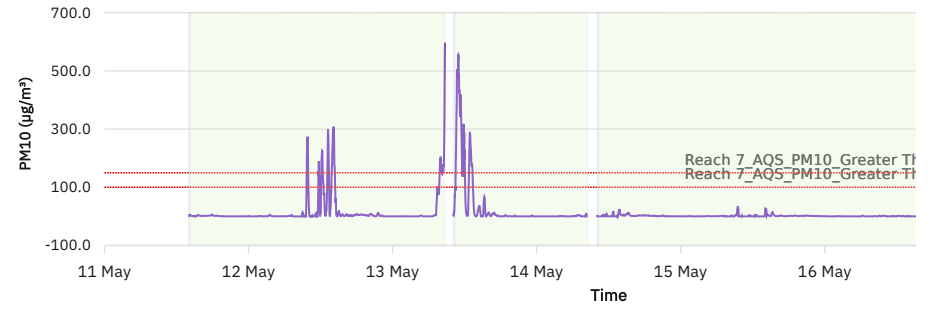

15 Min Rolling Avg PM10 Contribution


Stopped Initial Avg Rolling Avg

VOC Average Contribution (ppm)

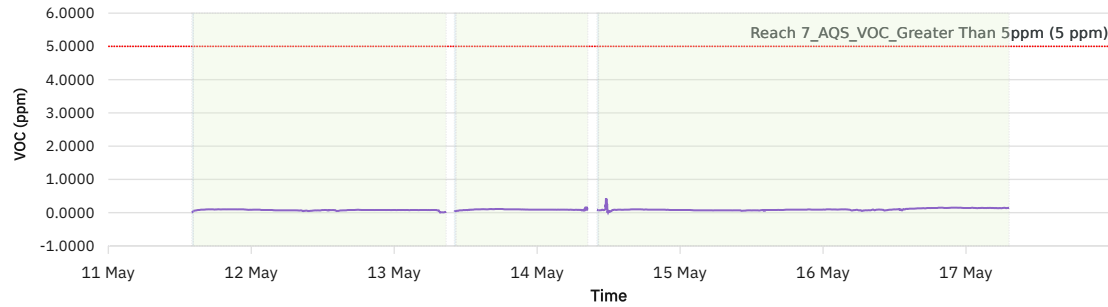


15 Min Rolling Avg VOC Contribution


Wind rose (mph)

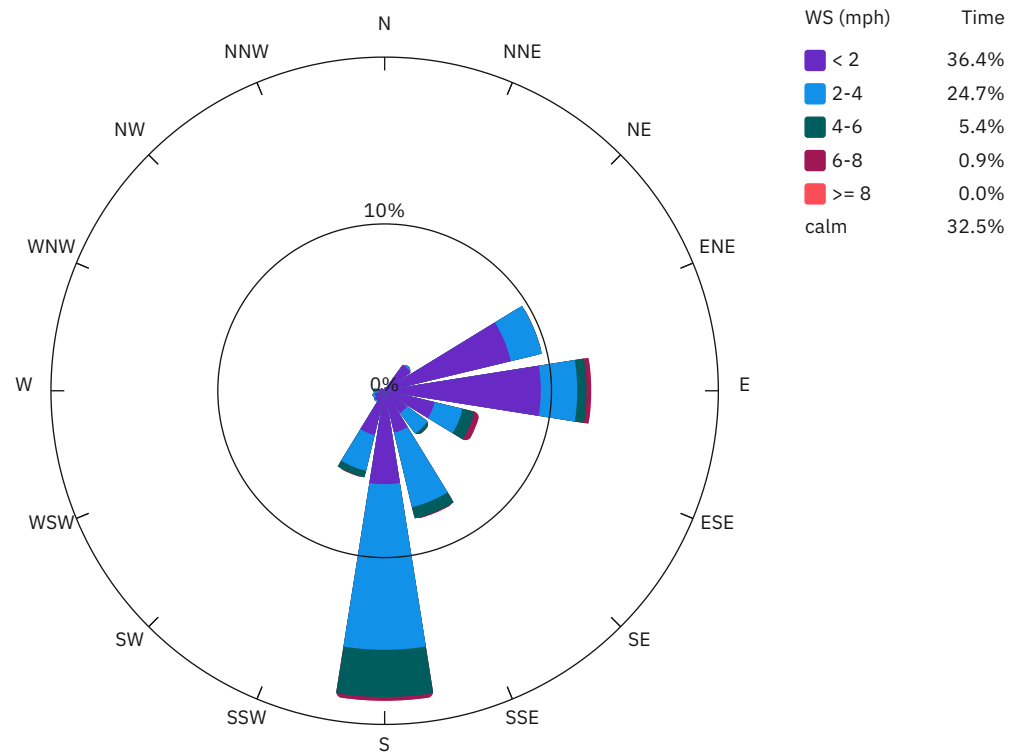


AM-01\_Reach 7\_3393\_WS

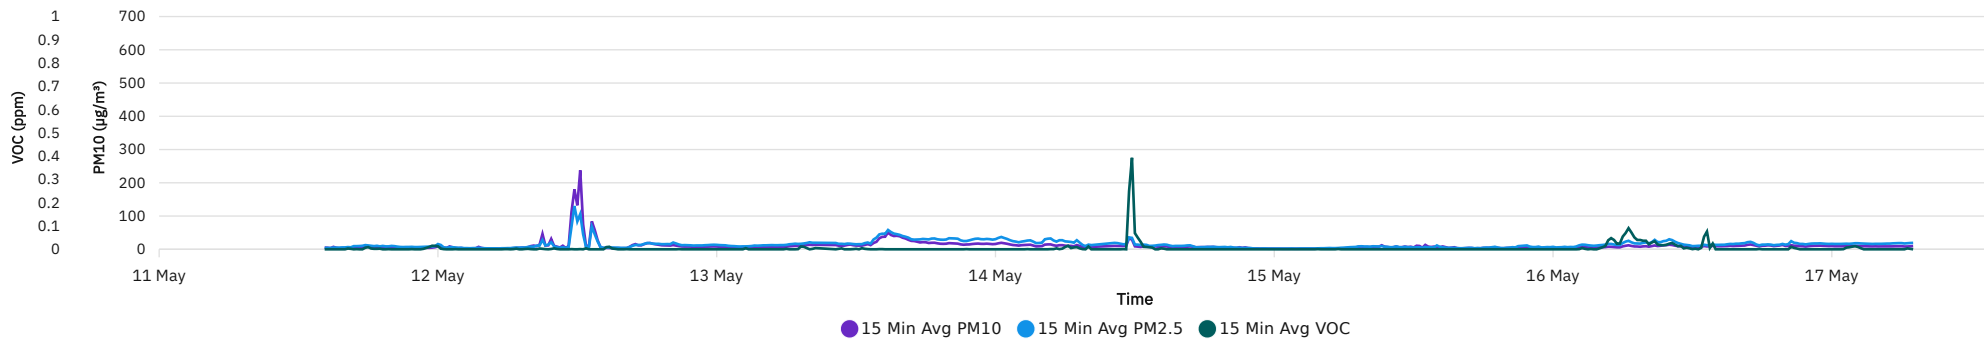


AM-02\_Reach 7\_3399

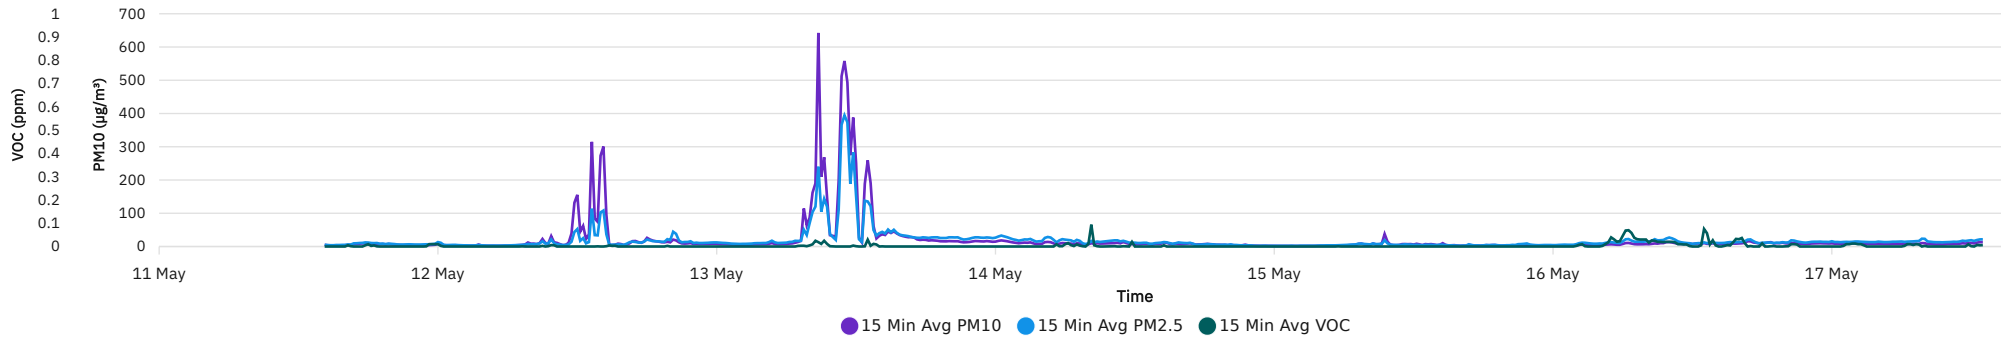


AM-03\_Reach 7\_3400

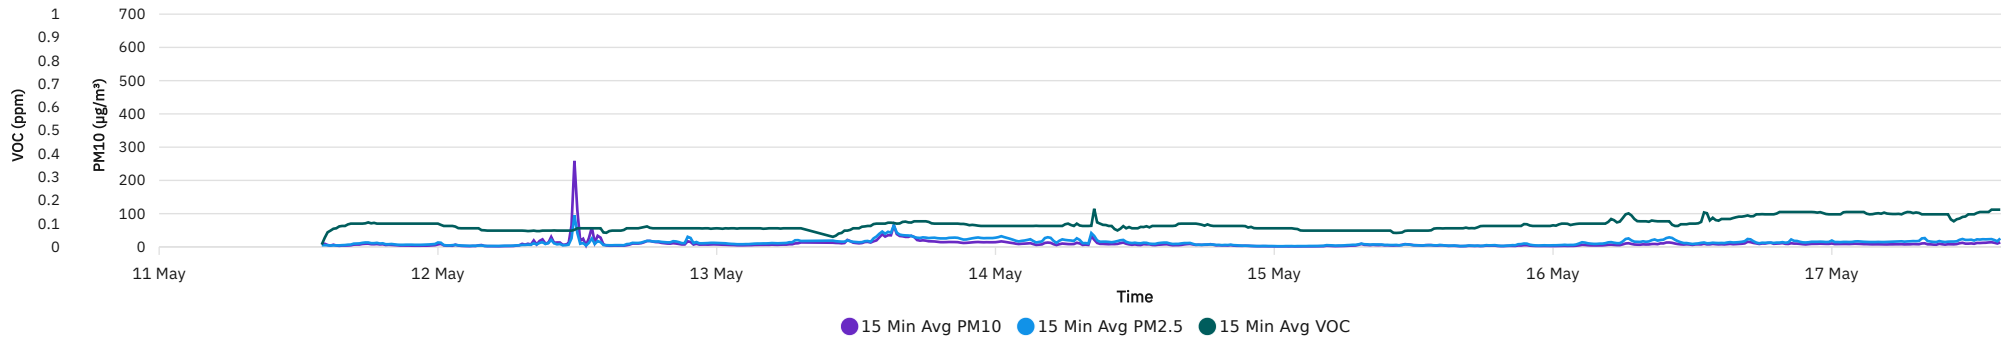


AM-04\_Reach 7\_3404

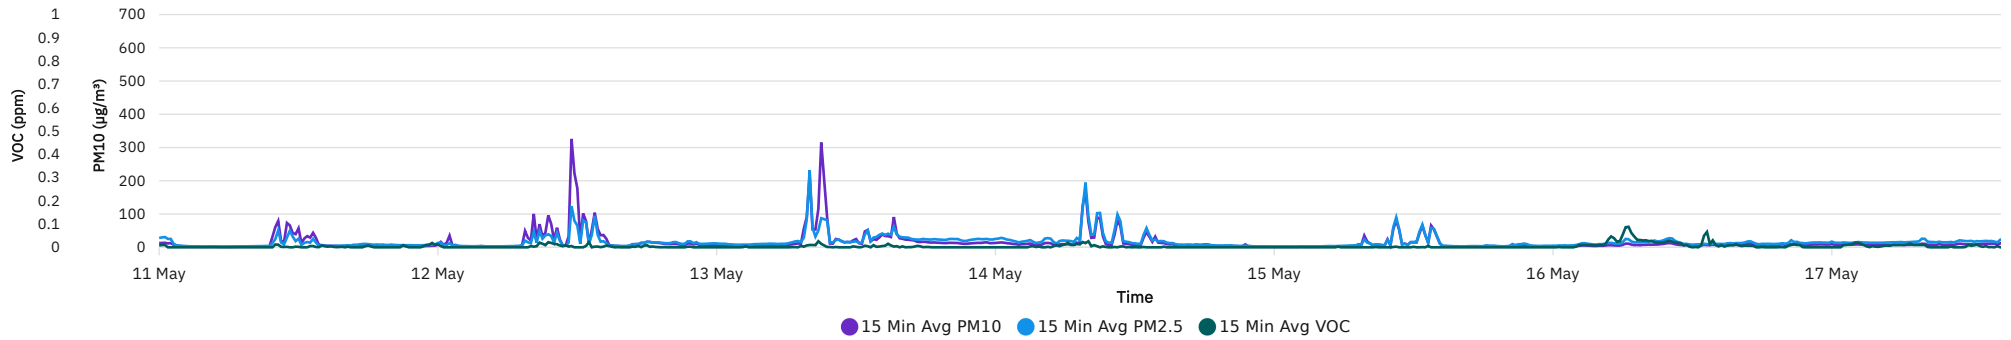

AM-05\_Reach 7\_3452

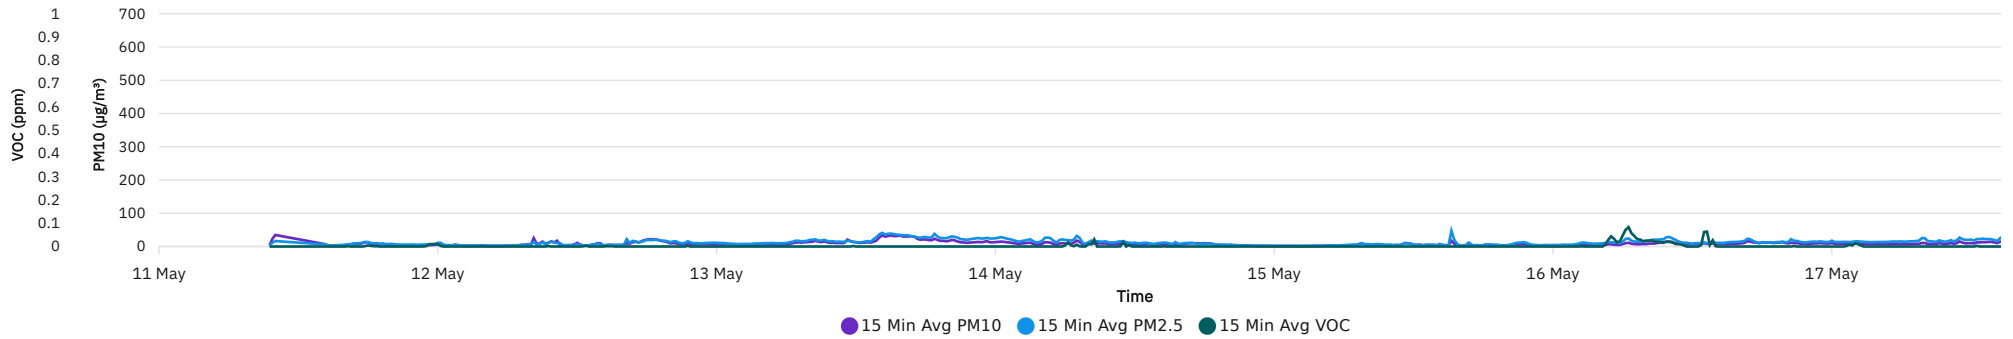

AM-06\_Reach 7\_3455\_WS

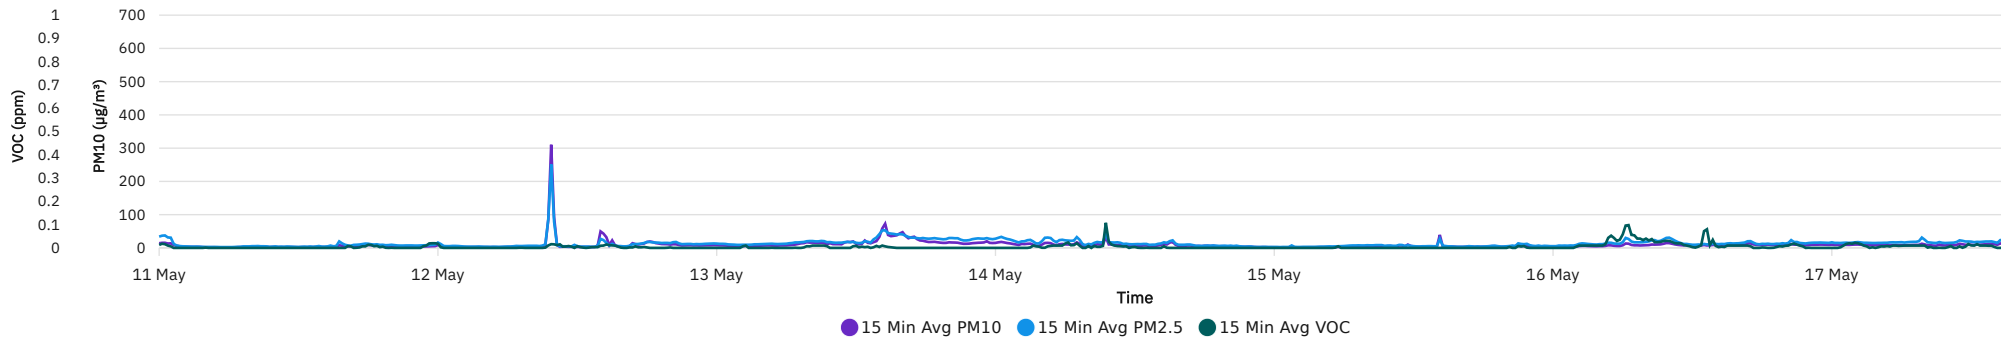

Exceedance Summary

Parameter	Action Level	Time Triggered	Cause	Mitigation
PM10	150.0 µg/m³	5/12/2026 09:40	Elevated readings were attributable to construction activities within the project area.	Contractor implemented dust control measures to mitigate fugitive dust.
PM10	150.0 µg/m³	5/12/2026 11:38	Elevated readings were attributable to construction activities within the project area.	Contractor implemented dust control measures to mitigate fugitive dust.
PM10	150.0 µg/m³	5/12/2026 12:05	Elevated readings were attributable to construction activities within the project area.	Contractor implemented dust control measures to mitigate fugitive dust.
PM10	150.0 µg/m³	5/12/2026 13:06	Elevated readings were attributable to construction activities within the project area.	Contractor implemented dust control measures to mitigate fugitive dust.
PM10	150.0 µg/m³	5/12/2026 13:48	Elevated readings were attributable to construction activities within the project area.	Contractor implemented dust control measures to mitigate fugitive dust.
PM10	100.0 µg/m³	5/13/2026 07:29	Elevated readings were attributable to construction activities within the project area.	Contractor implemented dust control measures to mitigate fugitive dust.
PM10	150.0 µg/m³	5/13/2026 07:47	Elevated readings were attributable to construction activities within the project area.	Contractor implemented dust control measures to mitigate fugitive dust.
PM10	150.0 µg/m³	5/13/2026 10:27	Elevated readings were attributable to construction activities within the project area.	Contractor implemented dust control measures to mitigate fugitive dust.
PM10	150.0 µg/m³	5/13/2026 10:29	Elevated readings were attributable to construction activities within the project area.	Contractor implemented dust control measures to mitigate fugitive dust.
PM10	150.0 µg/m³	5/13/2026 12:41	Elevated readings were attributable to construction activities within the project area.	Contractor implemented dust control measures to mitigate fugitive dust.
PM2.5	35.0 µg/m³	5/12/2026 09:37	Elevated readings were attributable to construction activities within the project area.	Contractor implemented dust control measures to mitigate fugitive dust.
PM2.5	25.0 µg/m³	5/12/2026 12:09	Elevated readings were attributable to construction activities within the project area.	Contractor implemented dust control measures to mitigate fugitive dust.

PM2.5	25.0 µg/m³	5/12/2026 13:12	Elevated readings were attributable to construction activities within the project area.	Contractor implemented dust control measures to mitigate fugitive dust.
PM2.5	25.0 µg/m³	5/12/2026 14:02	Elevated readings were attributable to construction activities within the project area.	Contractor implemented dust control measures to mitigate fugitive dust.
PM2.5	35.0 µg/m³	5/13/2026 07:47	Elevated readings were attributable to construction activities within the project area.	Contractor implemented dust control measures to mitigate fugitive dust.
PM2.5	35.0 µg/m³	5/13/2026 08:17	Elevated readings were attributable to construction activities within the project area.	Contractor implemented dust control measures to mitigate fugitive dust.
PM2.5	35.0 µg/m³	5/13/2026 08:27	Elevated readings were attributable to construction activities within the project area.	Contractor implemented dust control measures to mitigate fugitive dust.
PM2.5	35.0 µg/m³	5/13/2026 10:32	Elevated readings were attributable to construction activities within the project area.	Contractor implemented dust control measures to mitigate fugitive dust.
PM2.5	35.0 µg/m³	5/13/2026 11:37	Elevated readings were attributable to construction activities within the project area.	Contractor implemented dust control measures to mitigate fugitive dust.
PM2.5	35.0 µg/m³	5/13/2026 12:43	Elevated readings were attributable to construction activities within the project area.	Contractor implemented dust control measures to mitigate fugitive dust.



Reach 7\_Stage\_7ABC Report


Battery Park\_AQS


Report Period

From:	05/18/2026 00:00
To:	05/24/2026 23:59
PM10 Action Level:	100 µg/m³
PM2.5 Action Level:	25 µg/m³
VOC Action Level:	5 ppm

Daily Environmental Summary	Temp (°F)	Relative Humidity (%)	Barometer (inHg)	Wind Speed (mph)	Prevailing Wind Direction
05/18/2026	66.0 - 91.4	35.7 - 73.8	30.1 - 30.2	0.2 - 6.0	S
05/19/2026	71.8 - 95.7	31.3 - 71.7	30.0 - 30.3	0.3 - 6.2	SSE
05/20/2026	61.5 - 100.8	30.1 - 96.0	29.9 - 30.4	0.3 - 4.9	ESE
05/21/2026	55.2 - 64.9	46.2 - 88.4	30.1 - 30.6	0.2 - 3.7	ENE
05/22/2026	56.5 - 75.7	28.9 - 60.8	30.3 - 30.6	0.2 - 5.3	SSE
05/23/2026	48.2 - 58.6	42.0 - 88.8	30.4 - 30.7	0.3 - 3.5	SE
05/24/2026	48.9 - 55.9	85.3 - 90.3	30.2 - 30.7	0.2 - 3.0	SE


Daily Monitoring Summary	PM2.5 (µg/m³)	Time	PM10 (µg/m³)	Time	VOC (ppm)	Time
Min Contribution (15 min avg.) - 5/18/2026	0.0	12:30	0.0	14:45	0.0907	08:45
Max Contribution (15 min avg.) - 5/18/2026	53.7	08:15	312.9	08:15	0.2300	19:15
Daily Avg. Contribution (15 min avg.) - 5/18/2026	6.6	-	22.3	-	0.1868	-
Min Contribution (15 min avg.) - 5/19/2026	0.1	18:00	0.0	16:00	0.1473	11:00
Max Contribution (15 min avg.) - 5/19/2026	63.2	07:45	205.4	07:45	0.2853	22:15
Daily Avg. Contribution (15 min avg.) - 5/19/2026	4.4	-	15.9	-	0.2298	-
Min Contribution (15 min avg.) - 5/20/2026	0.0	01:15	0.0	01:15	0.1560	09:30
Max Contribution (15 min avg.) - 5/20/2026	31.1	07:45	466.2	19:15	0.3000	18:00
Daily Avg. Contribution (15 min avg.) - 5/20/2026	2.9	-	25.1	-	0.2517	-
Min Contribution (15 min avg.) - 5/21/2026	0.0	06:30	0.0	01:45	0.0407	11:30
Max Contribution (15 min avg.) - 5/21/2026	9.3	16:30	15.3	16:00	0.2473	09:30
Daily Avg. Contribution (15 min avg.) - 5/21/2026	1.0	-	2.6	-	0.1536	-
Min Contribution (15 min avg.) - 5/22/2026	0.0	09:00	0.0	07:30	0.0000	21:15
Max Contribution (15 min avg.) - 5/22/2026	8.2	08:30	25.9	08:30	0.1407	03:30
Daily Avg. Contribution (15 min avg.) - 5/22/2026	0.4	-	1.3	-	0.1162	-
Min Contribution (15 min avg.) - 5/23/2026	0.0	00:45	0.0	00:00	0.0000	04:15
Max Contribution (15 min avg.) - 5/23/2026	1.7	21:00	3.2	17:45	0.1300	01:30
Daily Avg. Contribution (15 min avg.) - 5/23/2026	0.2	-	0.5	-	0.0435	-
Min Contribution (15 min avg.) - 5/24/2026	0.0	01:00	0.0	03:15	0.0000	00:00
Max Contribution (15 min avg.) - 5/24/2026	3.1	20:30	4.0	20:30	0.1000	05:00
Daily Avg. Contribution (15 min avg.) - 5/24/2026	0.3	-	0.5	-	0.0433	-



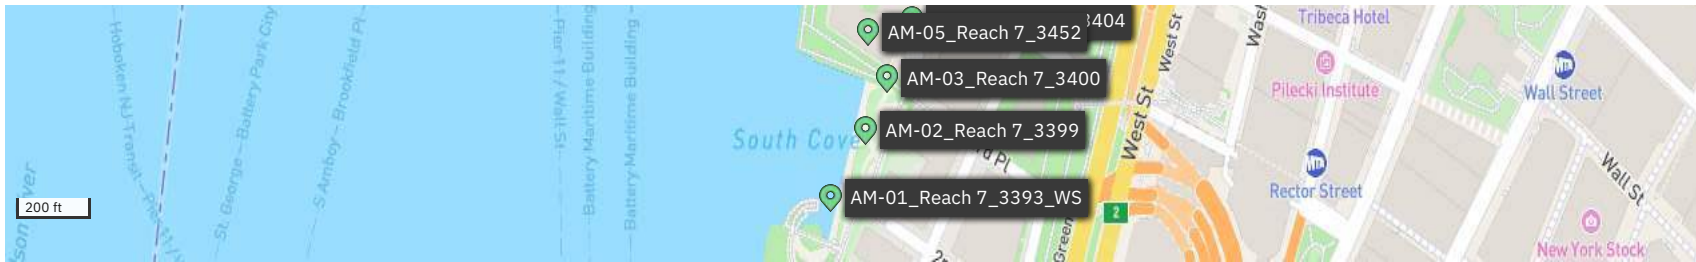

Stopped 
  Initial Avg 
  Rolling Avg


PM2.5 Average Contribution ( $\mu\text{g}/\text{m}^3$ )

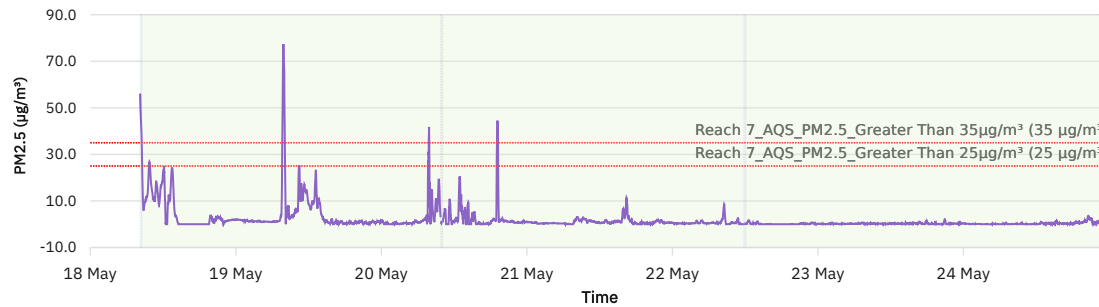

● 15 Min Rolling Avg PM2.5 Contribution

Stopped 
  Initial Avg 
  Rolling Avg


PM10 Average Contribution ( $\mu\text{g}/\text{m}^3$ )

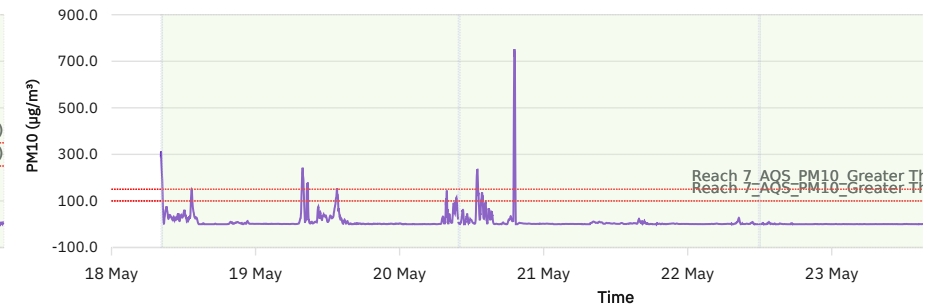

● 15 Min Rolling Avg PM10 Contribution


Stopped 
  Initial Avg 
  Rolling Avg

VOC Average Contribution (ppm)

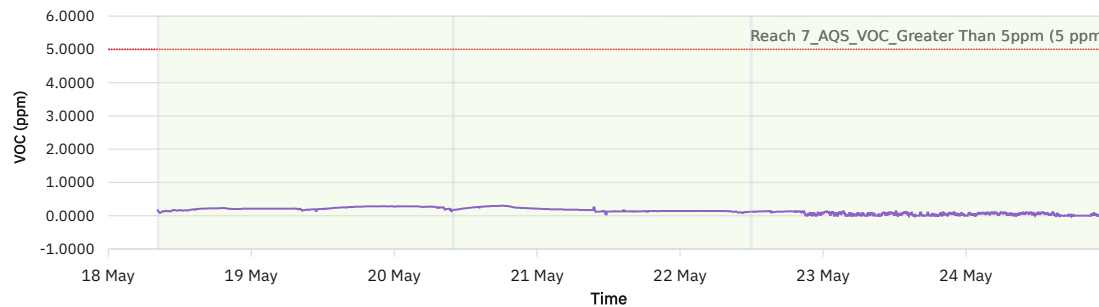


● 15 Min Rolling Avg VOC Contribution


Wind rose (mph)

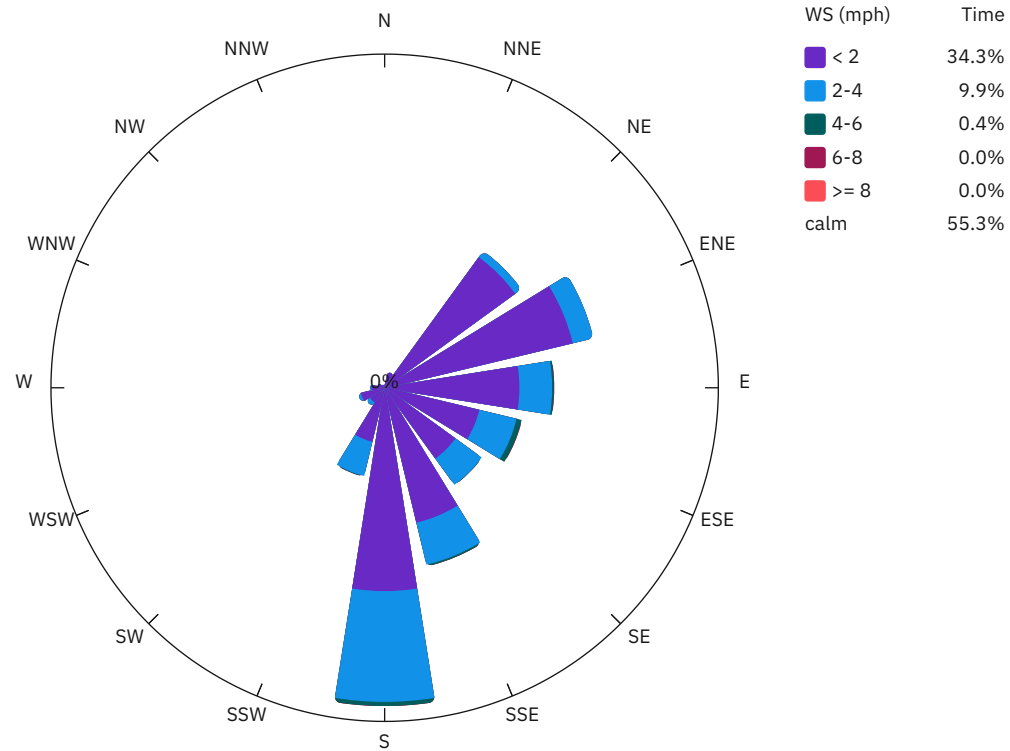


AM-01\_Reach 7\_3393\_WS

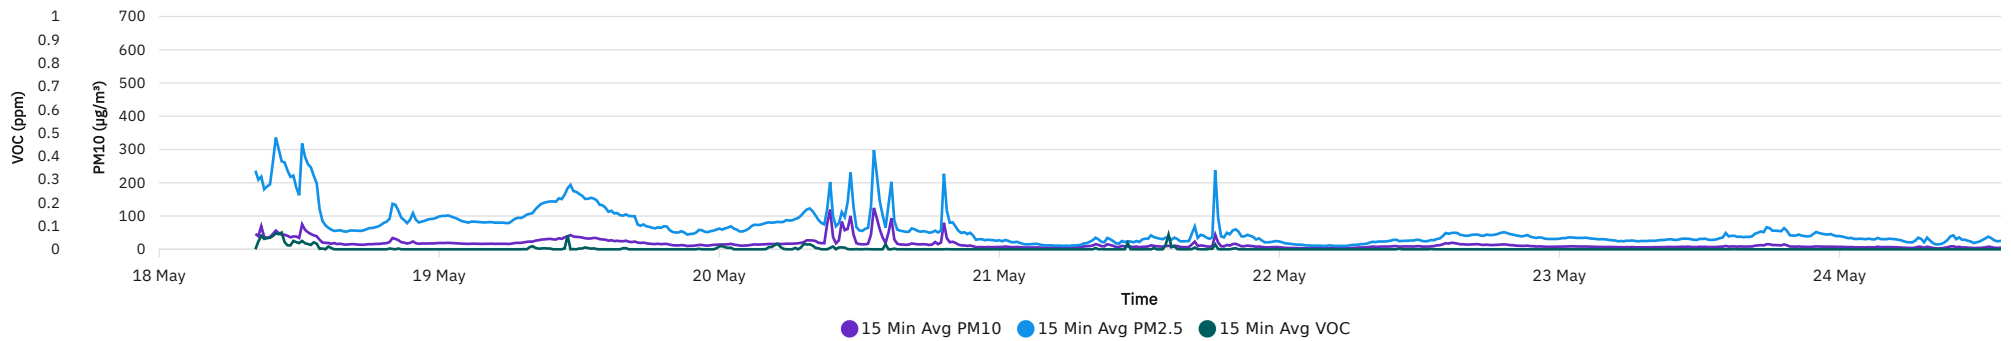


AM-02\_Reach 7\_3399

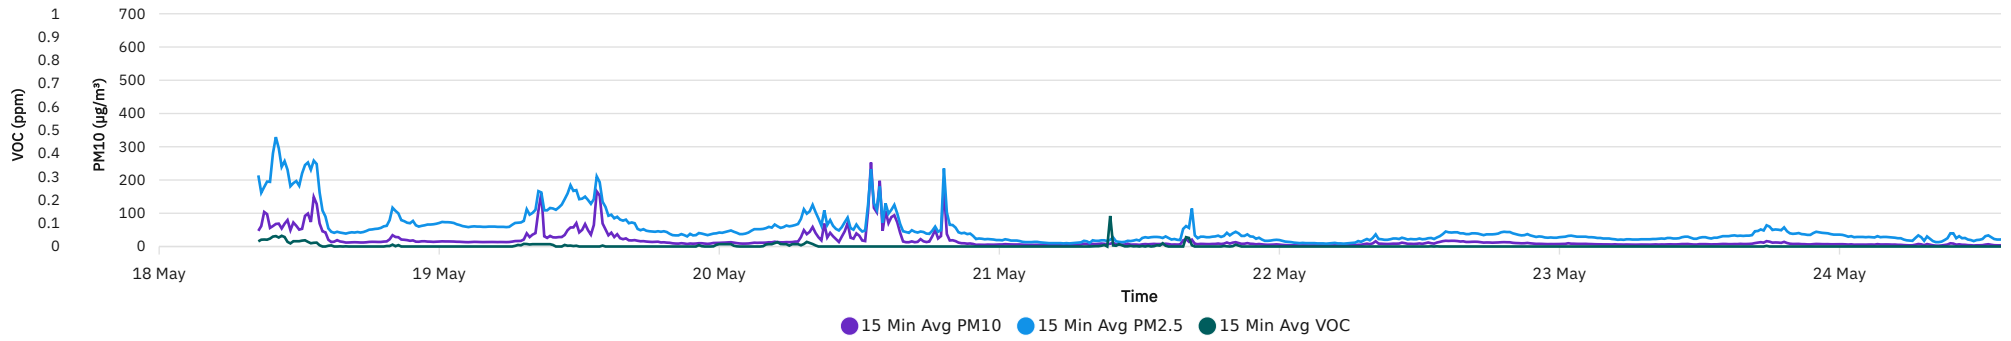


AM-03\_Reach 7\_3400

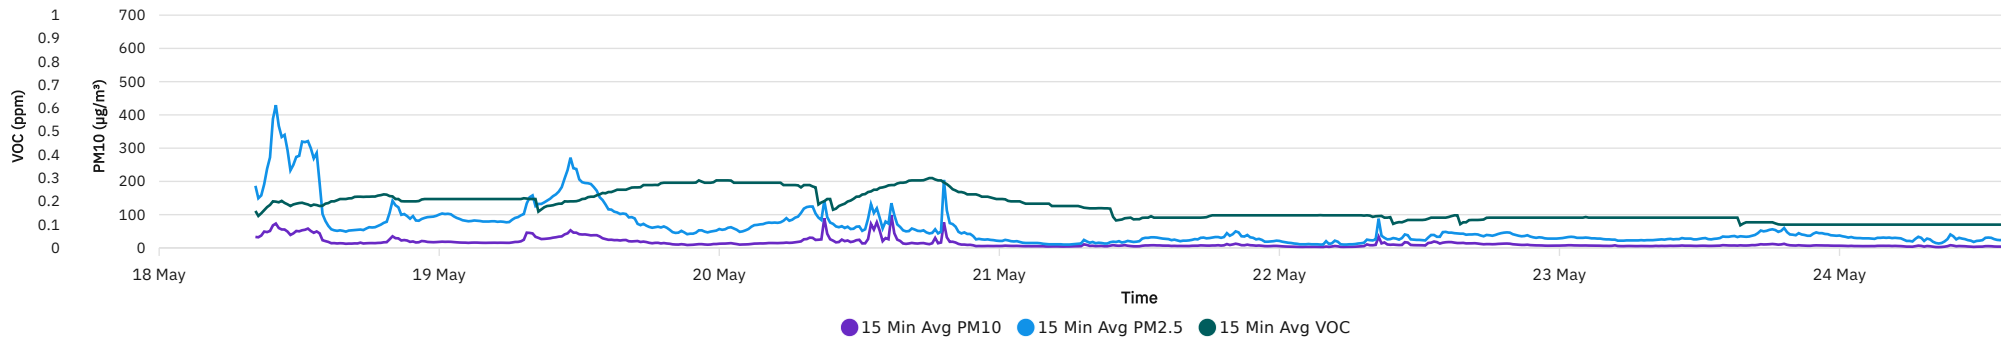


AM-04\_Reach 7\_3404

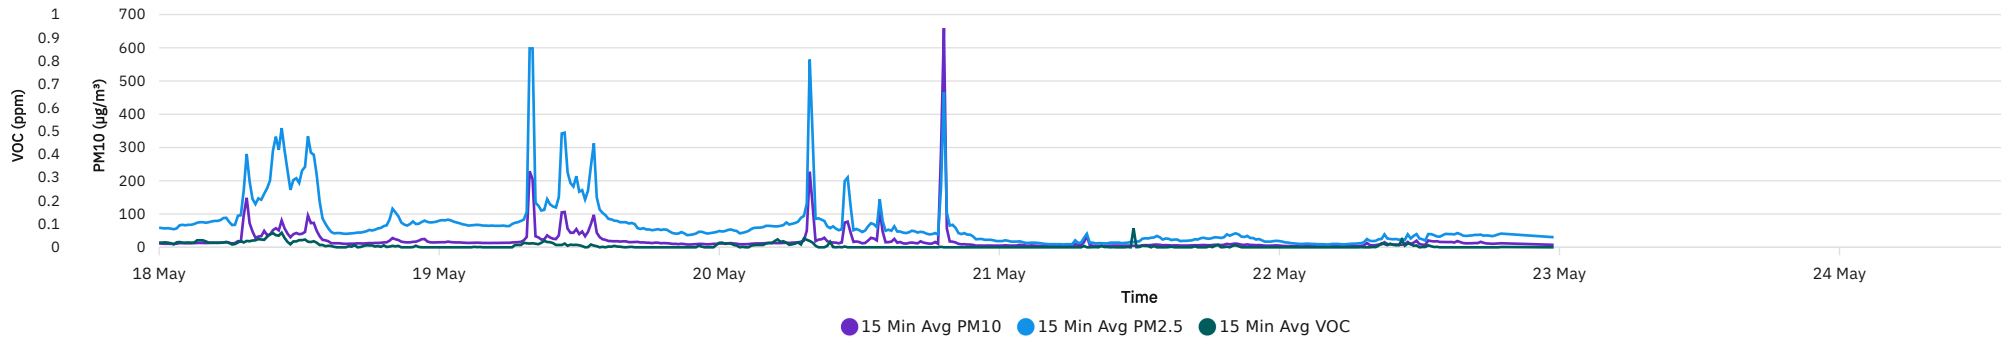

AM-05\_Reach 7\_3452

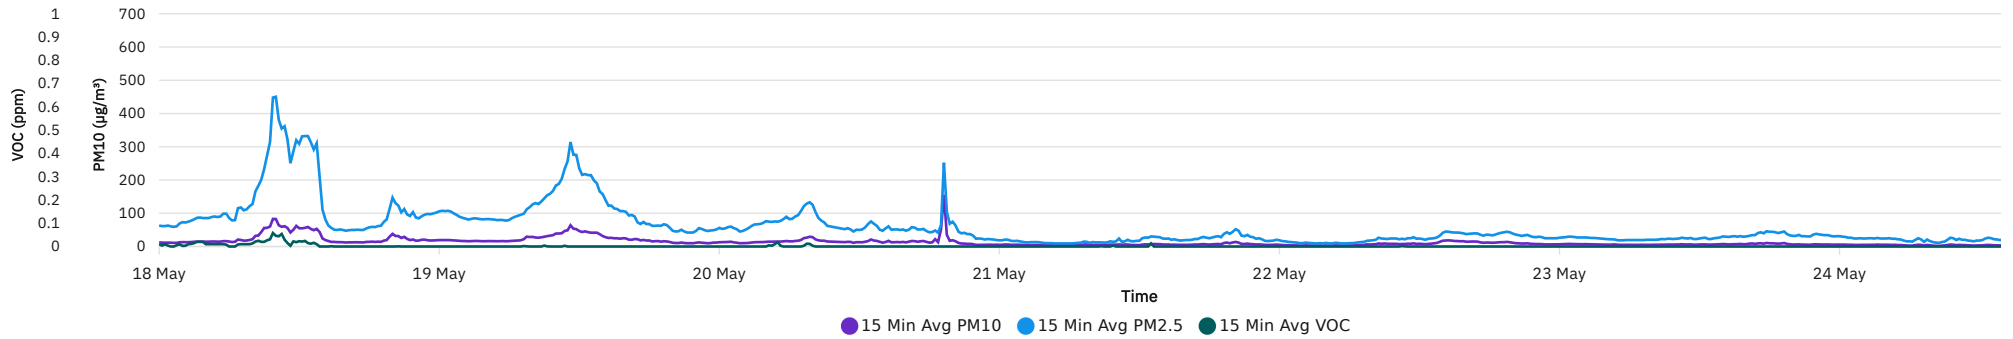

AM-06\_Reach 7\_3455\_WS

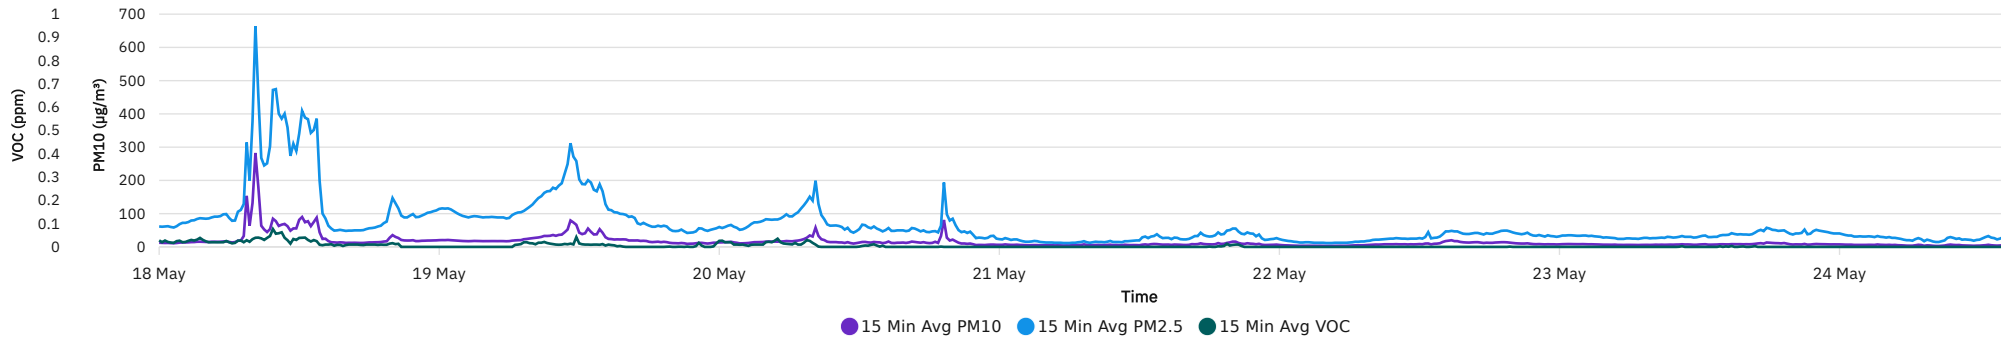

Exceedance Summary

Parameter	Action Level	Time Triggered	Cause	Mitigation
PM10	100.0 µg/m³	5/18/2026 13:14	Elevated readings were attributable to construction activities within the project area.	Contractor implemented dust control measures to mitigate fugitive dust.
PM10	150.0 µg/m³	5/19/2026 07:38	Elevated readings were attributable to construction activities within the project area.	Contractor implemented dust control measures to mitigate fugitive dust.
PM10	150.0 µg/m³	5/19/2026 08:31	Elevated readings were attributable to construction activities within the project area.	Contractor implemented dust control measures to mitigate fugitive dust.
PM10	150.0 µg/m³	5/19/2026 13:21	Elevated readings were attributable to construction activities within the project area.	Contractor implemented dust control measures to mitigate fugitive dust.
PM10	100.0 µg/m³	5/20/2026 07:42	Elevated readings were attributable to construction activities within the project area.	Contractor implemented dust control measures to mitigate fugitive dust.
PM10	100.0 µg/m³	5/20/2026 07:45	Elevated readings were attributable to construction activities within the project area.	Contractor implemented dust control measures to mitigate fugitive dust.
PM10	100.0 µg/m³	5/20/2026 09:25	Elevated readings were attributable to construction activities within the project area.	Contractor implemented dust control measures to mitigate fugitive dust.
PM10	150.0 µg/m³	5/20/2026 12:46	Elevated readings were attributable to construction activities within the project area.	Contractor implemented dust control measures to mitigate fugitive dust.
PM10	100.0 µg/m³	5/20/2026 13:34	Elevated readings were attributable to construction activities within the project area.	Contractor implemented dust control measures to mitigate fugitive dust.
PM10	100.0 µg/m³	5/20/2026 13:37	Elevated readings were attributable to construction activities within the project area.	Contractor implemented dust control measures to mitigate fugitive dust.
PM10	150.0 µg/m³	5/20/2026 18:59	Elevated readings were attributable to construction activities within the project area.	Contractor implemented dust control measures to mitigate fugitive dust.
PM2.5	25.0 µg/m³	5/18/2026 09:40	Elevated readings were attributable to construction activities within the project area.	Contractor implemented dust control measures to mitigate fugitive dust.

PM2.5	35.0 µg/m <sup>3</sup>	5/19/2026 07:38	Elevated readings were attributable to construction activities within the project area.	Contractor implemented dust control measures to mitigate fugitive dust.
PM2.5	25.0 µg/m <sup>3</sup>	5/19/2026 10:25	Elevated readings were attributable to construction activities within the project area.	Contractor implemented dust control measures to mitigate fugitive dust.
PM2.5	25.0 µg/m <sup>3</sup>	5/19/2026 10:27	Elevated readings were attributable to construction activities within the project area.	Contractor implemented dust control measures to mitigate fugitive dust.
PM2.5	35.0 µg/m <sup>3</sup>	5/20/2026 07:42	Elevated readings were attributable to construction activities within the project area.	Contractor implemented dust control measures to mitigate fugitive dust.
PM2.5	35.0 µg/m <sup>3</sup>	5/20/2026 07:44	Elevated readings were attributable to construction activities within the project area.	Contractor implemented dust control measures to mitigate fugitive dust.
PM2.5	35.0 µg/m <sup>3</sup>	5/20/2026 19:02	Elevated readings were attributable to construction activities within the project area.	Contractor implemented dust control measures to mitigate fugitive dust.



Reach 7\_Stage\_7ABC Report


Battery Park\_AQS


Report Period

From:	05/25/2026 00:00
To:	05/31/2026 23:59
PM10 Action Level:	100 µg/m³
PM2.5 Action Level:	25 µg/m³
VOC Action Level:	5 ppm

Daily Environmental Summary	Temp (°F)	Relative Humidity (%)	Barometer (inHg)	Wind Speed (mph)	Prevailing Wind Direction
05/25/2026	54.0 - 71.2	70.6 - 91.6	30.1 - 30.2	0.3 - 1.1	SE
05/26/2026	66.0 - 84.7	31.6 - 69.6	30.0 - 30.2	0.3 - 3.5	S
05/27/2026	66.0 - 81.5	43.5 - 71.0	29.8 - 30.0	0.1 - 5.0	SE
05/28/2026	61.2 - 81.9	33.1 - 58.1	29.8 - 30.1	0.3 - 4.4	NE
05/29/2026	56.7 - 82.6	25.0 - 62.9	29.7 - 30.2	0.3 - 6.0	E
05/30/2026	52.7 - 68.7	35.7 - 58.9	29.7 - 30.1	0.3 - 6.5	ENE
05/31/2026	50.0 - 80.8	25.1 - 71.8	29.9 - 30.2	0.2 - 3.3	ESE


Daily Monitoring Summary	PM2.5 (µg/m³)	Time	PM10 (µg/m³)	Time	VOC (ppm)	Time
Min Contribution (15 min avg.) - 5/25/2026	0.0	00:15	0.0	00:15	0.0000	01:00
Max Contribution (15 min avg.) - 5/25/2026	2.7	02:45	1.9	02:45	0.1093	03:45
Daily Avg. Contribution (15 min avg.) - 5/25/2026	0.9	-	0.8	-	0.0482	-
Min Contribution (15 min avg.) - 5/26/2026	0.0	10:45	0.0	10:45	0.0957	10:45
Max Contribution (15 min avg.) - 5/26/2026	2.5	18:15	11.0	15:00	0.1900	18:45
Daily Avg. Contribution (15 min avg.) - 5/26/2026	0.6	-	2.0	-	0.1690	-
Min Contribution (15 min avg.) - 5/27/2026	0.0	01:30	0.0	03:00	0.1507	10:45
Max Contribution (15 min avg.) - 5/27/2026	60.5	09:00	190.5	09:00	0.2300	20:00
Daily Avg. Contribution (15 min avg.) - 5/27/2026	3.4	-	9.7	-	0.1892	-
Min Contribution (15 min avg.) - 5/28/2026	0.1	17:45	0.0	14:00	0.1507	11:30
Max Contribution (15 min avg.) - 5/28/2026	9.2	15:00	36.9	15:00	0.2200	00:00
Daily Avg. Contribution (15 min avg.) - 5/28/2026	1.2	-	4.8	-	0.1905	-
Min Contribution (15 min avg.) - 5/29/2026	0.0	07:30	0.0	07:30	0.0533	11:45
Max Contribution (15 min avg.) - 5/29/2026	5.8	08:45	41.9	13:30	0.2093	21:30
Daily Avg. Contribution (15 min avg.) - 5/29/2026	0.5	-	3.2	-	0.1706	-
Min Contribution (15 min avg.) - 5/30/2026	0.0	09:30	0.0	19:15	0.0960	10:00
Max Contribution (15 min avg.) - 5/30/2026	22.4	15:15	37.3	04:30	0.2000	01:15
Daily Avg. Contribution (15 min avg.) - 5/30/2026	1.0	-	3.9	-	0.1422	-
Min Contribution (15 min avg.) - 5/31/2026	0.0	05:45	0.0	03:45	0.1043	10:00
Max Contribution (15 min avg.) - 5/31/2026	11.3	13:45	13.2	13:45	0.1880	23:15
Daily Avg. Contribution (15 min avg.) - 5/31/2026	0.8	-	1.4	-	0.1480	-



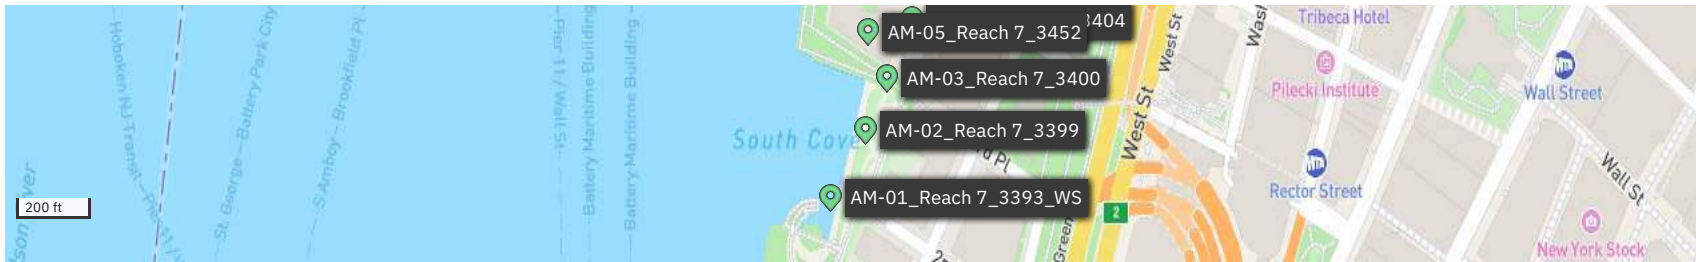

Stopped Initial Avg Rolling Avg


PM2.5 Average Contribution ( $\mu\text{g}/\text{m}^3$ )

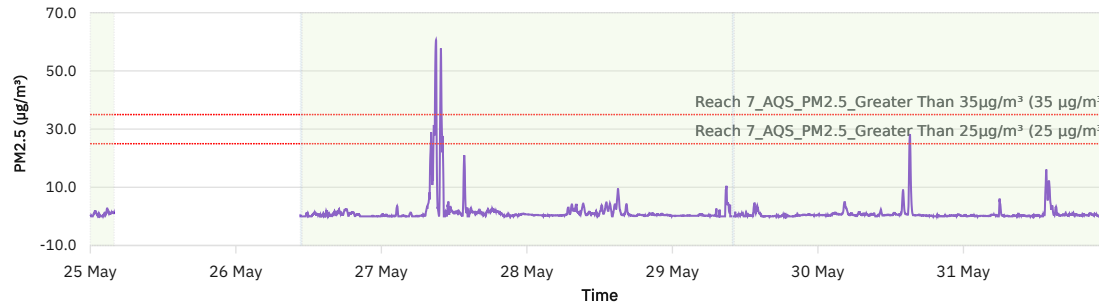

● 15 Min Rolling Avg PM2.5 Contribution

Stopped Initial Avg Rolling Avg


PM10 Average Contribution ( $\mu\text{g}/\text{m}^3$ )

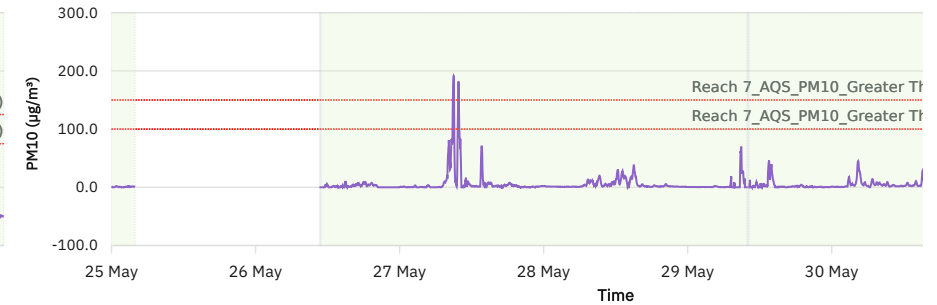

● 15 Min Rolling Avg PM10 Contribution


Stopped Initial Avg Rolling Avg

VOC Average Contribution (ppm)

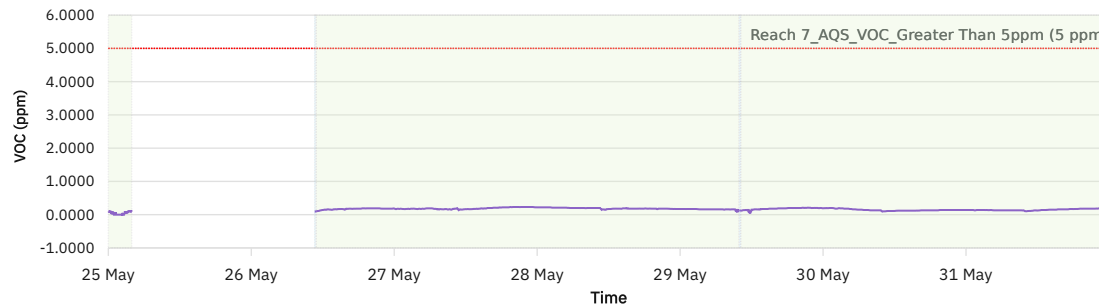


● 15 Min Rolling Avg VOC Contribution


Wind rose (mph)

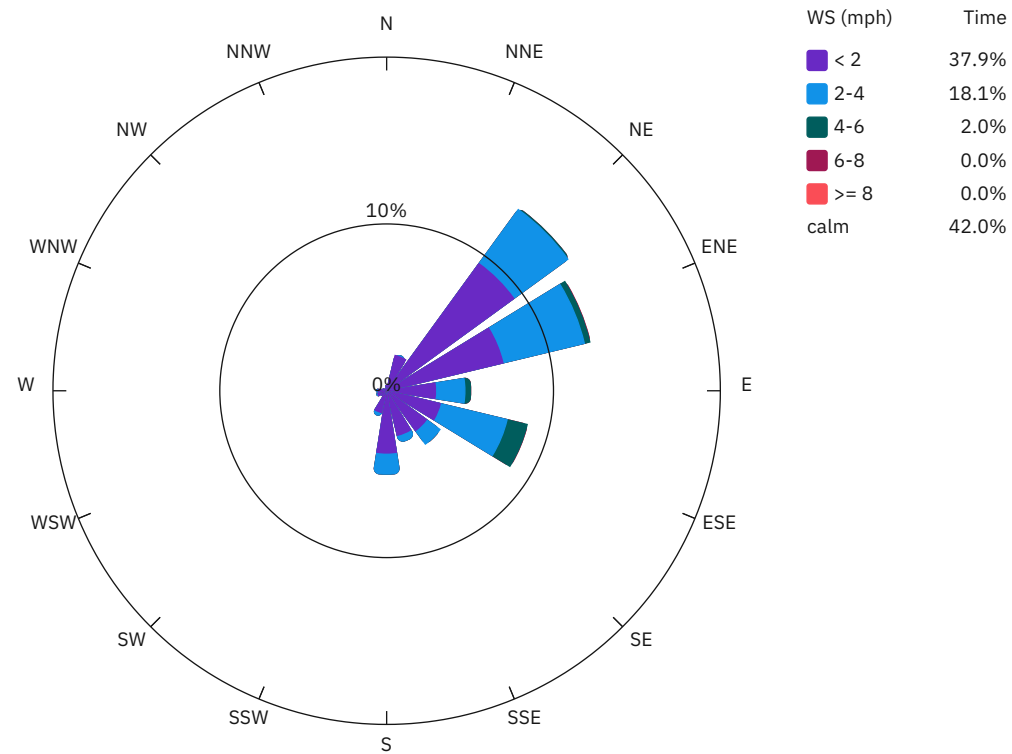


AM-01\_Reach 7\_3393\_WS

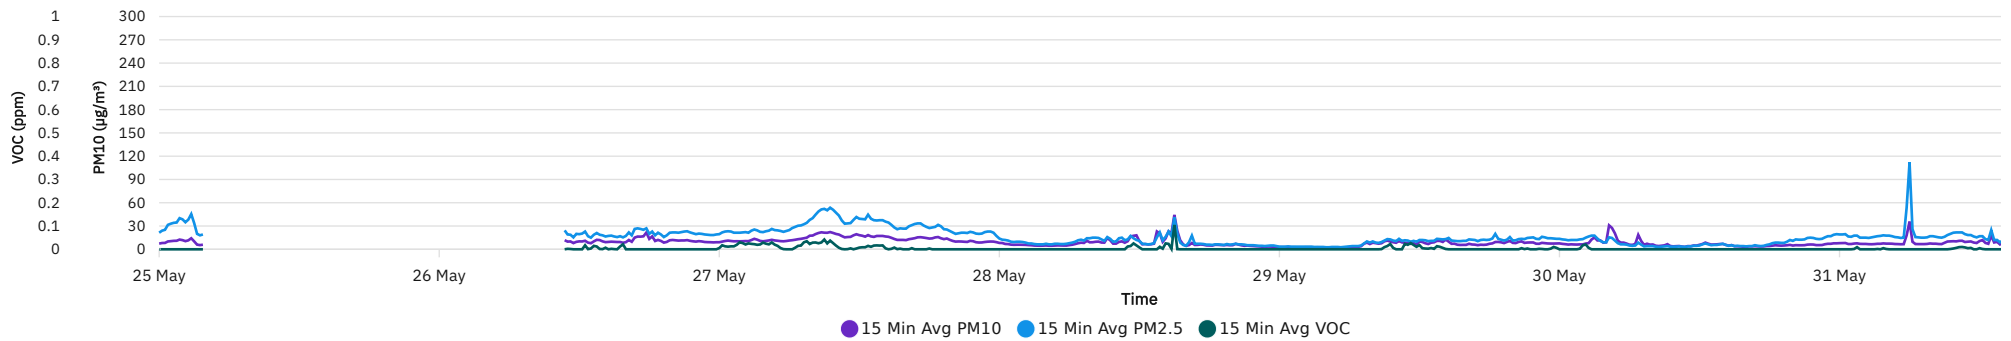


AM-02\_Reach 7\_3399

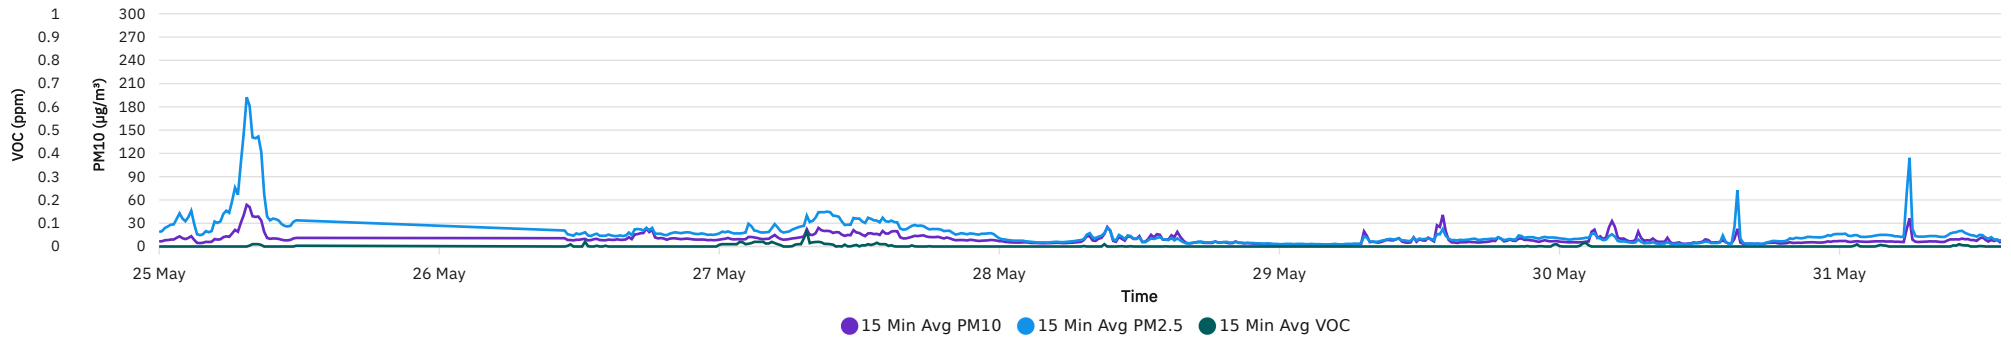


AM-03\_Reach 7\_3400

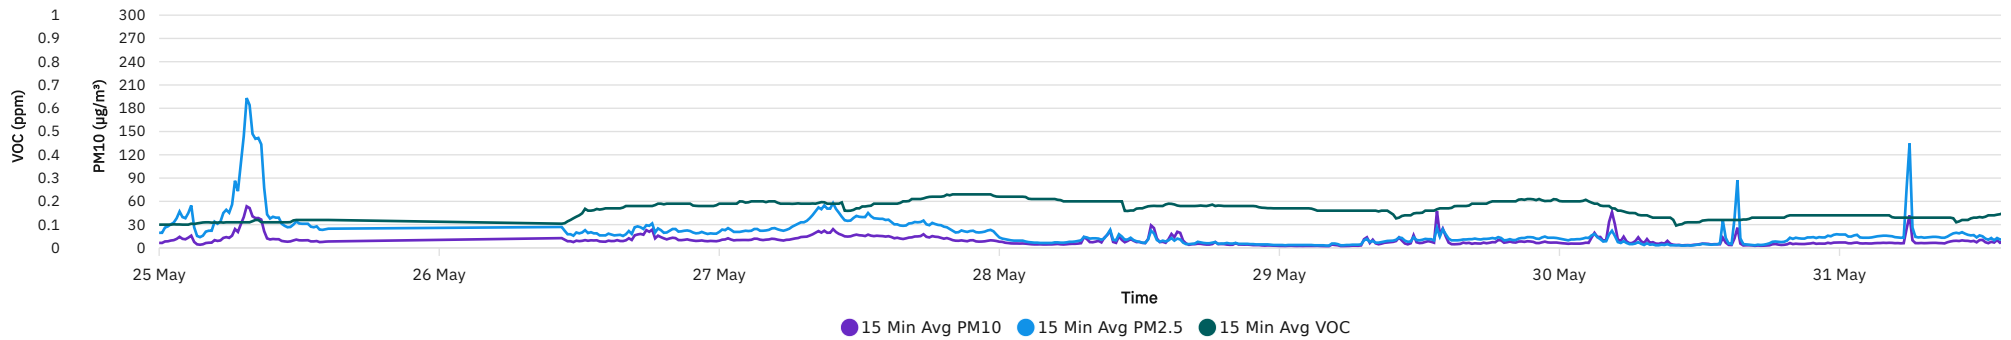


AM-04\_Reach 7\_3404

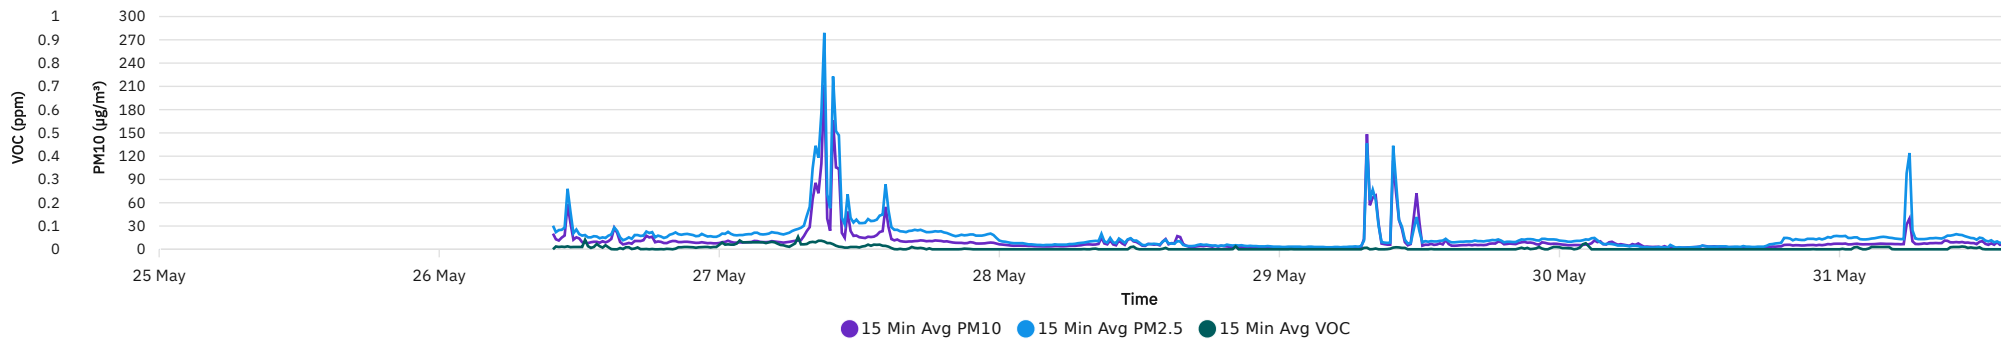

AM-05\_Reach 7\_3452

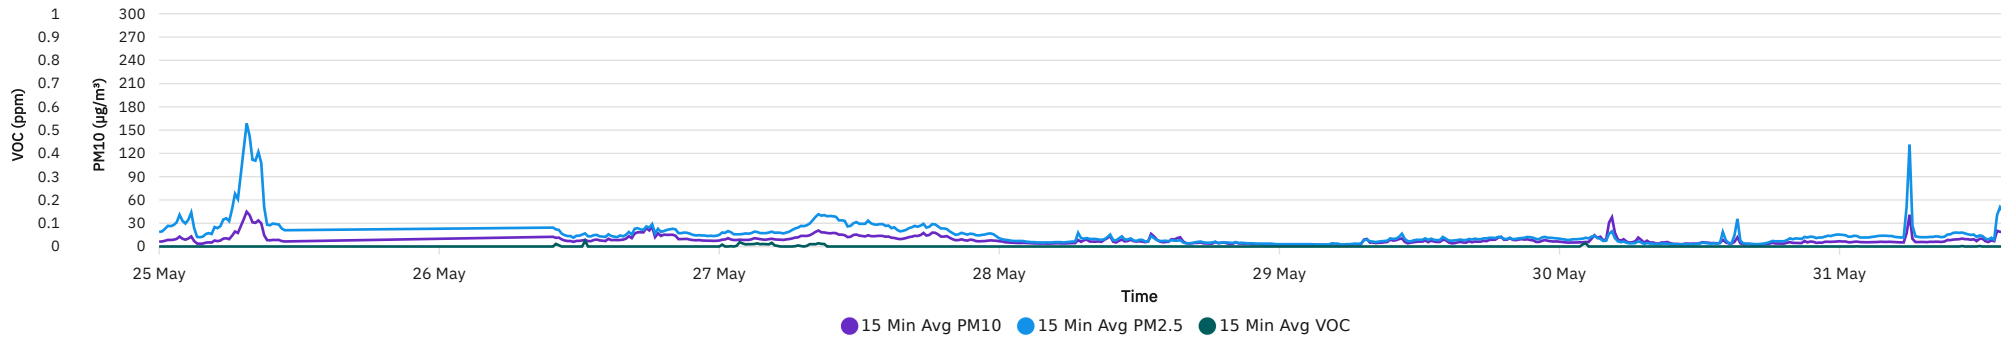

AM-06\_Reach 7\_3455\_WS

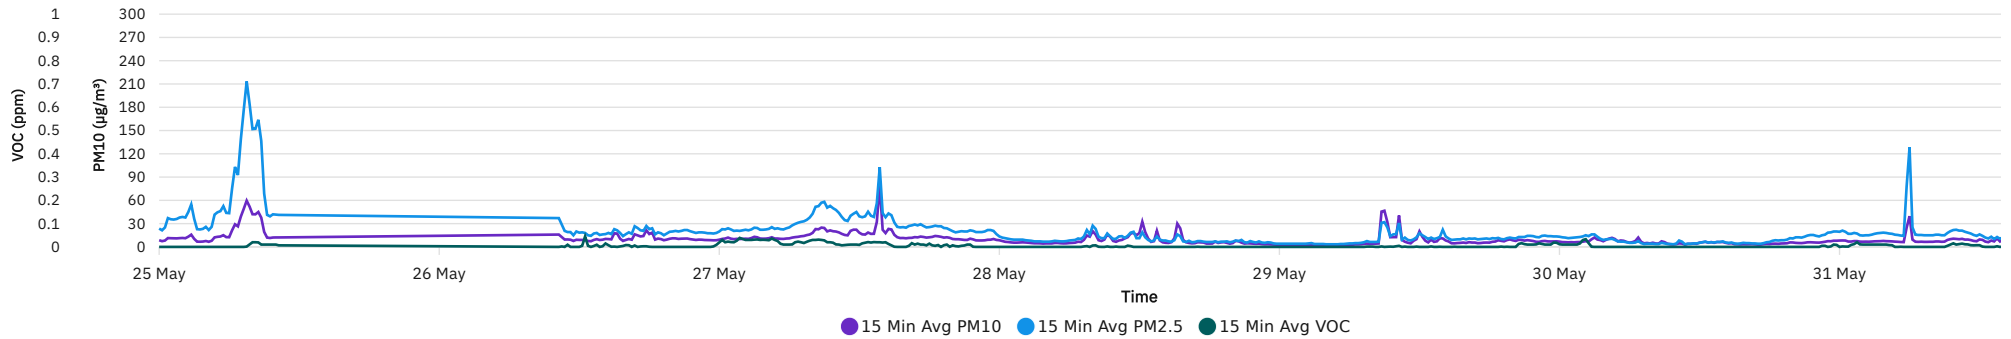

Exceedance Summary

Parameter	Action Level	Time Triggered	Cause	Mitigation
PM10	150.0 µg/m³	5/27/2026 08:50	Elevated readings were attributable to construction activities within the project area.	Contractor implemented dust control measures to mitigate fugitive dust.
PM10	150.0 µg/m³	5/27/2026 09:41	Elevated readings were attributable to construction activities within the project area.	Contractor implemented dust control measures to mitigate fugitive dust.
PM2.5	25.0 µg/m³	5/27/2026 08:10	Elevated readings were attributable to construction activities within the project area.	Contractor implemented dust control measures to mitigate fugitive dust.
PM2.5	35.0 µg/m³	5/27/2026 08:36	Elevated readings were attributable to construction activities within the project area.	Contractor implemented dust control measures to mitigate fugitive dust.
PM2.5	35.0 µg/m³	5/27/2026 09:40	Elevated readings were attributable to construction activities within the project area.	Contractor implemented dust control measures to mitigate fugitive dust.
PM2.5	25.0 µg/m³	5/27/2026 10:06	Elevated readings were attributable to construction activities within the project area.	Contractor implemented dust control measures to mitigate fugitive dust.
PM2.5	25.0 µg/m³	5/30/2026 15:06	Elevated readings were attributable to construction activities within the project area.	Contractor implemented dust control measures to mitigate fugitive dust.
